

Agreement No. CE 64/2020 (EP) Environmental Team for Tung Chung New Town Extension (West) – Design and Construction

Monthly Environmental Monitoring & Audit Report for May 2022

June 2022

Mott MacDonald 3/F Manulife Place 348 Kwun Tong Road Kwun Tong Kowloon Hong Kong

T +852 2828 5757 mottmac.hk

Civil Engineering and Development Department Sustainable Lantau Office 13/F, North Point Government Offices 333 Java Road North Point, Hong Kong

Agreement No. CE 64/2020 (EP) Environmental Team for Tung Chung New Town Extension (West) – Design and Construction

Monthly Environmental Monitoring & Audit Report for May 2022

June 2022





Environmental Permit No. EP-519/2016

Tung Chung New Town Extension (West)

Environmental Team Leader Certification

Reference Document/Plan

Document to be Certified: Monthly Environmental Monitoring and Audit Report

for May 2022

Date of Document: June 2022

Date received by ETL: 13 June 2022

Reference EP Condition

Environmental Permit Condition: 3.5 & 4.1

Email from EPD dated 10 June 2022

The Permit Holder shall submit 2 hard copies and 2 electronic copies of Monthly EM&A Reports for the construction stage of the Project to the Director, within 2 weeks after the end of the reporting month. The monthly EM&A Reports shall include an executive summary of all environmental audit results, together with actions taken in the event of non-compliance (exceedances) of the environmental quality performance limits (Action and Limit Levels), complaints received and emergency events relating to violation of environmental legislation (such as illegal dumping and landfilling). The submissions shall be certified by the ET Leader and verified by the IEC as having complied with the requirements as set out in the updated EM&A Manual before submission to the Director. Additional copies of the Monthly EM&A Reports shall be provided upon request by the Director.

ETL Certification

I hereby certify that the above reference document/plan complies with the above referenced condition of EP-519/2016.

85

Daniel Sum

Environmental Team Leader Date: 13 June 2022



Your Ref.

By Post

Our Ref. 198377-0516

Date 13 June 2022

Sustainable Lantau Office Civil Engineering and Development Department 13/F, North Point Government Offices 333 Java Road, North Point Hong Kong

Attention: Mr. Gary YUNG / Ms. Carol LAM

Dear Sir / Madam,

Agreement No. CE 59/2017 (EP)

Independent Environmental Checker for Tung Chung New Town Extension – Investigation Monthly Environmental Monitoring & Audit Report for May 2022 for TCW

We refer to the Monthly Environmental Monitoring & Audit Report for May 2022 for Tung Chung New Town Extension (West) (TCW) dated June 2022 and certified by the Environmental Team (ET) Leader of TCW on 13 June 2022. Please note the submission is hereby verified, in accordance with the requirement stipulated in Condition 3.5 of EP-519/2016.

Should you have any query, please feel free to contact the undersigned at 2608 7314 (chuawo@binnies.com) or our Edward Lau at 6848 5737 (iec.tcnte@gmail.com or lauky@binnies.com).

Yours faithfully, for and on behalf of BINNIES HONG KONG LIMITED

MANUEL CHUA

INDEPENDENT ENVIRONMENTAL CHECKER

cc: ET Leader / TCW – Mott (Attn: Mr. Daniel SUM) [by Email: daniel.sum@mottmac.com]
PM / TCW – Arup (Attn: Mr. Jackson WONG) [by Email: jackson.wong@tcw.c5c6.hk]



Binnies Hong Kong Limited 43/F, AIA Kowloon Tower, 100 How Ming Street, Kwun Tong, Kowloon, Hong Kong 賓尼斯工程顧問有限公司 香港九龍觀塘巧明街 100 號友邦九龍大樓 43 樓

+852 2601 3988











Contents

Exe	ecutive	summary	1
1	Intro	oduction	3
	1.1	Background	3
	1.2	Scope of this Report	3
	1.3	Organisation Structure	4
	1.4	Summary of Construction Works	4
	1.5	Summary of EM&A Requirements	6
	1.6	Status of Statutory Environmental Compliance with the Environmental Permit	7
	1.7	Status of Other Statutory Environmental Requirements	7
	1.8	Reporting of EM&A Results	8
2	Air C	Quality	9
	2.1	Monitoring Requirements	9
	2.2	Monitoring Locations	9
	2.3	Monitoring Parameters, Frequency, Duration and Monitoring Dates	9
	2.4	Action and Limit Levels	9
	2.5	Monitoring Equipment	9
	2.6	Monitoring Schedule for the Reporting Period	10
	2.7	Results and Observations	10
3	Nois	se	11
	3.1	Monitoring Requirements	11
	3.2	Monitoring Locations	11
	3.3	Monitoring Parameters, Frequency, Duration and Monitoring Dates	11
	3.4	Action and Limit Levels	12
	3.5	Monitoring Equipment	12
	3.6	Monitoring Schedule for the Reporting Period	12
	3.7	Results and Observations	12
4	Wat	er Quality	14
	4.1	Monitoring Requirements	14
	4.2	Monitoring Locations	14
	4.3	Monitoring Parameters, Frequency and Duration	14
	4.4	Action and Limit Levels	15
	4.5	Monitoring Equipment	15
	4.6	Monitoring Schedule for the Reporting Period	16
	4.7	Results and Observations	16

5	Ecol	ogy	17
	5.1	Monitoring Requirements	17
	5.2	Monitoring Locations	17
	5.3	Monitoring Frequency and Dates	17
	5.4	Monitoring Methodology	18
		5.4.1 Stream Fauna	18
		5.4.2 Water Quality	18
	5.5	Action and Limit Levels	19
	5.6	Results and Observations	20
		5.6.1 Environment of Stream Courses	20
		5.6.2 Stream Fauna	20
		5.6.3 Water Quality	22
	5.7	References	22
6	Was	te Management Status	23
	6.1	General	23
7	FM&	A Site Inspection	25
	7.1	Monitoring Requirements	25
	7.1 7.2	Site Inspections and Key Observations	25 25
	1.2	Site inspections and key observations	25
8	Imple	ementation Status of Environmental Mitigation Measures	28
9	Sum Limit	mary of Exceedances of the Environmental Quality Performance	29
10		mary of Complaints, Notification of Summons and Successful ecutions	30
11	Futu	re Key Issues	31
	11.1	Construction Programme for the Coming Reporting Period	31
	11.2	Monitoring Schedule for the Coming Reporting Period	31
12	2 Conclusions and Recommendations		33
Figu	ıres		34
Арр	endice	es e	35
Α.	Proje	ect Organisation	36
B.	Cons	struction Works Programme	37
	33110		0.

C.	Environmental Mitigation Implementation Schedule	38
D.	Status of Submissions and Implementation Status of Mitigation Measures under EP	39
E.	Status of Statutory Environmental Requirements	40
F.	Air Quality	41
G.	Noise	42
Н.	Water Quality	43
l.	Ecology	44
J.	Cumulative Statistics on Exceedances, Environmental Complaints, Notifications of Summons and Status of Prosecutions	45
K.	Monitoring Schedule for the Next Reporting Period	46
Tabl	es	
	2 1.1: Commencement Dates of Construction Works for the Active Works Contracts 2 1.2: Contact Information of Key Personnel	3 4
	1.3: Major Activities in the Reporting Period	5
Table	e 1.4: Summary of Status for the Environmental Aspects under the Updated EM&A	
Manu	al	6
Table	e 2.1: Impact Air Quality Monitoring Stations	9
Table Dates	e 2.2: Impact Air Quality Monitoring Parameters, Frequency, Duration and Monitoring	9
Table	2.3: Action and Limit Levels for 1-hour TSP	9
Table	2.4: Impact Air Quality Monitoring Equipment	10
Table	2.5: Summary of 1-hour TSP Monitoring Results in the Reporting Period	10
	e 3.1: Impact Construction Noise Monitoring Stations	11
	3.2: Impact Construction Noise Monitoring Parameters, Frequency, Duration and	
	oring Dates 3.3: Action and Limit Levels for Construction Noise	11 12
		12
	e 3.4: Noise Monitoring Equipment e 3.5: Summary of Construction Noise Monitoring Results in the Reporting Period	12
	4.1: Impact Water Quality Monitoring Stations	14
	4.2: Water Quality Monitoring Parameters, Duration and Frequency	14
	4.3: Calculated Action and Limit Levels for Impact Water Quality Monitoring	15

Table 4.4: Water Quality Monitoring Equipment	16
Table 4.5: Details of Exceedances Recorded for Water Quality Monitoring	16
Table 5.1: Impact Ecological Monitoring Stations	17
Table 5.2: Impact Ecological Monitoring Schedule	17
Table 5.3: Ecologically-related Water Quality Monitoring Parameters and Testing Methods	18
Table 5.4: Ecologically-related Water Quality Monitoring Equipment	19
Table 5.5: Action and Limit Levels for Impact Ecological Monitoring	19
Table 5.6: Action Level (AL) and Limit Level (LL) for Number of Aquatic Invertebrate	
Species at Each Monitoring Station during Wet (Apr - Oct) and Dry (Nov - Mar) Seasons	19
Table 5.7: Action Level (AL) and Limit Level (LL) for Number of Fish Species at Each	
Monitoring Station during Wet (Apr – Oct) and Dry (Nov – Mar) Seasons	20
Table 5.8: Environment of Stream Courses at each Monitoring Station	20
Table 5.9: Summary of Aquatic Invertebrate Species Recorded in the Reporting Period	21
Table 5.10: Summary of Fish Species Recorded in the Reporting Period	22
Table 6.1: Quantities of Different Waste Generated and Imported Fill Materials for TCW	24
Table 7.1: Key Observations Identified during Site Inspections in this Reporting Period	26
Table 11.1: Major Activities for the next Reporting Period	32

Executive summary

Tung Chung New Town Extension (TCNTE) is one of the major initiatives under the Government's multi-pronged approach to increase land supply to meet Hong Kong's medium- to long-term needs for housing, economic and social developments. The Environmental Impact Assessment (EIA) Report for TCNTE (Register No. AEIAR-196/2016) was approved on 8 April 2016 and the Environmental Permit (EP) No. EP-519/2016, covering the construction and operation of TCNTE, was granted on 9 August 2016. The EIA Report and EP cover both Tung Chung East (TCE) and Tung Chung West (TCW, hereafter referred to as "the Project").

Civil Engineering and Development Department (CEDD) commissioned Mott MacDonald Hong Kong Limited (MMHK) to undertake the role of Environmental Team (ET) for carrying out the Environmental Monitoring & Audit (EM&A) works during the construction phase of the Project in accordance with the requirements specified in the EP, Updated EM&A Manual (the Manual), EIA Report of the Project – i.e., Tung Chung New Town Extension (TCNTE) development in Tung Chung West (TCW) and other relevant statutory requirements.

This EM&A Report summarises the monitoring results and audit findings of the EM&A programme undertaken for the TCW Project during the reporting period from 1 to 31 May 2022 in accordance with the Manual. A summary of the monitoring and audit activities conducted in the reporting period is listed as below.

Summary of Monitoring and Audit Activities in the Reporting Period

Parameter	Number of Sessions	
Air Quality Monitoring	5 sessions	
Noise Monitoring	5 sessions	
Water Quality Monitoring	13 sessions	
Ecological Monitoring	1 session	
Environmental Site Inspection	Contract No. NL/2020/05 ("Contract 5"): 5 sessions Contract No. NL/2020/06 ("Contract 6"): 5 sessions	

Environmental auditing works, including weekly site inspections of construction works conducted by the ET, audit of implementation of Habitat Enhancement and Translocation Plan for Amphibian Species of Conservation Importance, Detailed Compensatory Woodland Planting Plan, Plan on Provision of Buffer Zones and Waste Management Plan were conducted in the reporting period. Based on the audit results and the observation for the reporting period, environmental pollution control and mitigation measures for the Project were properly implemented.

Breaches of Action and Limit Levels for Air Quality

No exceedance of Action and Limit Levels was recorded for construction air quality monitoring in the reporting period.

Breaches of Action and Limit Levels for Noise

No exceedance of Action and Limit Levels was recorded for construction noise monitoring in the reporting period.

Breaches of Action and Limit Levels for Water Quality

Turbidity and Suspended Solids (SS) exceedances were recorded during the reporting period. Relevant investigations and follow-up actions were conducted in accordance with the Event and Action Plan. The exceedances were considered not related to this Project after investigations.

Ecological Monitoring

No exceedance of Action and Limit Levels was recorded for impact ecological monitoring in the reporting period.

Environmental Complaints, Non-compliance & Summons

There was no environmental complaint, notification of summons or prosecution recorded in the reporting period.

Reporting Change

There was no reporting change in the reporting period.

Summary of Upcoming Construction Activities

Contract No. NL/2020/05 ("Contract 5") - Ma Wan Chung

- Demolition of Existing Structures, Pre-drilling Work and Piling Work at Part D;
- Ground Investigation and Installation of Geotechnical Instrumentation, Site Clearance, Slope Excavation and Soil Nail Installation, Temporary ELS Works, Road Diversion, Construction of Rock Fall Fence, Excavation for Drainage Work and Retaining Wall Construction and Sheet-piling Work at Part E;
- Trial Pit Excavation and Road Diversion at Part F;
- Geotechnical Investigation and Forming Site Access at Part G;
- Construction of Haul Road, Hoarding and Fencing Erection, Site Clearance, Trial Pit Excavation, Pre-drill for Piling Work and Piling Work at Part H;

Contract No. NL/2020/06 ("Contract 6") - Tung Chung Valley

- Site Investigation and sampling at the potential land contamination sites at Area 42 under EPD approved Supplementary Contamination Assessment Plan;
- Site Clearance and Site Formation at the non-contamination sites at Area 42;
- Site Clearance at Road L29 and Road L30;
- Backfilling for Ramp Formation at Temporary Bridge A;

1 Introduction

1.1 Background

Tung Chung New Town Extension (TCNTE) is one of the major initiatives under the Government's multi-pronged approach to increase land supply to meet Hong Kong's medium- to long-term needs for housing, economic and social developments. The Environmental Impact Assessment (EIA) Report for TCNTE (Register No. AEIAR-196/2016) was approved on 8 April 2016 and the Environmental Permit (EP) No. EP-519/2016, covering the construction and operation of TCNTE, was granted on 9 August 2016. The EIA Report and EP cover both Tung Chung East (TCE) and Tung Chung West (TCW, hereafter referred to as "the Project").

Civil Engineering and Development Department (CEDD) commissioned Mott MacDonald Hong Kong Limited (MMHK) to undertake the role of Environmental Team (ET) for carrying out the Environmental Monitoring & Audit (EM&A) works during the construction phase of the Project in accordance with the requirements specified in the EP, Updated EM&A Manual (the Manual), EIA Report of the TCW Project and other relevant statutory requirements. The scope of the Project works in TCW includes the following elements:

- Site formation works:
- Construction or the River Park including a visitor centre;
- Construction of proposed open space;
- Construction of sustainable urban drainage system;
- Construction of roads, footpath and the associated junction / road improvement works;
- Construction of coastal pedestrian access;
- Engineering infrastructure works covering drainage, sewerage, waterworks and landscaping works; and
- Implementation of environmental mitigation measures and environmental monitoring and audit works.

The construction works for the Project were commenced on 3 November 2021 and are divided into various works contracts. The following active works contracts were commenced on the dates shown in **Table 1.1**.

Table 1.1: Commencement Dates of Construction Works for the Active Works Contracts

Contract No.	Contract Name	Commencement Date of Construction Works	
Contract No. NL/2020/05 ("Contract 5")	Tung Chung New Town Extension – Site Formation and Infrastructure Works at Ma Wan Chung	3 Nov 2021	
Contract No. NL/2020/06 ("Contract 6")	Tung Chung New Town Extension – Site Formation and Infrastructure Works at Tung Chung Valley, Phase 1	3 Nov 2021 (Note: Construction works at Tung Chung Valley commenced on 30 Nov 2021)	

The locations of Contracts 5 and 6 are shown in Figures 1.1 and 1.2 respectively.

1.2 Scope of this Report

This is the Monthly EM&A Report for the TCW Project which summarises the key findings of the EM&A programme for the construction works during the reporting period from 1 to 31 May 2022.

1.3 Organisation Structure

The organisation structure of the Project is shown in **Appendix A**. The key personnel contact names and contact details of the active works contracts are summarised in **Table 1.2** below.

Table 1.2: Contact Information of Key Personnel

Project Proponent Ching Engineer Gavin Wong 2231 4439 Clivil Engineering and Development Department (CEDD)) Principal Resident Engineer Gavin Wong 2231 4472 Engineer's Representative (ER) Principal Resident Engineer Sam Chan 9671 5538 Engineer's Representative (ER) Principal Resident Engineer Sam Chan 9671 5538 Engineer Sam Chan 9673 5698 5790 Contractor Project Manager Artie Wong 9633 0977 Environmental Officer Calvin Chan 6117 2894 24-hour Complaint Hotline - 9326 1161 Contract No. NL/2020/06 ("Contract 6") Engineer Sam Chan 9100 7509 Environmental Officer Calvin Chan 6117 2894 24-hour Complaint Hotline - 9326 1161 Contract No. NL/2020/06 ("Contract 6") Engineer Samuel Yiu 2231 4469 Clivil Engineering and Development Senior Engineer Gavin Wong 2231 4469 Department (CEDD) Engineer Samuel Yiu 2231 4510 Engineer's Representative (ER) Principal Resident Engineer Jackson Wong 5699 5710 Cove Arup and Partners Hong Kong Principal Resident Engineer Shirley Yeung 9671 5518 Engineer's Representative (ER) Principal Resident Engineer Shirley Yeung 9671 5518 Contractor Project Director Andy Yeung 9650 0037 China Railway Group Limited Project Manager Robert Luo 9588 2485 Environmental Officer Simon Mak 6266 0745 Ste Agent Jim Ko 6365 8035 Environmental Officer Daniel Sum 2585 8495 Contractor Project Manager Paul Chan 6266 0745 Ste Agent Jim Ko 6365 8035 Environmental Officer Daniel Sum 2585 8495 Contractor Project Manager Paul Chan 6266 0745 Ste Agent Jim Ko 6365 8035 Ste Agent Jim Ko 6365 8035	Party	Position	Name	Telephone
Project Proponent (Civil Engineering and Development) Department (CEDD)) Chief Engineer Senior Engineer Gavin Wong Gary Yung 2231 4439 Engineer's Representative (ER) (Ove Arup and Partners Hong Kong Limited) Principal Resident Engineer Jackson Wong 5699 5710 Contractor (Build King – Richwell Civil Joint Venture) Resident Engineer Sam Chan 9671 5538 Contractor (Build King – Richwell Civil Joint Venture) Project Manager Eric Yip 9196 6098 Contract No. NL/2020/06 ("Contract 6") Site Agent Ricky Hon 9100 7509 Environmental Officer Calvin Chan 6117 2894 24-hour Complaint Hotline - 9326 1161 Project Proponent (Civil Engineering and Development (Civil Engineering and Development (Civil Engineering and Development (Civil Engineer) Chief Engineer Gavin Wong 2231 4439 Contract Or Arup and Partners Hong Kong Limited) Principal Resident Engineer Jackson Wong 5699 5710 Contractor (China Railway Group Limited) Principal Resident Engineer Jackson Wong 5699 5746 Contractor (China Railway Group Limited) Project Director Andy Yeung 9650 0037 Contractor (China Railway Group Limited) Pr	Contract No. NL/2020/05 ("Contract 5")			
(Civil Engineering and Development Department (CEDD)) Senior Engineer Gary Yung 2195 0847 Department (CEDD)) Engineer Carol Lam 2231 4472 Engineer's Representative (ER) (Ove Arup and Partners Hong Kong Limited) Principal Resident Engineer Jackson Wong 5699 5710 Contractor Resident Engineer Sam Chan 9671 5538 (Build King – Richwell Civil Joint Venture) Project Manager Eric Yip 9196 6098 (Build King – Richwell Civil Joint Venture) Site Agent Ricky Hon 9633 0977 Site Agent Ricky Hon 9100 7509 Environmental Officer Calvin Chan 6117 2894 24-hour Complaint Hotline - 9326 1161 Contract No. NL/2020/06 ("Contract 6") Project Proponent Chief Engineer Gavin Wong 2231 4439 (Civil Engineering and Development Senior Engineer Gavin Wong 2231 4439 (Civil Engineering and Development Senior Engineer Gramuel Yiu 2231 4460 Department (CEDD)) Senior Engineer Samuel Yiu 2231 4460 Contractor Principal Resident Engineer	Tung Chung New Town Extension – Site	Formation and Infrastructure We	orks at Ma Wan Chun	g
Engineer Carol Lam 2231 4472	Project Proponent	Chief Engineer	Gavin Wong	2231 4439
Engineer's Representative (ER) Principal Resident Engineer Jackson Wong 5699 5710	•	Senior Engineer	Gary Yung	2195 0847
(Ove Arup and Partners Hong Kong Limited) Resident Engineer Sam Chan 9671 5538 Contractor (Build King – Richwell Civil Joint Venture) Project Manager Eric Yip 9196 6098 (Build King – Richwell Civil Joint Venture) Project Manager Artie Wong 9633 0977 Site Agent Ricky Hon 9100 7509 Environmental Officer Calvin Chan 6117 2894 24-hour Complaint Hotline - 9326 1161 Contract No. NL/2020/06 ("Contract 6") Tung Chung New Town Extension – Site Formation and Infrastructure Works at Tung Chung Valley, Phase 1 Project Proponent Chief Engineer Gavin Wong 2231 4439 (Civil Engineering and Development Department (CEDDI) Senior Engineer Grund 2231 4469 Engineer's Representative (ER) Principal Resident Engineer Jackson Wong 5699 5710 (Ove Arup and Partners Hong Kong Limited) Resident Engineer Shirley Yeung 9671 5518 Contractor Project Director Andy Yeung 9650 0037 (China Railway Group Limited) Project Manager Robert Luo 9588 2485 Environmental Officer <td>Department (CEDD))</td> <td>Engineer</td> <td>Carol Lam</td> <td>2231 4472</td>	Department (CEDD))	Engineer	Carol Lam	2231 4472
Senior Inspector of Works Tony Chiu 5699 5792	Engineer's Representative (ER)	Principal Resident Engineer	Jackson Wong	5699 5710
Senior Inspector of Works Tony Chiu 5699 5792	(Ove Arup and Partners Hong Kong	Resident Engineer	Sam Chan	9671 5538
Construction Manager	Limited)	Senior Inspector of Works	Tony Chiu	5699 5792
Site Agent Ricky Hon 9100 7509 Environmental Officer Calvin Chan 6117 2894 24-hour Complaint Hotline - 9326 1161 Contract No. NL/2020/06 ("Contract 6") Tung Chung New Town Extension - Site Formation and Infrastructure Works at Tung Chung Valley, Phase 1 Project Proponent Chief Engineer Gavin Wong 2231 4439 (Civil Engineering and Development Senior Engineer CT Lam 2231 4469 Department (CEDD)) Engineer Samuel Yiu 2231 4510 Engineer's Representative (ER) Principal Resident Engineer Jackson Wong 5699 5710 (Ove Arup and Partners Hong Kong Resident Engineer Shirley Yeung 9671 5518 Limited) Senior Inspector of Works Jensen Lo 5699 5746 Contractor Project Director Andy Yeung 9650 0037 (China Railway Group Limited) Project Manager Paul Chan 6263 0621 Deputy Project Manager Robert Luo 9588 2485 Superintendent Site Agent Jim Ko 6365 8035 Environmental Officer Simon Mak 6266 0745 24-hour Complaint Hotline - 9326 1161 Environmental Team (ET) ET Leader Daniel Sum 2585 8495 (Mott MacDonald Hong Kong Limited) Deputy ET Leader Heidi Yu 2828 5704 Independent Environmental Checker (IEC) IEC Manuel Chua 3894 9501	Contractor	Project Manager	Eric Yip	9196 6098
Environmental Officer Calvin Chan 6117 2894 24-hour Complaint Hotline - 9326 1161	(Build King – Richwell Civil Joint Venture)	Construction Manager	Artie Wong	9633 0977
Contract No. NL/2020/06 ("Contract 6") Tung Chung New Town Extension – Site Formation and Infrastructure Works at Tung Chung Valley, Phase 1 Project Proponent (Civil Engineering and Development Department (CEDD)) Engineer Samuel Yiu 2231 4469 Engineer Samuel Yiu 2231 4510 Engineer's Representative (ER) (Ove Arup and Partners Hong Kong Limited) Resident Engineer Shirley Yeung 9671 5518 Senior Inspector of Works Jensen Lo 5699 5746 Contractor (China Railway Group Limited) Project Director Andy Yeung 9650 0037 Project Manager Paul Chan 6263 0621 Deputy Project Manager Robert Luo 9588 2485 Superintendent Site Agent Jim Ko 6365 8035 Environmental Officer Simon Mak 6266 0745 24-hour Complaint Hotline - 9326 1161 Environmental Team (ET) (Mott MacDonald Hong Kong Limited) Deputy ET Leader Daniel Sum 2585 8495 Independent Environmental Checker (IEC) IEC Manuel Chua 3894 9501		Site Agent	Ricky Hon	9100 7509
Tung Chung New Town Extension – Site Formation and Infrastructure Works at Tung Chung Valley, Phase 1 Project Proponent (Civil Engineering and Development Department (CEDD)) Engineer's Representative (ER) (Ove Arup and Partners Hong Kong Limited) Project Director Andy Yeung 9671 5518 Contractor (China Railway Group Limited) Project Manager Paul Chan 6263 0621 Deputy Project Manager / Superintendent Site Agent Jim Ko 6365 8035 Environmental Team (ET) ET Leader Daniel Sum 2585 8495 (Mott MacDonald Hong Kong Limited) Engineer Savin Wong 2231 4439 Chief Engineer Savin Wong 2231 4469 Engineer Samuel Yiu 2231 4510 Engineer Samuel Yiu 2610 450 Engineer Samuel Yiu 2610 450		Environmental Officer	Calvin Chan	6117 2894
Tung Chung New Town Extension – Site Formation and Infrastructure Works at Tung Chung Valley, Phase 1 Project Proponent (Civil Engineering and Development Department (CEDD)) Chief Engineer CT Lam 2231 4469 Department (CEDD)) Engineer Samuel Yiu 2231 4510 Engineer's Representative (ER) (Ove Arup and Partners Hong Kong Limited) Principal Resident Engineer Paul Chan 3699 5710 Contractor (China Railway Group Limited) Project Director Works Project Manager Paul Chan 9650 0037 Project Manager Project Manager Project Manager Paul Chan 9588 2485 Superintendent Superintendent Site Agent Jim Ko 6365 8035 Environmental Officer Simon Mak 6266 0745 24-hour Complaint Hotline - 9326 1161 9326 1161 Environmental Team (ET) (Mott MacDonald Hong Kong Limited) ET Leader Daniel Sum 2585 8495 Independent Environmental Checker (IEC) IEC Manuel Chua 3894 9501		24-hour Complaint Hotline	-	9326 1161
(Civil Engineering and Development Department (CEDD)) Senior Engineer CT Lam 2231 4469 Engineer's Representative (ER) (Ove Arup and Partners Hong Kong Limited) Principal Resident Engineer Jackson Wong 5699 5710 Resident Engineer Shirley Yeung 9671 5518 Senior Inspector of Works Jensen Lo 5699 5746 Contractor Project Director Andy Yeung 9650 0037 (China Railway Group Limited) Project Manager Paul Chan 6263 0621 Deputy Project Manager / Superintendent Robert Luo 9588 2485 Superintendent Site Agent Jim Ko 6365 8035 Environmental Officer Simon Mak 6266 0745 24-hour Complaint Hotline - 9326 1161 Environmental Team (ET) ET Leader Daniel Sum 2585 8495 (Mott MacDonald Hong Kong Limited) Deputy ET Leader Heidi Yu 2828 5704 Independent Environmental Checker (IEC) IEC Manuel Chua 3894 9501	Tung Chung New Town Extension - Site			• •
Engineer Samuel Yiu 2231 4510	, ,	Chief Engineer		2231 4439
Engineer's Representative (ER) (Ove Arup and Partners Hong Kong Limited) Resident Engineer Shirley Yeung 9671 5518 Senior Inspector of Works Senior Inspector (China Railway Group Limited) Project Director Project Manager Paul Chan 6263 0621 Deputy Project Manager / Robert Luo Superintendent Site Agent Jim Ko 6365 8035 Environmental Officer Simon Mak 6266 0745 24-hour Complaint Hotline - 9326 1161 Environmental Team (ET) (Mott MacDonald Hong Kong Limited) Deputy ET Leader Heidi Yu 2828 5704 Independent Environmental Checker (IEC) IEC Manuel Yiu 2231 4510 2331 4510 2348 Somple Shirley Yeung 9671 5518 2699 5746 Andy Yeung 9650 0037 Project Manager / Robert Luo 9588 2485 Superintendent Site Agent Jim Ko 6365 8035 Environmental Officer Simon Mak 6266 0745 24-hour Complaint Hotline - 9326 1161 Environmental Team (ET) (Mott MacDonald Hong Kong Limited) Deputy ET Leader Heidi Yu 2828 5704		Senior Engineer	CT Lam	2231 4469
(Ove Arup and Partners Hong Kong Limited) Resident Engineer Shirley Yeung 9671 5518 Senior Inspector of Works Jensen Lo 5699 5746 Contractor (China Railway Group Limited) Project Director Andy Yeung 9650 0037 Project Manager Paul Chan 6263 0621 Deputy Project Manager / Robert Luo 9588 2485 Superintendent Site Agent Jim Ko 6365 8035 Environmental Officer Simon Mak 6266 0745 24-hour Complaint Hotline - 9326 1161 Environmental Team (ET) (Mott MacDonald Hong Kong Limited) Deputy ET Leader Heidi Yu 2828 5704 Independent Environmental Checker (IEC) IEC Manuel Chua 3894 9501	- openion (0 == = //	Engineer	Samuel Yiu	2231 4510
Limited) Senior Inspector of Works Jensen Lo 5699 5746 Contractor (China Railway Group Limited) Project Director Andy Yeung 9650 0037 Project Manager Deputy Project Manager / Superintendent Robert Luo 9588 2485 Superintendent Jim Ko 6365 8035 Environmental Officer Simon Mak 6266 0745 24-hour Complaint Hotline - 9326 1161 Environmental Team (ET) (Mott MacDonald Hong Kong Limited) ET Leader Daniel Sum 2585 8495 Independent Environmental Checker (IEC) IEC Manuel Chua 3894 9501	Engineer's Representative (ER)	Principal Resident Engineer	Jackson Wong	5699 5710
Senior Inspector of Works Jensen Lo 5699 5746		Resident Engineer	Shirley Yeung	9671 5518
(China Railway Group Limited) Project Manager Paul Chan 6263 0621 Deputy Project Manager / Superintendent Robert Luo 9588 2485 Site Agent Jim Ko 6365 8035 Environmental Officer Simon Mak 6266 0745 24-hour Complaint Hotline - 9326 1161 Environmental Team (ET) ET Leader Daniel Sum 2585 8495 (Mott MacDonald Hong Kong Limited) Deputy ET Leader Heidi Yu 2828 5704 Independent Environmental Checker (IEC) IEC Manuel Chua 3894 9501	Limited)	Senior Inspector of Works	Jensen Lo	5699 5746
Deputy Project Manager / Superintendent Deputy Project Manager / Superintendent	Contractor	Project Director	Andy Yeung	9650 0037
Superintendent Site Agent Jim Ko 6365 8035 Environmental Officer Simon Mak 6266 0745 24-hour Complaint Hotline - 9326 1161 Environmental Team (ET) ET Leader Daniel Sum 2585 8495 (Mott MacDonald Hong Kong Limited) Deputy ET Leader Heidi Yu 2828 5704 Independent Environmental Checker (IEC) IEC Manuel Chua 3894 9501	(China Railway Group Limited)	Project Manager	Paul Chan	6263 0621
Environmental Officer Simon Mak 6266 0745 24-hour Complaint Hotline - 9326 1161 Environmental Team (ET) ET Leader Daniel Sum 2585 8495 (Mott MacDonald Hong Kong Limited) Deputy ET Leader Heidi Yu 2828 5704 Independent Environmental Checker (IEC) IEC Manuel Chua 3894 9501			Robert Luo	9588 2485
24-hour Complaint Hotline - 9326 1161 Environmental Team (ET) ET Leader Daniel Sum 2585 8495 (Mott MacDonald Hong Kong Limited) Deputy ET Leader Heidi Yu 2828 5704 Independent Environmental Checker (IEC) IEC Manuel Chua 3894 9501		Site Agent	Jim Ko	6365 8035
Environmental Team (ET) ET Leader Daniel Sum 2585 8495 (Mott MacDonald Hong Kong Limited) Deputy ET Leader Heidi Yu 2828 5704 Independent Environmental Checker (IEC) IEC Manuel Chua 3894 9501		Environmental Officer	Simon Mak	6266 0745
(Mott MacDonald Hong Kong Limited) Deputy ET Leader Heidi Yu 2828 5704 Independent Environmental Checker (IEC) IEC Manuel Chua 3894 9501		24-hour Complaint Hotline	-	9326 1161
Independent Environmental Checker (IEC) IEC Manuel Chua 3894 9501	Environmental Team (ET)	ET Leader	Daniel Sum	2585 8495
	(Mott MacDonald Hong Kong Limited)	Deputy ET Leader	Heidi Yu	2828 5704
(Binnies Hong Kong Limited) Deputy IEC Edward Lau 3894 9502	Independent Environmental Checker (IEC)	IEC	Manuel Chua	3894 9501
	(Binnies Hong Kong Limited)	Deputy IEC	Edward Lau	3894 9502

1.4 Summary of Construction Works

The programme of the construction is shown in **Appendix B**.

As informed by the Contractors of the active works contracts, details of the major works carried out in this reporting period are listed in **Table 1.3**.

The environmental mitigation implementation schedule is presented in **Appendix C**.

Table 1.3: Major Activities in the Reporting Period

Activities Key Issues Key Mitigation Measures Contract No. NL/2020/05 ("Contract 5") Tung Chung New Town Extension – Site Formation and Infrastructure Works at Ma Wan Chung Ground Investigation and Installation of Geotechnical Good site practices **Dust Emission** Instrumentation at Part E Handling and storage of C&D materials generated from Regular water spraying on stockpiles Geotechnical Investigation Works at Part G construction activities Provide tarpaulin sheets coverage on stockpiles Temporary ELS Works at Part E Noise from plant operation Sorting and reuse of C&D materials as far as practicable Road Diversion at Part E and F Emission of dark smoke from PMEs Use of QPME and noise barrier/acoustic mat Construction of Rock Fall Fence at Part E Efficiency of wastewater and drainage management Regular maintenance of PMEs Site Clearance at Part D and H Tree Protection Implementation of wastewater and drainage management Removal of Former Church Structure at Part D Retain and protect all existing trees and vegetation within Construction of Haul Road at Part H the study area which are not directly affected by the works Hoarding and Fencing Erection at Part E and H Trial Pit Excavation at Part F and H Temporary Drainage Diversion at Part E Contract No. NL/2020/06 ("Contract 6") Tung Chung New Town Extension - Site Formation and Infrastructure Works at Tung Chung Valley, Phase 1 Site Clearance at Area 42 and Road L29 Good site practices **Dust Emission** Site Survey at Sewage Pumping Station-A Handling and storage of C&D materials generated from Regular water spraying on stockpiles construction activities Sorting of C&D Materials at Area 42 Provide tarpaulin sheets coverage on stockpiles Noise from plant operation Site Formation at the non-contamination sites at Area 42 Sorting and reuse of C&D materials as far as practicable Emission of dark smoke from PMEs Use of QPME and noise barrier/acoustic mat Site Investigation and sampling at the potential land contamination sites at Area 42 under the EPD approved Efficiency of wastewater and drainage management Regular maintenance of PMEs Supplementary Contamination Assessment Plan Tree Protection Implementation of wastewater and drainage management Decking of bridge at Temporary Bridge A Retain and protect all existing trees and vegetation within Fencing Erection at Sewage Pumping Station-A the study area which are not directly affected by the works Road Diversion at Road L30 Tree Planting and vegetation removal at Compensatory Woodland Tree Felling at Road L29 Plants removal at Yu Tung Road

1.5 Summary of EM&A Requirements

The status of all environmental aspects is presented in **Table 1.4**. The EM&A requirements remained unchanged during the reporting period.

Table 1.4: Summary of Status for the Environmental Aspects under the Updated EM&A Manual

Parameter	Status		
Air Quality			
Baseline Monitoring	The results of baseline air quality monitoring for TCW were reported in the Baseline Monitoring Report and submitted to EPD under Eff Condition 3.4.		
Impact Monitoring	On-going for TCW. Monitoring conducted three times in every 6 days.		
Noise			
Baseline Monitoring (Construction Noise)	The results of baseline noise monitoring for TCW were reported in the Baseline Monitoring Report and submitted to EPD under EP Condition 3.4.		
Impact Monitoring (Construction Noise)	On-going for TCW. Monitoring conducted once per week.		
Impact Monitoring for Road Traffic Noise during Operational Phase	To be conducted during operational phase.		
ixed Noise Commissioning Test To be implemented by the Contractor before operation of Tung New Town Extension (TCNTE) development.			
Water Quality			
Baseline Monitoring	The results of baseline water quality monitoring for TCW were reported in the Baseline Monitoring Report and submitted to EPD under EF Condition 3.4.		
Impact Monitoring	On-going for TCW. Monitoring conducted three times per week.		
Waste Management			
Waste Monitoring	On-going.		
Land Contamination			
Contamination Assessment Plan (CAP), Remediation Action Plan (RAP) and Remediation Report (RR)	Site investigation in Area 42 was carried out in accordance with the Supplementary Contamination Assessment Plan as approved by EPD. Proposed site investigation of the remaining potentially contaminated areas identified in the approved EIA Report is to be conducted after land resumption.		
Ecology	·		
Monitoring for Compensation Woodland	To be conducted when compensation woodland is planted.		
Monitoring for Emergent Plant inside the future River Park	To be conducted when the emergent plants are planted.		
Monitoring for Translocated Amphibians of Conservation Importance	Pre-construction survey was conducted during 20-22 October 2021. Capture and translocation exercise was conducted during 29-31 October 2021.		
Monitoring for Preserved/Transplanted Plant Species of Conservation Importance	To be conducted after preservation/transplantation.		
Baseline Monitoring for Tung Chung Stream Ecologically Important Stream (EIS) and Wong Lung Hang EIS	The results of baseline ecological monitoring for TCW were reported in the Baseline Monitoring Report and submitted to EPD under EP Condition 3.4. Monitoring for Wong Lung Hang was not required and the proposal by		
	the ET Leader of TCE was accepted by EPD on 2 September 2021.		
Impact Monitoring for Tung Chung Stream	On-going for TCW. Monitoring conducted at monthly intervals.		

Parameter	Status	
Landscape and Visual		
Baseline Monitoring	The results of baseline landscape and visual monitoring were reported in the Baseline Monitoring Report and submitted to EPD under EF Condition 3.4.	
Site Environmental Audit		
Regular Site Inspection	On-going.	
Plan on Provision of Buffer Zones implementation measures	Under implementation by the Contractor of Contract 6.	
Plan for Review of Use of New Low Noise Road Surfacing Material implementation measures	Not applicable during this reporting period.	
River Park Plan implementation measures	Not applicable during this reporting period.	
Preservation and/or Translocation Plan for Plant Species of Conservation Importance implementation measures	Under implementation by the Contractors of Contracts 5 and 6.	
Detailed Compensatory Woodland Planting Plan implementation measures	Under implementation by the Contractor of Contract 6.	
Habitat Enhancement and Translocation Plan for Amphibian Species of Conservation Importance implementation measures	Under implementation by the Contractor of Contract 6.	
Waste Management Plan implementation measures	Under implementation by the Contractors of Contracts 5 and 6.	
Complaint Hotline and Email Channel	Under implementation by the Contractors of Contracts 5 and 6.	
Environmental Log Book	On-going.	

Taking into account the construction works, impact monitoring of air quality, noise, water quality, ecology and waste management were carried out in the reporting period. The monitoring schedule of air quality, noise, water quality and ecological monitoring are provided in **Appendix F**, **Appendix G**, **Appendix H** and **Appendix I** respectively.

The EM&A programme also involved environmental site inspections and related auditing conducted by the ET for checking the implementation of the required environmental mitigation measures recommended in the approved EIA Report and relevant EP submissions, including Habitat Enhancement and Translocation Plan for Amphibian Species of Conservation Importance, Detailed Compensatory Woodland Planting Plan, Plan on Provision of Buffer Zones and Waste Management Plan.

1.6 Status of Statutory Environmental Compliance with the Environmental Permit

The status of statutory environmental compliance with the EP conditions under the EIAO, submission status under the EP and implementation status of mitigation measures are presented in **Appendix D**.

1.7 Status of Other Statutory Environmental Requirements

The environmental licences and permits (including Environmental Permit, waste disposal billing account, registration as chemical waste producer and construction noise permit) which were valid in the reporting period are presented in **Appendix E**. No non-compliance with environmental statutory requirements was recorded.

1.8 Reporting of EM&A Results

The EM&A programme for the Project required environmental monitoring for air quality, noise and water quality as well as environmental site inspections for air quality, noise, water quality, waste management, ecology, and landscape and visual impacts. The EM&A requirements and related findings for each component are summarised in the following sections:

- Section 2 Air Quality;
- Section 3 Noise;
- Section 4 Water Quality;
- Section 5 Ecology;
- Section 6 Waste Management Status;
- Section 7 EM&A Site Inspection;
- Section 8 Implementation Status of Environmental Mitigation Measures;
- Section 9 Summary of Exceedances of the Environmental Quality Performance Limit;
- Section 10 Summary of Complaints, Notification of Summons and Successful Prosecutions;
- · Section 11 Future Key Issues; and
- Section 12 Conclusions and Recommendations.

2 Air Quality

2.1 Monitoring Requirements

According to the requirements in the Updated EM&A Manual, regular impact air quality monitoring shall be carried out at the designated monitoring locations during the construction period of the Project to obtain 1-hour Total Suspended Particulate (TSP) concentrations. One-hour sampling should be done at least 3 times per 6 days while the highest dust impact is expected. Further details of the impact air quality monitoring are presented in the following sections.

2.2 Monitoring Locations

A total of two air quality monitoring stations were identified for impact monitoring in the TCNTE possible development area (PDA) at Tung Chung West and are covered by this Report.

Locations of the impact air quality monitoring stations covered in this Report are summarised in **Table 2.1** and shown in **Appendix F1**.

Table 2.1: Impact Air Quality Monitoring Stations

Monitoring Station	Location
DM-5	Lung Tseung Tau
DM-6	Mok Ka

2.3 Monitoring Parameters, Frequency, Duration and Monitoring Dates

Table 2.2 summarises the parameters, frequency, duration and monitoring dates for impact air quality monitoring during the reporting period.

Table 2.2: Impact Air Quality Monitoring Parameters, Frequency, Duration and Monitoring Dates

Monitoring Station	Parameter	Frequency and Duration	Monitoring Dates
DM-5	1-hour Total Suspended	3 times per 6 days during the	6, 11, 17, 23 & 27 May
DM-6	Particulates (TSP)	construction period of the Project	2022

2.4 Action and Limit Levels

The Action and Limit Levels of the air quality monitoring are provided in **Table 2.3** below.

Table 2.3: Action and Limit Levels for 1-hour TSP

Monitoring Station	Action Level (μg/m³)	Limit Level (µg/m³)
DM-5	266	500
DM-6	260	500
DIVI-0	200	300

2.5 Monitoring Equipment

Portable direct reading dust meter was used to carry out the 1-hour TSP impact monitoring for the Project. The proposed use of portable direct reading dust meters was submitted to IEC and agreed by IEC in accordance with Section 5.5 of the Updated EM&A Manual. With the use of direct reading dust meter, it can allow prompt and direct results for the EM&A reporting and the implementation of the Event and Action Plan. The portable direct reading dust meter would be

calibrated every year against High Volume Sampler (HVS) to check the validity and accuracy of the results measured by direct reading method.

Table 2.4 summarizes the equipment used in the impact air quality monitoring during the reporting period. Copies of the calibration certificates for the portable dust meters are presented in **Appendix F2** and show that the portable direct reading dust meter is capable of providing comparable results with that provided by HVS.

Table 2.4: Impact Air Quality Monitoring Equipment

Monitoring Station	Equipment	Model
DM-5	Portable direct reading dust meter	SIBATA LD-3B (Serial No. 276019 and
DM-6	_	6Z7784)

2.6 Monitoring Schedule for the Reporting Period

The schedule for impact air quality monitoring during the reporting period is provided in **Appendix F3**

2.7 Results and Observations

The monitoring results for 1-hour TSP are summarised in **Table 2.5**. The monitoring data and the graphical presentation are provided in **Appendix F4**.

Table 2.5: Summary of 1-hour TSP Monitoring Results in the Reporting Period

Monitoring Station	Average (μg/m³)	Range (µg/m³)	Action Level (μg/m³)	Limit Level (µg/m³)
DM-5	24	13 – 43	266	500
DM-6	23	14 – 31	260	500

The dust sources in the reporting period included road traffic and nearby construction sites.

No exceedance of Action and Limit Levels was recorded for construction air quality monitoring in the reporting period. No action was thus required to be undertaken in accordance with the Event and Action Plan presented in **Appendix F5**.

3 Noise

3.1 Monitoring Requirements

According to the requirements in the Updated EM&A Manual, regular impact construction noise monitoring shall be carried out at the designated monitoring locations once per week during the construction period of the Project. Construction noise level shall be measured in terms of the A-weighted equivalent continuous sound pressure level (L_{eq}). L_{eq} (30min) shall be used as the monitoring parameter for the time period between 0700 and 1900 hours on normal weekdays. For all other time periods, L_{eq} (5min) shall be employed for comparison with the Noise Control Ordinance (NCO) criteria. As supplementary information for data auditing, statistical results such as L_{10} and L_{90} shall also be obtained for reference.

During the reporting period, regular impact construction noise monitoring at NMS-CA-6, NMS-CA-7, NMS-CA-8 and NMS-CA-9 in Tung Chung Valley commenced on 2 December 2021 (after the commencement of construction works in Tung Chung Valley), while regular impact construction noise monitoring at NMS-CA-5 in Ma Wan Chung continued.

Further details of the impact construction noise monitoring are presented in the following sections.

3.2 Monitoring Locations

A total of five construction noise monitoring stations were identified for impact monitoring in the TCNTE possible development area (PDA) at Tung Chung West and are covered by this Report.

Locations of the impact construction noise monitoring stations covered in this Report are summarised in **Table 3.1** and shown in **Appendix G1**.

Table 3.1: Impact Construction Noise Monitoring Stations

Monitoring Station Location		Type of Measuremer	
NMS-CA-5	Village house in Ma Wan Chung (G/F)	Free field^	
NMS-CA-6	Village house in Shek Mun Kap (G/F)	Free field^	
NMS-CA-7	YMCA of Hong Kong Christian College (Roof Floor)	Façade	
NMS-CA-8	Caritas Charles Vath College (Roof Floor)	Façade	
NMS-CA-9*	Hong Chi Shiu Pong Morninghope School (Roof Floor)	Façade	

Remark: * NMS-CA-9, which was described as "possible school development near Tung Chung Area 39" in the Updated EM&A Manual, was subsequently confirmed as "Hong Chi Shiu Pong Morninghope School" prior to commencement of baseline monitoring.

3.3 Monitoring Parameters, Frequency, Duration and Monitoring Dates

Table 3.2 summarises the parameters, frequency, duration and monitoring dates for impact construction noise quality monitoring during the reporting period.

Table 3.2: Impact Construction Noise Monitoring Parameters, Frequency, Duration and Monitoring Dates

Monitoring Station	Parameter	Frequency and Duration	Monitoring Dates
NMS-CA-5	30-min measurement		
NMS-CA-6	between 0700 & 1900 hrs on	Once every week for 30 mins during the construction period of	4, 13, 19, 26 & 31 May
NMS-CA-7	normal weekdays (Monday	the Project	2022
NMS-CA-8	to Saturday)	•	

[^] For Free Field measurement, +3dB(A) should be added to the measured results.

Monitoring Station	Parameter	Frequency and Duration	Monitoring Dates
NMS-CA-9	L_{eq},L_{10} and L_{90} would be recorded		

3.4 Action and Limit Levels

The Action and Limit Levels for construction noise of the Project are provided in **Table 3.3** below.

Table 3.3: Action and Limit Levels for Construction Noise

Monitoring Station	Time Period	Action Level	Limit Level (dB(A), Leq(30min))
NMS-CA-5			75
NMS-CA-6		When one	75
NMS-CA-7*	0700-1900 hrs on normal weekdays#	documented complaint	70
NMS-CA-8*	nomai weekaaye	is received	70
NMS-CA-9*			(65 during school examination periods)

Note:
If works are to be carried out during restricted hours, the conditions stipulated in the construction noise permit issued by the Noise Control Authority have to be followed.

3.5 Monitoring Equipment

Integrating Sound Level Meters were used to conduct impact construction noise monitoring. They were the Type 1 sound level meter capable of giving a continuous readout of the noise level readings including equivalent continuous sound pressure level (L_{Aeq}) and percentile sound pressure level (L_{X}). They complied with International Electrotechnical Commission Publications 651:1979 (Type 1) and 804:1985 (Type 1). **Table 3.4** summarizes the equipment used in the impact construction noise monitoring. Copies of the calibration certificates for the sound level meters and acoustical calibrators are attached in **Appendix G2**.

Table 3.4: Noise Monitoring Equipment

Monitoring Station	Equipment & Model		
	Integrating Sound Level Meter	Acoustical Calibrator	
NMS-CA-5			
NMS-CA-6			
NMS-CA-7	Rion NL-52 (serial no. 00710259)	Larson Davis CAL200 (serial no. 11333)	
NMS-CA-8			
NMS-CA-9			

3.6 Monitoring Schedule for the Reporting Period

The schedule for impact construction noise monitoring during the reporting period is provided in **Appendix G3**.

3.7 Results and Observations

The monitoring results for construction noise are summarised in **Table 3.5**. The monitoring data and the graphical presentation are provided in **Appendix G4**.

Table 3.5: Summary of Construction Noise Monitoring Results in the Reporting Period

Monitoring Station	Average	Range	Limit Level
	(dB(A), L _{eq(30min)})	$(dB(A), L_{eq(30min)})$	$(dB(A), L_{eq(30min)})$
NMS-CA-5	58^	54 – 61^	- 75
NMS-CA-6	53^	50 – 54^	75

^{*} Denotes school / educational institution.

Monitoring Station	Average	Range	Limit Level
	(dB(A), L _{eq(30min)})	(dB(A), L _{eq(30min)})	$(dB(A), L_{eq(30min)})$
NMS-CA-7	61	56 – 63	70
NMS-CA-8	61	57 – 63	(65 ^{#(1)} during school
NMS-CA-9	61	59 – 62	examination periods)

Note:

The major noise sources during the construction noise monitoring in the reporting period included bird sound, nearby traffic, school activities and aircraft as well as nearby construction sites.

No exceedance of Action and Limit Levels was recorded for construction noise monitoring in the reporting period. No action was thus required to be undertaken in accordance with the Event and Action Plan presented in **Appendix G5**.

^{^ +3}dB(A) Façade correction included for Free Field measurement.

^{*} No school examination was taken place at NMS-CA-9 during this reporting period.

⁽¹⁾ Reduced to 65 dB(A) during HKDSE examination periods at NMS-CA-7 and NMS-CA-8. HKDSE examination period took place from 22 Apr to 14 May. School examination took place at NMS-CA-7 from 16 May to 21

4 Water Quality

4.1 Monitoring Requirements

According to the requirements in the Updated EM&A Manual, regular impact water quality monitoring shall be carried out 3 days per week at the designated monitoring locations during the construction period of the Project. The interval between two sets of monitoring shall not be less than 36 hours. Further details of the impact water quality monitoring are presented in the following sections.

4.2 Monitoring Locations

The locations of the monitoring stations under the Project are shown in **Table 4.1** and **Appendix H1**.

Table 4.1: Impact Water Quality Monitoring Stations

Monitoring Description		Location	
Station		Easting	Northing
TCW-WQM1	Downstream of Tung Chung Stream	810784	815710
Tung Chung Stre	am (West)		
TCW-WQM2	Middle of Tung Chung Stream (West)	810701	815015
TCW-WQM4	Upstream of Tung Chung Stream (West)	810641	814405
TCW-WQM6 ⁽¹⁾	Downstream of Tung Chung Stream (West)	810814	815385
Tung Chung Stre	am (East)		
TCW-WQM3A ⁽²⁾	Middle of Tung Chung Stream (East) [aka Upstream of River Park]	811080	814965
TCW-WQM5A ⁽³⁾	Upstream of Tung Chung Stream (East)	811194	814368
		811138	814498
TCW-WQM7 ⁽¹⁾	Downstream of Tung Chung Stream (East)	810862	815400
	[aka Downstream of River Park]		

Notes

4.3 Monitoring Parameters, Frequency and Duration

Table 4.2 summarises the parameters, frequency and duration for impact water quality monitoring during the reporting period.

Table 4.2: Water Quality Monitoring Parameters, Duration and Frequency

Monitoring Station	Parameters (Units)	Frequency, Duration and Replication	Monitoring Dates
TCW-WQM1, TCW-WQM2, TCW-WQM3A, TCW-WQM4,	 Dissolved Oxygen (DO) (mg/L and % saturation) Temperature (°C) Turbidity (NTU) Salinity (ppt) 	Impact monitoring: 3 days per week during the construction period of the Project.	3, 5, 7, 10, 12, 14, 16, 18, 20, 23, 25, 27 & 30 May 2022

⁽¹⁾ TCW-WQM6 and TCW-WQM7 are additional monitoring stations which can monitor the water quality impact associated with construction activities along the Tung Chung Stream (West) and Tung Chung Stream (East) respectively.

⁽²⁾ TCW-WQM3A is the proposed relocated TCW-WQM3, which will be upstream of the River Park where there are no direct works on Tung Chung Stream (East). The original TCW-WQM3 location lies within the construction works area for the future River Park, which will be directly modified and inaccessible during construction phase.

⁽³⁾ The monitoring location of TCW-WQM5A will be bounded by the coordinates shown, with the exact location depending on the nearest safe accessible and practical location to the original TCW-WQM5.

Monitoring Station	Parameters (Units)	Frequency, Duration and Replication	Monitoring Dates
TCW-WQM5A, TCW-WQM6, TCW-WQM7	pH Suspended Solids (SS) (mg/L) Conductivity ⁽¹⁾ (µS/cm)	Not less than 36 hours' interval between two sets of monitoring. Two (2) replicate in-situ measurements and water samples.	

Remark:

- 1. Water depth measurement is not applicable due to very shallow depth of the monitoring locations. Note:
- (1) Conductivity is an additional reference monitoring parameter adopted during a review of the baseline monitoring programme in June 2021. It is not compulsory as prescribed in the Updated EM&A Manual.

In addition to the parameters presented in **Table 4.2**, other relevant data were also recorded, including monitoring location, time, approximate water depth (by visual observation), tidal condition (if applicable), weather conditions and any special phenomena or work underway at the Project site.

4.4 Action and Limit Levels

The calculated Action and Limit Levels of the impact water quality monitoring for the monitoring stations of Tung Chung Stream (West), Tung Chung Stream (East) and TCW-WQM1 are shown in **Table 4.3** below.

Table 4.3: Calculated Action and Limit Levels for Impact Water Quality Monitoring

Parameters	Action Level	Limit Level
Tung Chung Stre	am (West)	
DO in mg/L	3.4 mg/L	3.3 mg/L
SS in mg/L	7.0 mg/L or	16.9 mg/L or
	120% of upstream control station at the same tide of the same day, whichever is higher	130% of upstream control station at the same tide of the same day, whichever is higher
Turbidity in NTU	6.7 NTU or	22.0 NTU or
	120% of upstream control station at the same tide of the same day, whichever is higher	130% of upstream control station at the same tide of the same day, whichever is higher
Tung Chung Stre	am (East)	
DO in mg/L	4.2 mg/L	4.0 mg/L
SS in mg/L	7.2 mg/L or	9.7 mg/L or
	120% of upstream control station at the same tide of the same day, whichever is higher	130% of upstream control station at the same tide of the same day, whichever is higher
Turbidity in NTU	9.8 NTU or	22.5 NTU or
	120% of upstream control station at the same tide of the same day, whichever is higher	130% of upstream control station at the same tide of the same day, whichever is higher
TCW-WQM1		
DO in mg/L	2.2 mg/L	1.8 mg/L
SS in mg/L	7.3 mg/L	9.7 mg/L
Turbidity in NTU	24.7 NTU	35.3 NTU

Notes:

- (1) For DO, non-compliance occurs when monitoring results is lower than the limits.
- (2) For SS and Turbidity, non-compliance occurs when monitoring results is larger than the limits.
- (3) Action and Limit Levels do not apply to TCW-WQM4 and TCW-WQM5A which are upstream control stations.

4.5 Monitoring Equipment

Table 4.4 summarizes the equipment used in the impact water quality monitoring works. All the monitoring equipment complied with the requirements set out in the Updated EM&A Manual. Copies of the calibration certificates are attached in **Appendix H2**.

Table 4.4: Water Quality Monitoring Equipment

Equipment	Brand and Model
Multifunctional Meter (in-situ measurement of DO, pH,	Horiba U-53
temperature, salinity, turbidity and conductivity)	(serial no. LUAVCDWU)

4.6 Monitoring Schedule for the Reporting Period

The schedule for impact water quality monitoring during the reporting period is provided in **Appendix H3**.

4.7 Results and Observations

A total of 13 monitoring events for impact water quality monitoring were conducted at all designated monitoring stations during the reporting period. Impact water quality monitoring results and graphical presentations were provided in **Appendix H4**.

Action Level exceedances were recorded for water quality impact monitoring in the reporting period and the Event and Action Plan (**Appendix H5**) was undertaken. Investigations on the action level exceedances were conducted and summarised in **Table 4.5** below.

Table 4.5: Details of Exceedances Recorded for Water Quality Monitoring

Date	Parameter	Station	Type	Justification
12 May 2022	Suspended Solids	Suspended Solids TCW-WQM1		(a) (b) (c) (d) (e)
	Suspended Solids	TCW-WQM3A		(a) (b) (c) (d) (e)
	Turbidity			(a) (b) (c) (d) (e)

Remarks: (a) No spillage incident in the Tung Chung Stream was reported by the Contractors.

- (b) Elevated measurement results were recorded from the corresponding upstream monitoring stations of Tung Chung Stream, which indicated that the deterioration of the water quality was not due the activity at the vicinity of the monitoring stations.
- (c) Rainy weather was recorded during the sampling day. High river water flow which might cause the resuspension of the deposited sediment in the river bed.
- (d) The existing surface drain along the site boundary of Area 42 has been intercepted and the construction runoff as collected from Area 42 was diverted to the settling tank and reused on-site. No deficiency in the practices of the implementation of the environmental mitigation measures was observed.
- (e) No similar exceedance was recorded from the subsequent monitoring event.

Based on the investigation findings, the exceedances were considered not related to the Project.

Nevertheless, the Contractors were reminded to implement all relevant mitigation measures for the works, including provide periodic maintenance of construction plant and equipment as well as maintain good site practice. The ET will keep on checking monitoring data, plant, equipment and Contractors' working methods.

5 Ecology

5.1 Monitoring Requirements

According to the requirements in the Updated EM&A Manual, regular impact ecological monitoring in terms of water quality, aquatic invertebrate and fish species shall be carried out on a monthly basis at the designated monitoring locations during the construction period of the Project. Further details of the impact ecological monitoring are presented in the following sections.

5.2 Monitoring Locations

A total of seven (7) monitoring stations at Tung Chung Stream covering both River Park and other Public Works (road crossings, polders, and stormwater attenuation and treatment ponds) were identified for the construction phase monitoring.

The locations of the monitoring stations are presented in **Table 5.1** and **Appendix I1**. Note that the exact monitoring locations were subject to fine adjustment based on site conditions (e.g. adverse weather conditions, blockage by plants, rocks or other obstacles).

Table 5.1: Impact Ecological Monitoring Stations

Monitoring	Description	Coordinates					
Station		Easting	Northing	Latitude (N)	Longitude (E)		
RP1	Conservation Zone (Natural Section)	811150	814469	22°16'07.95"N	113°55'59.41"E		
RP2	Upstream of River Park	811083	814895	22°16'21.77"N	113°55'57.05"E		
RP3	Revitalisation Zone (Channelised Section)	811036	815076	22°16'27.66"N	113°55'55.38"E		
RP4	Downstream of River Park	810846	815402	22°16'38.25"N	113°55'48.72"E		
PW1	Near Public Works	811099	814589	22°16'11.83"N	113°55'57.63"E		
PW2	Near Public Works	810933	815318	22°16'35.54"N	113°55'51.79"E		
PW3	Near Public Works	810789	815658	22°16'46.56"N	113°55'46.71"E		

5.3 Monitoring Frequency and Dates

As required under the Updated EM&A Manual, the impact ecological monitoring shall cover the full construction programme on a monthly basis. **Table 5.2** summarises the frequency and monitoring dates for the impact monitoring during the reporting period.

Table 5.2: Impact Ecological Monitoring Schedule

May 2022	18 May 2022
Month	Other Public Works Study Area (PW1, PW2 and PW3)
Reporting	River Park Study Area (RP1, RP2, RP3 and RP4) and

5.4 Monitoring Methodology

5.4.1 Stream Fauna

Several survey methods which covered different components of the stream fauna (which includes fish species and aquatic invertebrates) were used to monitor the study areas to yield a comprehensive result:

- 1. Direct Observation covered all along the accessible part of the watercourse to provide a species list of fish and aquatic invertebrate with corresponding relative abundance.
- 2. Baited Fish Cage At each sampling location, two replicates of baited fish cages were deployed for a duration of at least one hour. All collected fish and aquatic invertebrate species were recorded and their abundance were counted. This method may collect fishes which are wary of humans. Permit from the AFCD was obtained before the use of any equipment to collect stream fauna in any streams and watercourses.
- 3. Kick Sampling at least two replicates of kick sampling were performed at each monitoring station to obtain aquatic invertebrate (and fish) samples. Kick sampling is a relatively quick method to survey aquatic invertebrates in shallow fast-flowing streams. A ~30 cm x ~30 cm kick sampler with ~0.5 mm mesh size was placed on the stream bed and the area just upstream of the sampler were vigorously disturbed by kicking for one minute. The contents of the net were transferred to suitable containers with freshwater for identification and counting in situ. All identifiable samples were released back to the sampling locations.

5.4.2 Water Quality

Ecologically-related water quality monitoring, including *in situ* measurements and collection of water samples for laboratory analysis, was conducted at each monitoring location. Duplicate water samples were collected at surface water level at each monitoring location.

Water quality parameters including Dissolved Oxygen (in % saturation and mg/L), pH value, temperature, turbidity and salinity were measured in situ while the other parameters, including Suspended Solids (SS), Ammonia, Total Kjeldahl Nitrogen (TKN), Total Phosphorus (TP), Escherichia coli (E. coli), 5-day Biochemical Oxygen Demand (BOD5), Chemical Oxygen Demand (COD) and Oil & Grease, were measured at a HOKLAS accredited laboratory for water quality analysis. Other relevant data, including time, water depth, weather conditions and special phenomena or works underway in the vicinity were recorded.

The measured water quality parameters and laboratory testing method are shown in **Table 5.3**.

Table 5.3: Ecologically-related Water Quality Monitoring Parameters and Testing Methods

i didilictoi		
In situ measurements	Instrument Range Capability (1)	Measurement Resolution
рН	0 – 14 pH units	0.01 pH units
Salinity	0 – 70 ppt	0.01 ppt
Temperature	-5 – 70°C	0.1°C
Turbidity	0 – 4000 NTU	0.1 NTU
Dissolved Oxygen (DO)	0 – 50 mg/L	0.1 mg/L
	0 – 500% saturation	0.1% saturation
Laboratory testing and analyses	Method Reference	Level of Reporting
Suspended Solids (SS)	APHA 2540 D	0.5 mg/L
Ammonia as N	APHA 4500 NH₃ G	0.01 mg/L

Parameter

Parameter

Total Kjeldahl Nitrogen (TKN) as N	АРНА 4500 Р: J; АРНА 4500 NO3: I	0.05 mg/L
Total Phosphorus as P	APHA 4500 P: J	0.01 mg/L
E. coli	TM09/EC/10/98 Issue 3, HKEPD	1 CFU/100mL
5-day Biochemical Oxygen Demand (BOD₅)	APHA 5210 B	1 mg/L
Chemical Oxygen Demand (COD)	APHA 5220 B	2 mg/L
Oil & Grease	APHA 5520 B	2 mg/L

Note (1): Specifications based on YSI ProDSS Multiparameter Water Quality Meter

The equipment used for the *in situ* ecologically-related water quality monitoring work is summarised in **Table 5.5**. Copies of the calibration certificates are attached in **Appendix 12**.

Table 5.4: Ecologically-related Water Quality Monitoring Equipment

Equipment	Brand and Model
Multifunctional Meter (in-situ measurement of DO, pH,	Horiba U-53
temperature, salinity and turbidity)	(serial no. X42XKBNO)

5.5 Action and Limit Levels

The Action and Limit Levels for the impact ecological monitoring are defined in **Table 5.5**.

Table 5.5: Action and Limit Levels for Impact Ecological Monitoring

Exceedance Level	Description		
Action Level	Reduction in the monthly taxa diversity (i.e. number of species) of fish or aquatic invertebrate (macroinvertebrate only) of any monitoring station compared to the corresponding monitoring season and station of the baseline survey by 30% .		
Limit Level	Reduction in the monthly taxa diversity (i.e. number of species) of fish or aquatic invertebrate (macroinvertebrate only) of any monitoring station compared to the corresponding monitoring station and season of the baseline survey by 50% .		

For ease of reference, the Action and Limit Levels for aquatic invertebrate and fish (rounded to nearest 0.1) in Wet Season (April to October) and Dry Season (November to March) at each monitoring station are provided in **Table 5.6** and **Table 5.7** respectively.

Table 5.6: Action Level (AL) and Limit Level (LL) for Number of Aquatic Invertebrate Species at Each Monitoring Station during Wet (Apr - Oct) and Dry (Nov - Mar) Seasons

		River Park Study Area				Public	Works Stud	ly Area
		RP1	RP2	RP3	RP4	PW1	PW2	PW3
Wet	AL	2.1	1.2	1.3	2.0	0.9	2.8	1.6
season	LL	1.5	0.9	1.0	1.5	0.7	2.0	1.2
Dry	AL	1.5	1.3	0.7	2.5	1.4	2.6	0.5
season	LL	1.1	0.9	0.5	1.8	1.0	1.9	0.4

Table 5.7: Action Level (AL) and Limit Level (LL) for Number of Fish Species at Each Monitoring Station during Wet (Apr – Oct) and Dry (Nov – Mar) Seasons

		River Park Study Area				Public	Works Stud	ly Area
		RP1	RP2	RP3	RP4	PW1	PW2	PW3
Wet	AL	3.6	3.5	0.9	5.0	2.8	0.9	4.4
season	LL	2.6	2.5	0.7	3.6	2.0	0.7	3.2
Dry season	AL	4.1	3.5	0.1	4.3	4.7	0.5	4.2
	LL	2.9	2.5	0.1	3.1	3.4	0.4	3.0

5.6 Results and Observations

5.6.1 Environment of Stream Courses

The environment of stream courses at the monitoring stations for the River Park Study Area (RP1 to RP4) and other Public Works Study Area (PW1 to PW3) are presented in **Table 5.8.**

Table 5.8: Environment of Stream Courses at each Monitoring Station

Station Name	Location	Physical Environment
RP1	Conservation Zone (Natural Section)	Fast flowing natural stream. The substrate was dominant with boulders and rocks, and sands were sometimes observed. Woodland with dense vegetation was on the river banks.
RP2	Upstream of River Park	Moderate fast flowing natural stream. The substrate was in the form of boulders, rocks, sand and silt mixture. Short but dense herbaceous vegetation was on the right bank of the stream, while dense woodland was on the left bank. A truck with water pump was observed extracting water from the stream.
RP3	Revitalisation Zone (Channelised Section)	Slow flowing artificial, concretised and channelised stream. Pavement was the dominant substrate with little sand and rock. Algal mat was observed at this site. Short but dense herbaceous vegetation was on the river banks. A culvert was on the right bank of the stream, and a footbridge was on the upstream of the location.
RP4	Downstream of River Park	The channelised section of Tung Chung Stream ended at the upstream of RP4. RP4 is a moderate fast flowing natural stream close to the estuary. The substrate was in the form of boulders, rocks, sand and silt mixture. Woody plants and herbaceous plants were along the river banks.
PW1	Near Public Works	Fast flowing natural stream. The substrate was dominant with boulders and rocks, and sand was sometimes observed. Woodland with dense vegetation was on the river banks.
PW2	Near Public Works	Slow flowing artificial, concretised and channelised stream. Pavement was the dominant substrate with little sand and rock. Algal mat was observed at this site. Short but dense herbaceous vegetation was on the left bank of the stream, woody plants and herbaceous plants were on right bank of the river.
PW3	Near Public Works	A natural estuary. The substrate was dominant with sand and mud. Dense mangroves were on the shores of the estuary.

5.6.2 Stream Fauna

A total of 14 aquatic invertebrate species and 16 fish species were recorded across all monitoring stations during the reporting period. The monitoring results for aquatic invertebrate and fish species are summarised in **Table 5.9** and **Table 5.10**. The monitoring data is provided in

Appendix I4 and **Appendix I5**. Representative photos of the species of conservation importance and other species recorded are presented in **Appendix I3**.

Table 5.9: Summary of Aquatic Invertebrate Species Recorded in the Reporting Period

Common Name	Species Name	River Park Study Area			Public Works Study Area			
		RP1	RP2	RP3	RP4	PW1	PW2	PW3
Scud	Amphipoda							✓
Small Minnow Mayfly	Baetidae	~	✓	~		~	~	
Freshwater Shrimp	Caridina cantonensis			~			~	
Hepu Mitten Crab	Eriocheir hepuensis				~			
Black-banded Gossamerwing (Larva) Euphaea decorata		~				✓		
Caddisfly (Larva)	Hydropsychidae	~	✓			~		
Caddisfly (Larva) Lepidostomatidae						✓		
Freshwater Prawn Macrobrachium sp.					~			
Chinese Hooktail (Larva) Ophiogomphus sinicus						~		
European Physa Physella acuta						~		
Water Strider	Ptilomera tigrina	~			~			✓
Smaller Water Strider	Rhagovelia sp.	~					~	✓
Caddisfly (Larva) Rhyacophilidae			✓					
Freshwater Snail	Tarebia granifera				~			
	Total no. of species	5	3	2	4	6	3	3
	Action Level (Wet Season)	2.1	1.2	1.3	2.0	0.9	2.8	1.6
-	Limit Level (Wet Season)	1.5	0.9	1.0	1.5	0.7	2.0	1.2

Table 5.10: Summary of Fish Species Recorded in the Reporting Period

Common Name	Species Name	River Park Study Area			Public Works Study Area			
		RP1	RP2	RP3	RP4	PW1	PW2	PW3
Beijiang Thick-lipped Barb	Acrossocheilus beijiangensis (1)		~			~		
Chinese Barb	Barbodes semifasciolatus		~		~			
Sharp-nosed Sand Goby	Favonigobius gymnauchen						~	
Common Silverbiddy	Gerres oyena						✓	
Fork Tongue Goby	Glossogobius giuris							✓
Broken-band Hillstream Loach	Liniparhomaloptera disparis	* *			✓			
Mullet	Mugilidae				~			~
Rice Fish	Oryzias curvinotus (1)				~			
Predaceous Chub	Parazacco spilurus ⁽²⁾	✓	~		~	~		
Southern Platyfish	Poecilia maculatis					~		
Sucker-belly Loach	Pseudogastromyzon myersi	✓						
-	Rhinogobius duospilus	✓	~					
Jarbua Terapon	Terapon jarbua							✓
Tilapia	Tilaipia sp.							✓
Swordtail	Xiphophorus hellerii		✓	~	~	~	~	
Variable Platyfish	Xiphophorus variatus					~		
	Total no. of species	4	6	1	5	6	1	6
	Action Level (Wet Season)	3.6	3.5	0.9	5.0	2.8	0.9	4.4
	Limit Level (Wet Season)	2.6	2.5	0.7	3.6	2.0	0.7	3.2

Note (1): Species of conservation importance (Fellowes et. al., 2002)

Note (2): Species of conservation importance (Zheng & Wang,1998)

No exceedance of Action and Limit Levels was recorded for the impact ecological monitoring in the reporting period, comparing against the baseline monitoring data. No action was thus required to be undertaken in accordance with the Event and Action Plan presented in **Appendix 16**.

5.6.3 Water Quality

As the EM&A programme of TCW already has its own river water quality monitoring (i.e. 3 times per week, refer to **Section 4** of this EM&A Report) and its associated Action and Limit Levels, this section of ecologically-related water quality monitoring results (i.e. at monthly basis) will be adopted for facilitating the investigation in case of any trigger of Action and Limit Levels of the ecological monitoring. The ecologically-related water quality monitoring result during the reporting period is summarised in **Appendix 17**.

5.7 References

Fellowes, J., M. Lau, D. Dudgeon, G.T. Reels, G.W.J., Ades, G. Carey, B. Chan, K. Roger, K.S. Lee M. Leven, K. Wilson and Y.T. Yu. 2002. Wild animals to watch: terrestrial and freshwater fauna of conservation concern in Hong Kong. Memoirs of the Hong Kong Natural History Society. 25:123-159.

Zheng, G., and Wang, Q. 1998. China Red Data Book of Endangered Animals: Aves. Science Press, Beijing. China. 346pp.

6 Waste Management Status

6.1 General

The Contractors of Contracts 5 and 6 have each obtained a waste disposal billing account and registered as chemical waste producer. Sufficient numbers of receptacles were available for general refuse collection and sorting.

All dump trucks engaged on site were equipped with Real Time Tracking and Monitoring (RTTM) system during the reporting period. The Surveillance Team of the ET conducted regular site inspections on the dump trucks and their track records. No illegal dumping and landfilling of C&D materials was found during the reporting period.

Wastes generated during this reporting period include mainly non-inert construction wastes. Reference has been made to the waste flow tables prepared by the Contractors. The quantities of different types of wastes and imported fill materials are summarised in **Table 6.1**.

Table 6.1: Quantities of Different Waste Generated and Imported Fill Materials for TCW

Month / Year	Inert C&D Materials ^(a) (in '000m ³)	Imported Fill Materials ^(d) (in '000m ³)	Inert Construction Waste Re-used in the Contract (in '000m³)	Inert Construction Waste Re-used in other Projects ^(e) (in '000m³)	Non-inert Construction Waste ^(b) (in '000m³)	Recyclable Materials ^(c) (in '000kg)	Chemical Waste (kg)
Mar 2022	0.42*	0.015	0	0.42*	0.46	0.103	0
Apr 2022	3.99*	2.53	0.93	3.06*	0.46	0.103	0
May 2022	0.85	0	0	0.85	0.23	0.166	0

(a) Inert construction and demolition wastes include hard rock and large broken concrete, and materials disposed as public fill.

- (b) Non-inert construction wastes include general refuse disposed at landfill.
 (c) Recyclable materials include metals, paper, cardboard, plastics and others.
 (d) Imported fill materials include public fill.
- (e) Inert Construction Waste reused in other construction contracts under TCNTE.
- (f) Updated figure for the previous month is reported and marked with an asterisk (*).

7 EM&A Site Inspection

7.1 Monitoring Requirements

Environmental site inspections were carried out on a weekly basis with the Contractors and ER to monitor the implementation of proper environmental pollution control and mitigation measures for air quality, noise, water quality, waste management, ecology and landscape and visual impacts under the Project.

7.2 Site Inspections and Key Observations

In the reporting period:

- Five (5) site inspections were carried out on 3, 11, 19, 24 and 31 May 2022 for Contract 5; and
- Five (5) site inspections were carried out on 5, 12, 17, 26 and 31 May 2022 for Contract 6.

Key observations during the site inspections are summarised in **Table 7.1**.

The Contractors have rectified all of the observations identified during environmental site inspections in the reporting period. The Contractors were reminded to implement all relevant mitigation measures related to construction dust, construction noise, water quality, waste management, ecology and landscape and visual outlined in the EIA Report and the Updated EM&A Manual.

Table 7.1: Key Observations Identified during Site Inspections in this Reporting Period

Contract No.	Inspection Date(s)	Environmental Observation	Recommendation / Remark
Contract 5	3 May 2022	Area Part D and Part E in Ma Wan Chung	• Nil
		No deficiency was observed	
	11 May 2022	Area Part D, Part E and Part H in Ma Wan Chung	• Nil
		 No deficiency was observed 	
	19 May 2022	Area Part D, Part E and Part H in Ma Wan Chung	• Nil
		 No deficiency was observed 	
	24 May 2022	Area Part D and Part E in Ma Wan Chung	• Nil
		 No deficiency was observed 	
	31 May 2022	Area Part D, Part E and Part H in Ma Wan Chung	• Nil
		 No deficiency was observed 	
Contract 6	5 May 2022	Area 42 in Tung Chung Valley	Area 42 in Tung Chung Valley
		 Hoarding was not extended along the site boundary 	The Contractor was urged to extend the hoarding along the site
		Temporary Bridge A	boundary.
		 No deficiency was observed 	
	12 May 2022	Area 42 in Tung Chung Valley	Area 42 in Tung Chung Valley
		 Hoarding was not extended along the site boundary 	The Contractor was urged to extend the hoarding along the site
		Temporary Bridge A	boundary.
		 No deficiency was observed 	
	17 May 2022	Area 42 in Tung Chung Valley	Area 42 in Tung Chung Valley
		 Hoarding was not extended along the site boundary 	 The Contractor was urged to extend the hoarding along the site
		Operation Manual was not observed at the wastewater treatment	boundary.
		facilities	 The Contractor was urged to provide a copy of Operation Manual a the wastewater treatment facilities.
		 Flow measuring device was not observed at the wastewater treatment facilities 	The Contractor was urged to install a flow measuring device at the
		 No drip tray was observed for the chemicals 	wastewater treatment facilities.
		Compensatory Woodland	The Contractor was urged to provide drip tray for the proper
		No deficiency was observed	containment of chemicals.
	26 May 2022	Area 42 in Tung Chung Valley	Area 42 in Tung Chung Valley
		 Flow measuring device was not observed at the wastewater treatment facilities 	 The Contractor was urged to install a flow measuring device at the wastewater treatment facilities.
		Sewage Pumping Station-A and Temporary Bridge A	
		 No deficiency was observed 	

Contract No.	Inspection Date(s)	Environmental Observation	Recommendation / Remark			
	31 May 2022	Area 42 in Tung Chung Valley	Area 42 in Tung Chung Valley			
		 Flow measuring device was not observed at the wastewater treatment facilities 	 The Contractor was urged to install a flow measuring device at the wastewater treatment facilities. 			
		 Coverage and notice at the boreholes for Land Contamination Assessment was not observed 	 The Contractor was urged to provide proper coverage and notice at the boreholes when the Land Contamination Assessment has not 			
		Compensatory Woodland and Temporary Bridge A	yet completed.			
		 No deficiency was observed 				

8 Implementation Status of Environmental Mitigation Measures

A summary of the Environmental Mitigation Implementation Schedule is presented in **Appendix C**. The necessary mitigation measures were implemented properly for the Project.

9 Summary of Exceedances of the Environmental Quality Performance Limit

The monitoring results for air quality monitoring (1-hour TSP) complied with the Action/Limit levels in the reporting period. No Action/Limit Level exceedance was recorded for the construction noise monitoring in the reporting period.

Three (3) action level exceedances were recorded for water quality impact monitoring in the reporting period. The investigations on the action level exceedances were conducted and the results were summarised in **Section 4.7**.

No Action/Limit Level exceedance was recorded for impact ecological monitoring in the reporting period.

Cumulative statistics on exceedance are summarised in Appendix J.

10 Summary of Complaints, Notification of Summons and Successful Prosecutions

There was no environmental complaint, notification of summons or prosecution recorded in the reporting period.

Statistics on complaints, notifications of summons, successful prosecutions are summarised in Appendix J.

11 Future Key Issues

11.1 Construction Programme for the Coming Reporting Period

Works to be undertaken in the next monitoring period of June 2022 are summarised in **Table 11.1** below, together with the key issues and the key mitigation measures.

The ET will keep track on the construction works to confirm compliance of environmental requirements and the proper implementation of all necessary mitigation measures. The ET will also recommend to the Contractors about the environmental toolbox topics on the abovementioned key issues for the next reporting period.

11.2 Monitoring Schedule for the Coming Reporting Period

The tentative schedules for environmental monitoring in June 2022 are provided in Appendix K.

Retain and protect all existing trees and vegetation within the study area which are not directly affected by the works

Table 11.1: Major Activities for the next Reporting Period

Activities Key Issues Key Mitigation Measures Contract No. NL/2020/05 ("Contract 5") Tung Chung New Town Extension - Site Formation and Infrastructure Works at Ma Wan Chung Ground Investigation and Installation of Geotechnical **Dust Emission** Good site practices Instrumentation at Part E Handling and storage of C&D materials generated from Regular water spraying on stockpiles Site Clearance at Part E and H construction activities Provide tarpaulin sheets coverage on stockpiles Geotechnical Investigation at Part G Noise from plant operation Sorting and reuse of C&D materials as far as practicable Forming Site Access at Part G Emission of dark smoke from PMEs Use of QPME and noise barrier/acoustic mat Slope Excavation and Soil Nail Installation at Part E Efficiency of wastewater and drainage management Regular maintenance of PMEs Temporary ELS Works at Part E Tree Protection Implementation of wastewater and drainage management Road Diversion at Part E and F Retain and protect all existing trees and vegetation within the study area which are not directly affected by the works Construction of Rock Fall Fence at Part E Excavation for Drainage Work at Part E Sheet-piling Work at Part E Excavation for Retaining Wall Construction at Part E Construction of Haul Road at Part H Hoarding and Fencing Erection at Part H Trial Pit Excavation at F and H Pre-drill for Piling Work at Part D and H Piling Work at Part D and H Demolition of Existing Structures at Part D Contract No. NL/2020/06 ("Contract 6") Tung Chung New Town Extension - Site Formation and Infrastructure Works at Tung Chung Valley, Phase 1 Site Clearance at Area 42, Road L29 and Road L30 **Dust Emission** Good site practices Handling and storage of C&D materials generated from Site Investigation and sampling at the potential land Regular water spraying on stockpiles contamination sites at Area 42 under EPD approved construction activities Provide tarpaulin sheets coverage on stockpiles Supplementary Contamination Assessment Plan Noise from plant operation Sorting and reuse of C&D materials as far as practicable Site Formation at the non-contamination sites at Area 42 Emission of dark smoke from PMEs Use of QPME and noise barrier/acoustic mat Backfilling for Ramp Formation at Temporary Bridge A Efficiency of wastewater and drainage management Regular maintenance of PMEs Tree Protection Implementation of wastewater and drainage management

12 Conclusions and Recommendations

General

This EM&A Report presents the findings of the EM&A activities undertaken for the Project – i.e., Tung Chung New Town Extension (TCNTE) development in Tung Chung West (TCW) – during the period from 1 to 31 May 2022 in accordance with the Updated EM&A Manual and the requirements of the Environmental Permit (EP) (No. EP-519/2016).

Air Quality

No exceedance of Action/Limit Levels was recorded for the air quality monitoring (1-hour TSP) in the reporting period.

Noise

No exceedance of Action/Limit Levels was recorded for the construction noise monitoring in the reporting period.

Water Quality

No Project-related Action/Limit level exceedance was recorded for water quality monitoring after investigation.

Ecology

No exceedance of Action/Limit Levels was recorded for impact ecological monitoring in the reporting period.

Environmental Site Inspections

Environmental site inspections were carried out during the reporting period. Recommendations on remedial actions were given to the Contractors for the deficiencies identified during the site inspections.


Environmental Complaint, Notification of Summons or Prosecution


There was no environmental complaint, notification of summons or prosecution recorded in the reporting period.

Recommendations

The ET will keep track of the construction works to confirm compliance of environmental requirements and the proper implementation of all necessary mitigation measures.

Figures

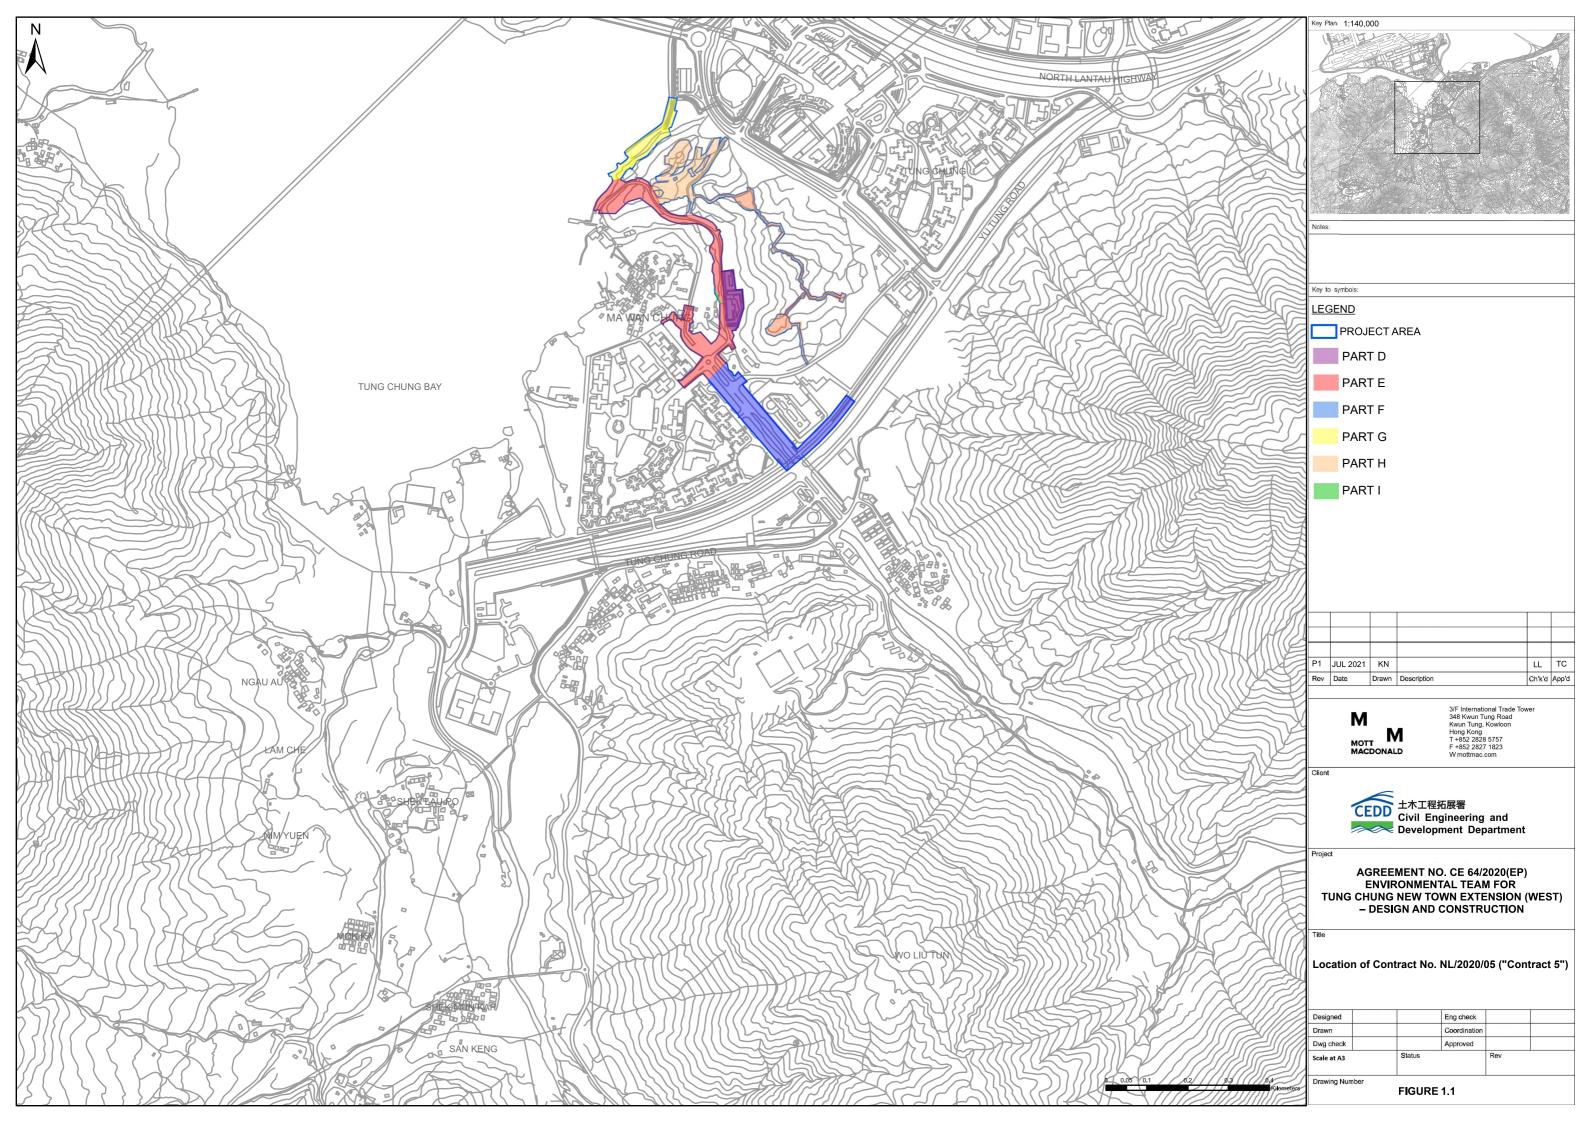


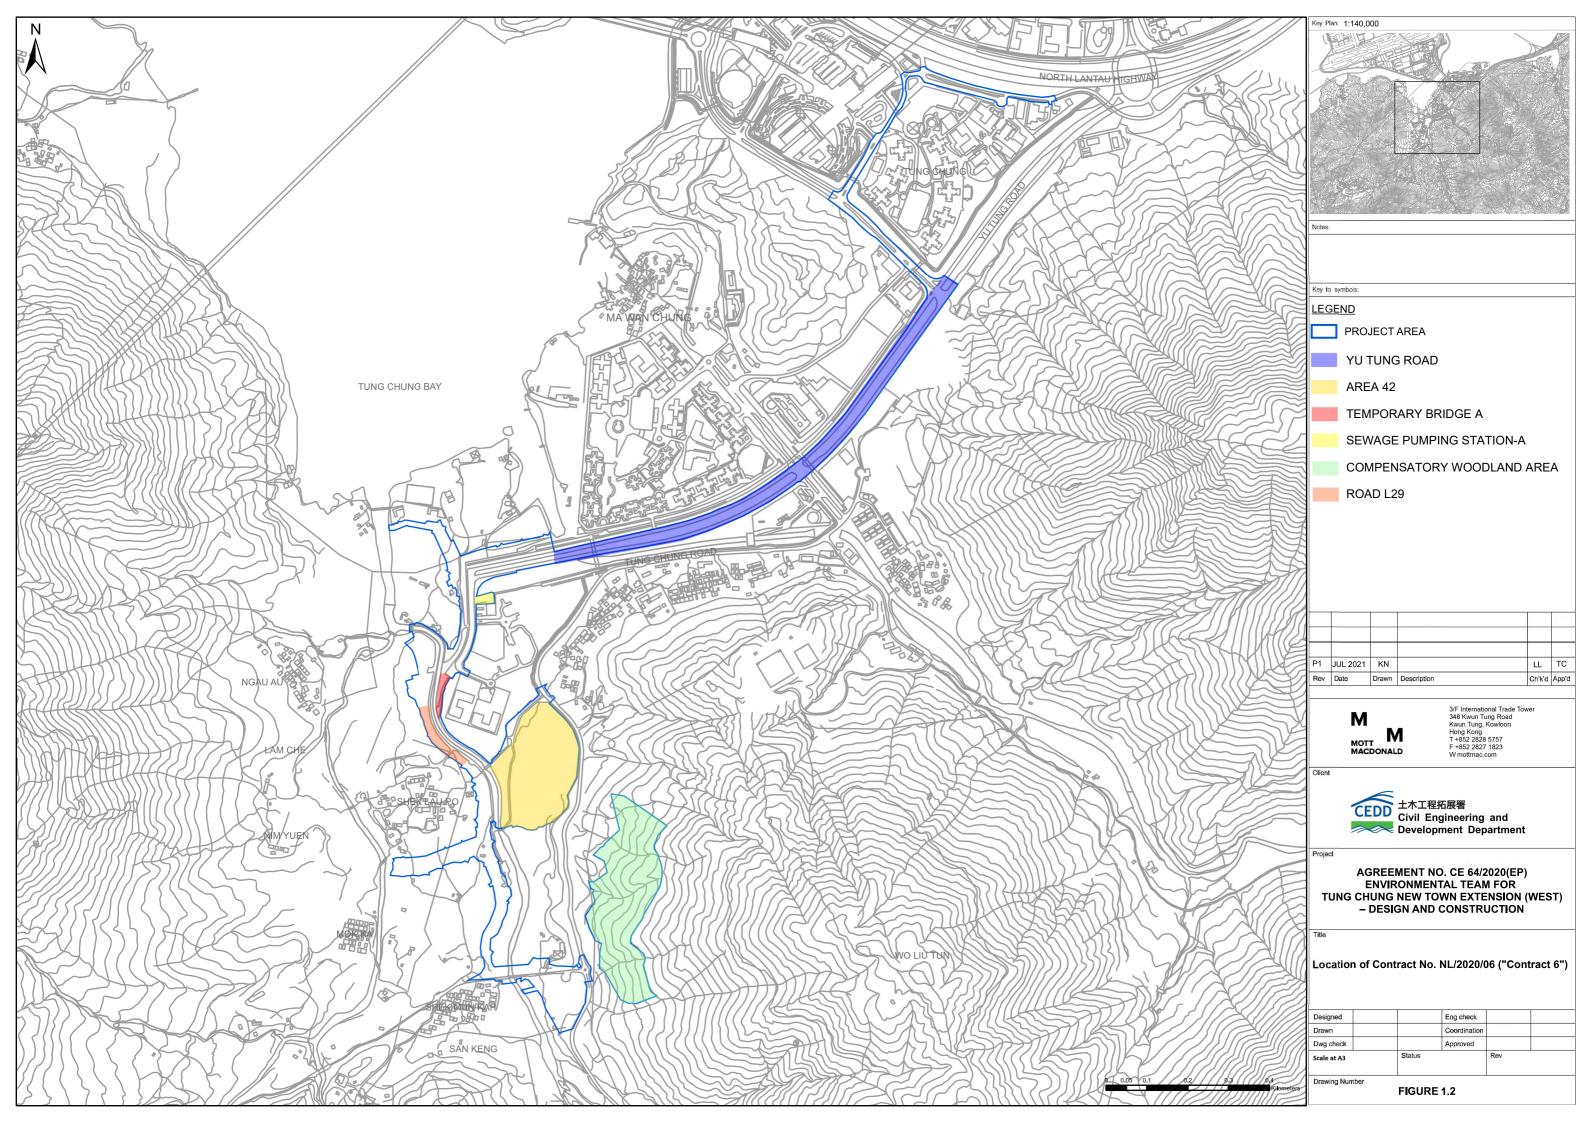


Appendices


A.	Project Organisation	36
B.	Construction Works Programme	37
C.	Environmental Mitigation Implementation Schedule	38
D.	Status of Submissions and Implementation Status of Mitigation Measures under EP	39
E.	Status of Statutory Environmental Requirements	40
F.	Air Quality	41
G.	Noise	42
H.	Water Quality	43
l.	Ecology	44
J.	Cumulative Statistics on Exceedances, Environmental Complaints, Notifications of Su Status of Prosecutions	mmons and 45
K.	Monitoring Schedule for the Next Reporting Period	46


A. Project Organisation

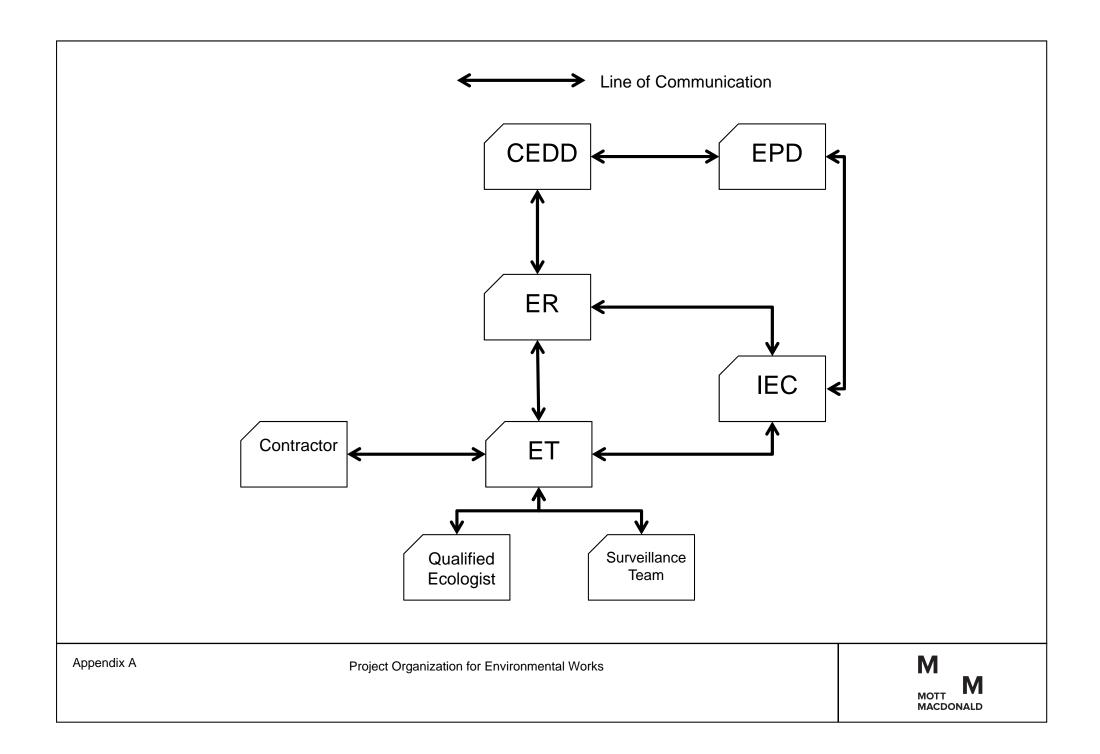

B. Construction Works Programme

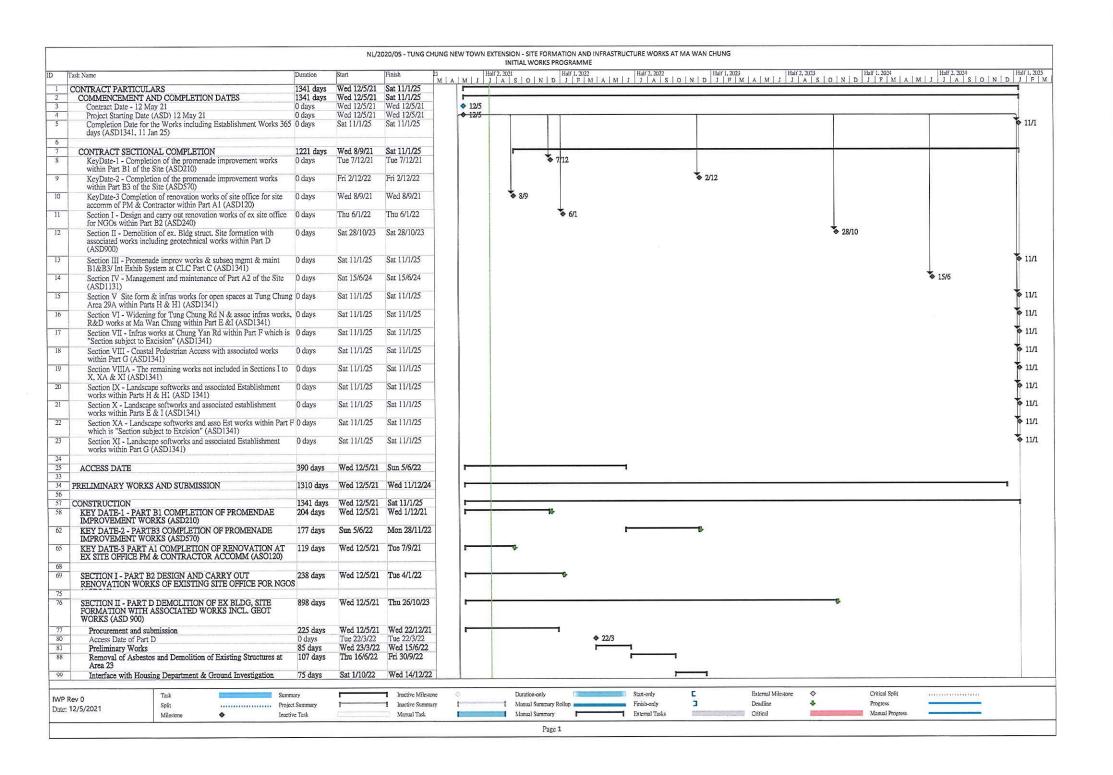

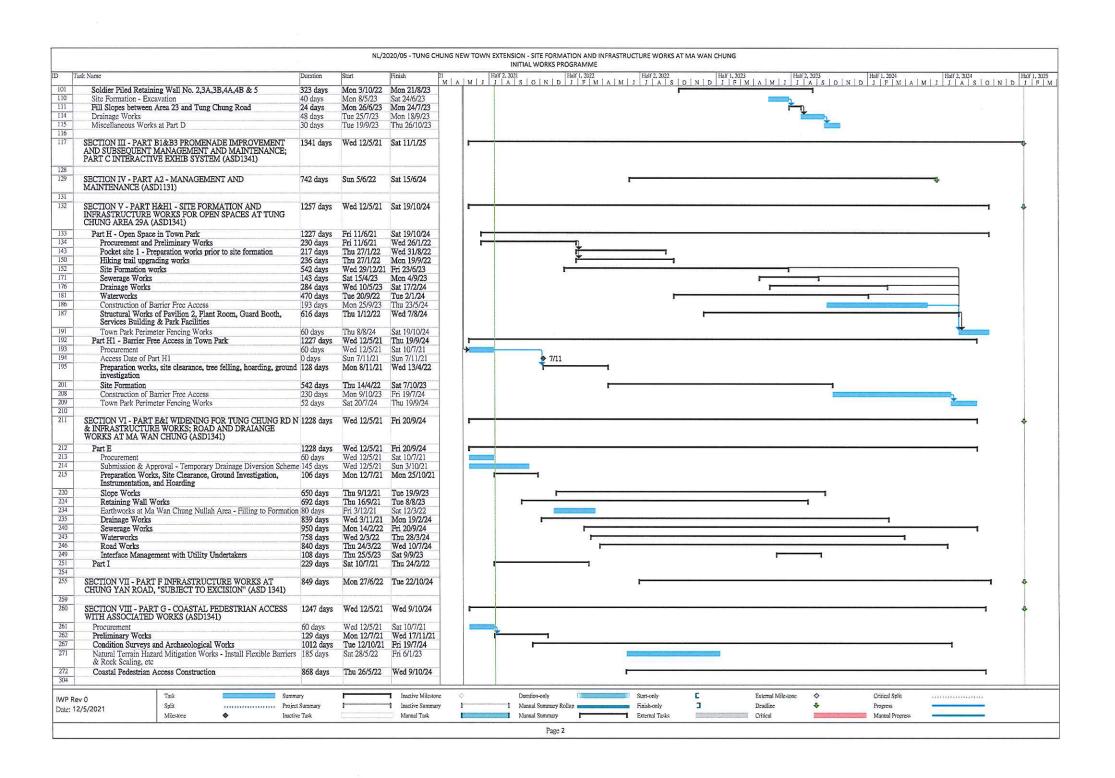

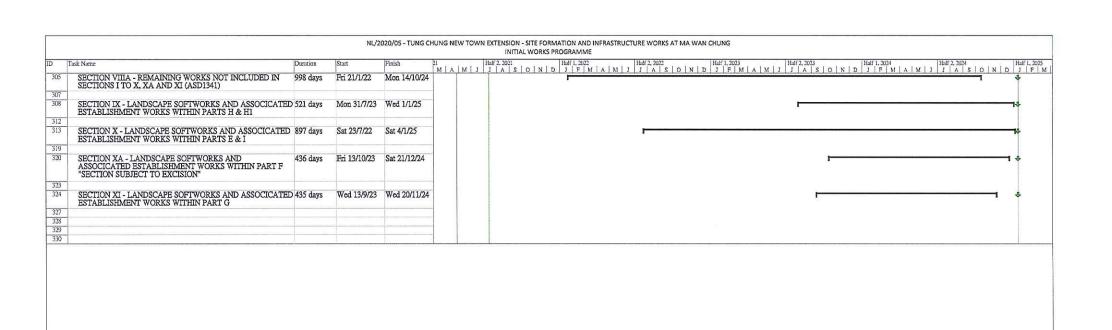

Contract No. NL/2020/06

Contract Title: Tung Chung New Town Extension – Site Formation and Infrastructure Works at Tung Chung Valley, Phase1

Working Programme														_																									
	 		2021							2022				┷				2023								2024								2025				202	_
	Mar Apr	May Ju	un Jul A	Aug Se	p Oct No	ov De	c Jan Feb	Mar Apı	r May J	un Jul	Aug Sep	Oct N	lov Dec	c Jan F	eb Ma	ar Apr	May J	un Jul	Aug Se	ep Oct	Nov D	ec Jan	Feb Ma	ar Apr	May	Jun Jul	Aug Se	ep Oct	Nov D	ec Jan	Feb N	/lar Apr	May .	un Jul	Aug Sep	Oct N	ov Dec	Jan	Feb
Preparation works (GI inverstigation and other preparation									1 1					11			1 1		1 1																				
works)																																							
Advance Work - Species Translocation																																							
Preparation and Construction works at Area 42																																							
Preparation and Construction works at Area 46																																							
Preparation and Construction of River Park and Visitor										-		П		т			П		П																				T
Centre									1 1					11			1 1		1 1																				
										$\neg \neg$				\top																									
Preparation and Construction works at Tung Chung River									1 1					11			1 1		1 1																				
														\Box																									
Preparation and Construction of River Park Footbridge									1 1					11			1 1		1 1																				
Attenuation & Treatment Ponds														т			П		П																				T
										-		П		т			П		П																				T
Preparation and Construction works of Yu Tung Road, Shun									1 1					11			1 1		1 1																				
Tung Road, Tat Tung Road and Cheung Tung Road									1 1					11			1 1		1 1																				
Preparation and Construction works of Improvement										-		П		т			П		П																				T
works for Chun Mun Road									1 1					11			1 1		1 1																				
Preparation and Construction for New Road L29										\Box				т			П		П																				T
												П		т			П		П																				T
Preparation and Construction works for New Road L30									1 1					11			1 1		1 1																				
Road Improvement works for Shek Mun Kap Road												П		т			П		П																				T
Woodland Compensation Works														\Box																									
									T																														
Pumping Station A (SPS-A) and Pumping Station B (SPS-B)																																							
Landscape Softworks																																							
Establishment works for Landscape Softworks																																							

Landscape related works Construction works except Landscape

C. Environmental Mitigation Implementation Schedule

(Relevant pages for the Project works in Tung Chung West, originally extracted from the Updated EM&A Manual, dated May 2018)

Note: Chapters 1 to 2 of the EIA report present the background information of the Project, identified concurrent projects, objectives and scope for various environmental aspects, and description on alternative options and construction description. Chapters 3 to 12 of the EIA report present the EIA findings and mitigation measures are described below with cross-reference to the EIA report. Chapters 13 to 15 describe the environmental monitoring requirements, summary of environmental outcomes and conclusion.

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
Common	Mitigation	Measures (Applicable to ALL Project Components, including D	Ps and Non-DPs)				
Construct	tion Dust In	npact					
S3.4.6	D1	Water spraying every hour on exposed worksites and haul road.	Minimize dust impact at the nearby sensitive receivers	Contractor	All construction sites	Construction stage	APCO To control the dust impact to meet HKAQO and TM-EIAO criteria
S3.4.6	D2	The contractor shall follow the procedures and requirements given in the Air Pollution Control (Construction Dust) Regulation	Minimize dust impact at the nearby sensitive receivers	Contractor	All construction sites	Construction stage	APCO To control the dust impact to meet HKAQO and TM-EIAO criteria
S3.4.6	D3	The following dust suppression measures should be incorporated to control the dust nuisance throughout the construction phase: • Any excavated or stockpile of dusty material should be covered entirely by impervious sheeting or sprayed with water to maintain the entire surface wet and then removed or backfilled or reinstated where practicable within 24 hours of the excavation or unloading; • Any dusty materials remaining after a stockpile is removed should be wetted with water and cleared from the surface of roads;	Minimize dust impact at the nearby sensitive receivers	Contractor	All construction sites	Construction stage	APCO To control the dust impact to meet HKAQO and TM-EIAO criteria

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
		• A stockpile of dusty material should not be extended beyond the pedestrian barriers, fencing or traffic cones;					
		• The load of dusty materials on a vehicle leaving a construction site should be covered entirely by impervious sheeting to ensure that the dusty materials do not leak from the vehicle;					
		 Where practicable, vehicle washing facilities with high pressure water jet should be provided at every discernible or designated vehicle exit point. The area where vehicle washing takes place and the road section between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores; 					
		 When there are open excavation and reinstatement works, hoarding of not less than 2.4m high should be provided as far as practicable along the site boundary with provision for public crossing. Good site practice shall also be adopted by the Contractor to ensure the conditions of the hoardings are properly maintained throughout the construction period; 					
		• The portion of any road leading only to construction site that is within 30m of a vehicle entrance or exit should be kept clear of dusty materials;					
		• Surfaces where any pneumatic or power-driven drilling, cutting, polishing or other mechanical breaking operation takes place should be sprayed with water or a dust suppression chemical continuously;					
		• Any area that involves demolition activities should be sprayed with water or a dust suppression chemical immediately prior to, during and immediately after the activities so as to maintain the entire surface wet;					
		• Where a scaffolding is erected around the perimeter of a building under construction, effective dust screens,					

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
		sheeting or netting should be provided to enclose the scaffolding from the ground floor level of the building, or a canopy should be provided from the first floor level up to the highest level of the scaffolding;					
		• Any skip hoist for material transport should be totally enclosed by impervious sheeting;					
		• Every stock of more than 20 bags of cement or dry pulverised fuel ash (PFA) should be covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides;					
		• Cement or dry PFA delivered in bulk should be stored in a closed silo fitted with an audible high level alarm which is interlocked with the material filling line and no overfilling is allowed;					
		• Loading, unloading, transfer, handling or storage of bulk cement or dry PFA should be carried out in a totally enclosed system or facility, and any vent or exhaust should be fitted with an effective fabric filter or equivalent air pollution control system; and					
		• Exposed earth should be properly treated by compaction, turfing, hydroseeding, vegetation planting or sealing with latex, vinyl, bitumen, shortcrete or other suitable surface stabiliser within six months after the last construction activity on the construction site or part of the construction site where the exposed earth lies.					
S3.4.6	D4	Implement regular dust monitoring under EM&A programme during the construction stage.	Monitoring of dust impact	Contractor	Selected dust monitoring stations	Construction stage	• TM-EIAO

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
Construc	ction Noise						
S4.3.4	N1	 Implement the following good site management practices: only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction programme; machines and plant (such as trucks, cranes) that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum; plant known to emit noise strongly in one direction, where possible, be orientated so that the noise is directed away from nearby NSRs; silencers or mufflers on construction equipment should be properly fitted and maintained during the construction works; mobile plant should be sited as far away from NSRs as possible and practicable; material stockpiles, site office and other structures should be effectively utilised, where practicable, to screen noise from on-site construction activities. 	Control construction airborne noise	Contractor	All construction sites where practicable	Construction stage	• Annex 5, TM-EIAO
S4.3.4	N2	Use of quiet plant which should be made reference to the Powered Mechanical Equipment (PME) listed in the Technical Memorandum or the Quality Powered Mechanical Equipment (QPME) / other commonly used PME listed in Environmental Protection Department (EPD) web pages as far as possible which includes the Sound Power Level (SWLs) for specific quiet PME.	Reduce the noise levels of plant items	Contractor	All construction sites where practicable	Construction stage	• Annex 5, TM-EIAO
S4.3.4	N3	Install movable temporary noise barriers (typical design is wooden framed barrier with a small-cantilevered upper portion of superficial density no less than 7kg/m² on a skid	Screen the noisy plant items to be used at all	Contractor	All construction sites where	Construction stage	• Annex 5, TM- EIAO

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
		footing with 25mm thick internal sound absorptive lining), and full enclosure, screen the noisy plants including air compressors, generators etc.	construction sites		practicable		
S4.3.4	N4	Implement a noise monitoring under EM&A programme.	Monitor the construction noise levels at the selected representative locations	Contractor	Selected noise monitoring stations	Construction stage	• TM-EIAO
Operation	onal Noise (I	Road Traffic Noise)					
S4.5.4	N5	Provide a series of noise mitigation measures including low noise surfacing material, noise barriers, facades with no openable window, school boundary walls and architectural fins before occupation of the protected NSRs. Locations of noise mitigation measures are stated as following: Year 2023: • Facade with no openable window at B1-1 and B1-2 for TCE; TCV-6 for TCW • 1.5m long architectural fin at B1-1 and B1-2 for TCE • Approx. 50m long, 4m high school boundary wall at possible school development near Tung Chung Area 39 • Approx. 120m long, 5m high vertical barrier with 3m cantilevered arm at 45° at the corner at junction between	Reduce operation noise from road traffic	Relevant government departments / Private developers	Refer to Figure 6.1, Figure 6.1a- b, Figure 6.2, Figures 6.2a-b, Figure 6.3, Figures 6.3a-d, Figure 6.4, and Figures 6.4a-e	While for mitigation measures to protect planned NSRs, it should be constructed before population intake	
		Chung Mun Road and Road L24 • Approx. 210m long LNRS along Chung Mun Road					
		Approx. 160m long LNRS along Road L24					
		Approx. 160m long LNRS along Road L30					
		Year 2025:					
		• Facade with no openable window at B1-1, B1-2, D1-1,					

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
		D1-2, D2-3 and D2-4 for TCE; TCV-6 for TCW					
		• 1.5m long architectural fin at B1-1, B1-2 and D2-4 for TCE; TCV-1 for TCW					
		• Approx. 60m long, 5m high school boundary wall along Road L3					
		• Approx. 70m long, 5m high school boundary wall with 3m cantilevered arm at 45° along Road L3					
		• Approx. 50m long, 4m high school boundary wall at possible school development near Tung Chung Area 39					
		• Approx. 120m long, 5m high vertical barrier with 3m cantilevered arm at 45° at the corner at junction between Chung Mun Road and Road L24					
		Approx. 210m long LNRS along Chung Mun Road					
		Approx. 160m long LNRS along Road L24					
		Approx. 160m long LNRS along Road L30					
		Year 2027:					
		• Facade with no openable window at A1-1, A1-2, A2-1, A2-2, A2-3, A2-4, B1-1, B1-2, D1-1, D1-2, D2-3 and D2-4 for TCE; TCV-6 for TCW					
		• 1.5m long architectural fin at A2-1, A2-4, B1-1, B1-2 and D2-4 for TCE;					
		• 1.8m long architectural fin at A1-1, A1-2, A2-1 and A2-4					
		• Approx. 60m long, 5m high school boundary wall along Road L3					
		• Approx. 70m long, 5m high school boundary wall with 3m cantilevered arm at 45° along Road L3					
		• Approx. 50m long, 4m high school boundary wall at					

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
		possible school development near Tung Chung Area 39					
		 Approx. 120m long, 5m high vertical barrier with 3m cantilevered arm at 45° at the corner at junction between Chung Mun Road and Road L24 					
		Approx. 210m long LNRS along Chung Mun Road					
		Approx. 160m long LNRS along Road L24					
		Approx. 160m long LNRS along Road L30					
		Year 2045:					
		• Facade with no openable window at A1-1, A1-2, A2-1, A2-2, A2-3, A2-4, B1-1, B1-2, C1-1, C2-1, C2-2, D1-1, D1-2, D2-3, D2-4, E1-4 and E1-5 for TCE; TCV-1 and TCV-6 for TCW					
		• 1.5m long architectural fin at A2-1, A2-4, B1-1, B1-2, C1-1 and D2-4 for TCE; TCV-1 for TCW					
		• 1.8m long architectural fin at A1-1, A1-2, A2-1, A2-4 and C1-1					
		• Approx. 100m long, 5m high absorptive vertical barrier along Road D3					
		• Approx. 50m long, 5m high absorptive vertical barrier with 3m cantilevered arm at 45° along Road L7					
		• Approx. 60m long, 5m high school boundary wall along Road L3					
		• Approx. 70m long, 5m high school boundary wall with 3m cantilevered arm at 45° along Road L3					
		• Approx. 80m long, 4m high school boundary wall along Road L2					
		• Approx. 40m long, 3m high school boundary wall along Road L2					

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
		Approx. 50m long, 4m high school boundary wall at possible school development near Tung Chung Area 39					
		• Approx. 120m long, 5m high vertical barrier with 3m cantilevered arm at 45° at the corner at junction between Chung Mun Road and Road L24					
		Approx. 210m long LNRS along Chung Mun Road					
		• Approx. 160m long LNRS along Road L24					
		• Approx. 160m long LNRS along Road L30					
Operation	nal Noise (I	Fixed Noise)					
S4.6.4	N6	For existing and planned NSRs which are located near to the proposed noise sources, the following tentative noise mitigation measures are considered:	Reduce operation fixed noise	government departments /	All plant rooms where practicable	Prior to operation of the Project	Ordinance and its TM, TM-
		• All the pumps should be enclosed inside building structures;		Future Operator			EIAO
		• Proper selection of quiet plant to reduce the tonality at NSRs;					
		• Installation of silencer / acoustic enclosure / acoustic louvers for the exhaust of ventilation system.					
		• For underground train stations, sound attenuators with sufficient attenuations can be installed to the ventilation shafts.					
		• Openings of ventilation system should be located away from NSRs.					
_	 nal Noise (1						

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
S4.8.4	N7	 Facade with no openable windows for residential block at B1-2 1.5m long architectural fin at B1-2 Before Phase 3 is occupied: It should be noted that Railway Stations at TCE and TCW and its associated railway system is a Designated Project under Item A.2 of Schedule 2 of TM-EIAO. Hence, the proposed mitigation measures are tentative for cumulative assessment purpose in this EIA and all the mitigation measures will be revised by the railway operator during their Schedule 2 EIA. Approx. 325m long, semi enclosure along the tracks of Tung Chung Line facing B0-2 and COM-1 Approx. 210m long, semi enclosure along the tracks of Tung Chung Line facing A1-2 and C1-1 Approx. 390m long, semi enclosure along the track of Tung Chung Line to Tung Chung direction facing C1-1 to C2-1 Approx. 630m long, semi enclosure along the track of Tung Chung Line to Hong Kong direction facing C1-1 and C2-1 		government	Refer to Figure 6.1, Figure 6.1a- b, Figure 6.2, Figures 6.2a-b, Figure 6.3, Figures 6.3a-d, Figure 6.4, and Figures 6.4a-e	population intake	• Noise Control Ordinance and its TM, TM-EIAO

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
Water Qu	uality (Const	ruction Phase)					
S5.4.3	W1	 General Construction Activities In accordance with the Practice Note for Professional Persons on Construction Site Drainage, Environmental Protection Department, 1994 (ProPECC PN1/94), best management practices should be implemented on site as far as practicable. The best practices are detailed below: At the start of site establishment, perimeter cut-off drains to direct off-site water around the site should be constructed with internal drainage works. Channels, earth bunds or sand bag barriers should be provided on site to direct stormwater to silt removal facilities.; Diversion of natural stormwater should be provided as far as possible. The design of temporary on-site drainage should prevent runoff going through site surface, construction machinery and equipment in order to avoid or minimize polluted runoff. Sedimentation tanks with sufficient capacity, constructed from pre-formed individual cells of approximately 6 to 8 m3 capacities, are recommended as a general mitigation measure which can be used for settling surface runoff prior to disposal. The system capacity shall be flexible and able to handle multiple inputs from a variety of sources and suited to applications where the influent is pumped; The dikes or embankments for flood protection should be implemented around the boundaries of earthwork areas. Temporary ditches should be provided to facilitate the runoff discharge into an appropriate watercourse, through a silt/sediment trap. The silt/sediment traps should be incorporated in the permanent drainage channels to enhance deposition rates; 	To minimize water quality impact from construction site runoff and general construction activities	Contractor	All construction sites where applicable	Construction stage	Water Pollution Control Ordinance ProPECC PN1/94 TM-EIAO TM-DSS
		• The design of efficient silt removal facilities should be					

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
		based on the guidelines in Appendix A1 of ProPECC PN 1/94. The detailed design of the sand/silt traps should be undertaken by the contractor prior to the commencement of construction;					
		Construction works should be programmed to minimize surface excavation works during the rainy seasons (April to September). All exposed earth areas should be completed and vegetated as soon as possible after earthworks have been completed. If excavation of soil cannot be avoided during the rainy season, or at any time of year when rainstorms are likely, exposed slope surfaces should be covered by tarpaulin or other means;					
		All drainage facilities and erosion and sediment control structures should be regularly inspected and maintained to ensure proper and efficient operation at all times and particularly following rainstorms. Deposited silt and grit should be removed regularly and disposed of by spreading evenly over stable, vegetated areas;					
		If the excavation of trenches in wet periods is necessary, it should be dug and backfilled in short sections wherever practicable. Water pumped out from trenches or foundation excavations should be discharged into storm drains via silt removal facilities;					
		All open stockpiles of construction materials (for example, aggregates, sand and fill material) should be covered with tarpaulin or similar fabric during rainstorms. Measures should be taken to prevent the washing away of construction materials, soil, silt or debris into any drainage system;					
		Manholes (including newly constructed ones) should always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris being washed into the drainage system and storm runoff being					

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
		directed into foul sewers;					
		Precautions to be taken at any time of year when rainstorms are likely, actions to be taken when a rainstorm is imminent or forecasted, and actions to be taken during or after rainstorms are summarized in Appendix A2 of ProPECC PN 1/94. Particular attention should be paid to the control of silty surface runoff during storm events;					
		• All vehicles and plant should be cleaned before leaving a construction site to ensure no earth, mud, debris and the like is deposited by them on roads. An adequately designed and sited wheel washing facilities should be provided at every construction site exit where practicable. Wash-water should have sand and silt settled out and removed at least on a weekly basis to ensure the continued efficiency of the process. The section of access road leading to, and exiting from, the wheel-wash bay to the public road should be paved with sufficient backfall toward the wheel-wash bay to prevent vehicle tracking of soil and silty water to public roads and drains;					
		Oil interceptors should be provided in the drainage system downstream of any oil/fuel pollution sources. The oil interceptors should be emptied and cleaned regularly to prevent the release of oil and grease into the storm water drainage system after accidental spillage. A bypass should be provided for the oil interceptors to prevent flushing during heavy rain;					
		Construction solid waste, debris and rubbish on site should be collected, handled and disposed of properly to avoid water quality impacts;					
		All fuel tanks and storage areas should be provided with locks and sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank to prevent spilled fuel oils from reaching water sensitive					

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
		 Regular environmental audit on the construction site should be carried out in order to prevent any malpractices. Notices should be posted at conspicuous locations to remind the workers not to discharge any sewage or wastewater into the water bodies, mangroves and open sea. 					
S5.4.3	W2	 Sewage from workforce Portable chemical toilets and sewage holding tanks are recommended for handling the construction sewage generated by the workforce. A licensed contractor should be employed to provide appropriate and adequate portable toilets and be responsible for appropriate disposal and maintenance; Notices should be posted at conspicuous locations to remind the workers not to discharge any sewage or wastewater into the nearby environment during the construction phase of the Project; Regular environmental audit on the construction site should be conducted in order to provide an effective control of any malpractices and achieve continual improvement of environmental performance on site. 	To minimize water quality from sewage effluent in construction phase	Contractor	All construction sites where practicable	Construction stage	Water Pollution Control Ordinance TM-DSS
S5.4.3	W3	Construction Works and Bridge Works near Tung Chung Stream Use precast structures or other similar approaches	To prevent any construction works in river and avoid any direct water quality impact to Tung Chung Stream	Contractor	All construction sites where practicable	Construction stage	• ProPECC PN1/94
S5.4.3	W4	Construction Works of Sewage Pumping Stations A buffer zone of about 20m or about 30m will be zoned to	To avoid any direct water quality impact to Tung Chung Stream		All construction sites where	Construction stage	• ProPECC PN1/94

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
		prevent any construction works near river.			practicable		
S5.4.3	W5	 Construction Work of Fresh Water and Salt Water Reservoirs Good site management as stipulated in ProPECC PN1/94 will be fully implemented to avoid polluted liquid or solid wastes from falling into the river waters or drainage. 	To avoid water quality impact	Contractor	All construction sites where practicable	Construction stage	• ProPECC PN1/94
\$5.4.3	W6	 Construction of Storm Water Management Facilities and Polder Scheme Good site management as stipulated in ProPECC PN1/94 will be fully implemented to avoid polluted liquid or solid wastes from falling into the river waters or drainage. 	To avoid any direct water quality impact to Tung Chung Stream		All construction sites where practicable	Construction stage	• ProPECC PN1/94
S5.4.3	W7	 Groundwater and Runoff for Tunnel Works Cut-and-Cover method for the underpass at Road D1 in Tung Chung East to minimise the intrusion of groundwater. Good site management as stipulated in ProPECC PN1/94 will be fully implemented to avoid polluted liquid or solid wastes from falling into the river waters or drainage. 	To avoid water quality impact	Contractor	All construction sites where practicable	Construction stage	• ProPECC PN1/94
\$5.5.8	W8	 Good Management Practice in Construction Phase The following good site management practices shall be adopted for the filling works: Water quality monitoring shall be implemented to ensure effective control of water pollution and recommend additional mitigation measures required; The decent speed of grabs shall be controlled to minimize the seabed impact and to reduce the volume of overdredging; A perimeter silt curtain shall be installed during the entire 	To avoid water quality impact	Contractor	All construction sites where practicable	Construction stage	• ProPECC PN1/94

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
		reclamation periods;					
		 Barges or hoppers shall not be filled to a level which will cause overflow of materials or pollution of water during loading or transportation; 					
		• Excess materials shall be cleaned from the decks and exposed fittings of barges before the vessels are moved;					
		• Plants should not be operated with leaking pipes and any pipe leakages shall be repaired quickly;					
		 Adequate freeboard shall be maintained on barges to reduce the likelihood of decks being washed by wave action; 					
		 All vessels should be sized so that adequate clearance is maintained between vessels and the seabed in all tide conditions, to ensure that undue turbidity is not generated by turbulence from vessel movement or propeller wash; and 					
		• The works shall not cause foam, oil, grease, litter or other objectionable matter to be present in the water within and adjacent to the works site.					
S5.5.8	W9	The recovered C&D materials for filling would be ensured no floating or non-inert material by visual inspection, quality assurance, etc.		Contractor	All construction sites where practicable	Construction stage	Waste Disposal Ordinance

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved		
Water Qu	ter Quality (Operational Phase)								
S5.6.10	W10	The following mitigation measures will be implemented to TCV East, North and West SPS, upgraded CMRSPS, proposed TCE West SPS and TCE East SPS • 100% standby pump capacity with spare pump of 50% pump capacity • Dual-feed power supply • Wet well storage providing up to 6-hours ADWF capacity (equivalent to about 4 hours of response time during peak flow condition); and • Emergency communication mechanism amongst relevant government departments.	To prevent the impact due to the emergency discharge at TCW and TCE		Proposed Sewage Pumping Station at TCW and TCE	Operational Stage	• DSD's Sewerage Manual		
S5.6.10	W11	 The following mitigation measures will be implemented to gravity sewers and rising mains Adopt high density polyethylene (HDPE) pipe for proposed gravity sewers and rising mains. Further protection on proposed rising mains with concrete surround will be provided to mitigate the risk of bursting. 	To minimize the risk of bursting and hence bursting discharge from gravity sewers and rising mains	DSD	Proposed rising mains within TCE and TCW	Operational Stage	-		
S5.6.10	W12	Maintenance Dredging for the Proposed Marina Silt curtain should be deployed to reduce the sediment dispersion from the dredging inside the marina.	To reduce the sediment dispersion	Future operator	Proposed marina at TCE	Operational Stage	-		

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
Sewage d	and Sewerag	e Treatment Implications					
S6.5.4	SS1	 Emergency Discharge of Proposed TCV West SPS, TCV East SPS, TCV North SPS and Upgraded CMRSPS The following mitigation measures will be implemented to TCV East, North and West SPS, and upgraded CMRSPS: 100% standby pumping capacity within each SPS, with spare pump up to 50% pumping capacity stockpiled in each SPS for any emergency use Twin rising mains Dual-feed power supply Emergency storage facilities up to 6-hours ADWF capacity; and Emergency communication mechanism amongst relevant government departments. 	To prevent the impact due to the emergency discharge at TCW	DSD	Proposed Sewage Pumping Station at TCW	Operational stage	N/A
S6.5.4	SS2	 Emergency Discharge of Proposed TCE West SPS and TCE East SPS In order to minimize the impact due to the emergency discharge, the following precautionary measures shall be included in the design of sewage pumping station: 100% standby pumping capacity within each SPS, with spare pump up to 50% pumping capacity stockpiled in each SPS for any emergency use Twin rising mains Dual-feed power supply Emergency storage facilities up to 6-hours ADWF capacity; and Emergency communication mechanism amongst relevant 	To minimize the impact due to the emergency discharge at TCE	DSD	Proposed Sewage Pumping Station at TCE	Operational stage	N/A

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
		government departments.					
S6.5.4	SS3	The following mitigation measures will be implemented to prevent pipe bursting on Rising Mains within TCE and TCW: • Strong pipe – use HDPE pipe with welded joints • Concrete encasement – concrete surround all rising mains	To minimize the risk of bursting and hence bursting discharge from gravity sewers and rising mains		Proposed rising mains within TCE and TCW		N/A

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
Waste M	anagement (Construction Waste)					
S7.4.1	WM1	Good Site Practices The following good site practices are recommended throughout the construction activities:	Minimize waste generation during construction	Contractor	All construction sites	Construction stage	Waste Disposal Ordinance
		 nomination of an approved personnel, such as a site manager, to be responsible for the implementation of good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site; 					
		training of site personnel in site cleanliness, appropriate waste management procedures and concepts of waste reduction, reuse and recycling;					
		 provision of sufficient waste disposal points and regular collection for disposal; 					
		• imposition of penalty system on Contractors' improper behaviours when illegal dumping and landfilling outside their respective construction sites, i.e. on nearby farmlands and riverbanks, are reported;					
		appropriate measures to minimise windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers;					
		regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors; and					
		• the contractor should prepare a Waste Management Plan (WMP) as part of the Environmental Management Plan (EMP) in accordance with the ETWB TC(W) No. 19/2005 for construction phase. The EMP should be submitted to the Engineer for approval. Mitigation measures proposed in the EIA Report and the EM&A Manual should be adopted.					

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
S7.4.1	WM2	 Waste Reduction Measures Waste reduction is best achieved at the planning and design phase, as well as by ensuring the implementation of good site practices. The following recommendations are proposed to achieve reduction: segregate and store different types of waste in different containers, skip or stockpiles to enhance reuse or recycling of materials and their proper disposal; proper storage and site practices to minimize the potential for damage and contamination of construction materials; plan and stock construction materials carefully to minimize amount of waste generated and avoid unnecessary generation of waste; sort out demolition debris and excavated materials from demolition works to recover reusable/recyclable portions (i.e. soil, broken concrete, metal etc.); provide training to workers on the importance of appropriate waste management procedures, including waste reduction, reuse and recycling. 	Reduce waste generation	Contractor	All construction sites	Construction stage	• Waste Disposal Ordinance
S7.4.1	WM3	 Storage of Waste The following recommendation should be implemented to minimize the impacts: waste such as soil should be handled and stored well to ensure secure containment; and Depends on actual site activities, certain locations within the site area would be used for storage of waste to enhance reuse. However, there would not be any designated location for storage of waste, and the storage locations would need to be adjusted to suite actual site conditions; 	Good site practice to minimize the waste generation and recycle the C&D materials as far as practicable so as to reduce the amount for final disposal		All construction sites	Construction stage	 Land (Miscellaneous Provisions) Ordinance Waste Disposal Ordinance ETWB TCW No. 19/2005

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
S7.4.1	WM4	Collection and Transportation of Waste The following recommendation should be implemented to minimize the impacts: • remove waste in timely manner; • employ the trucks with cover or enclosed containers for waste transportation; • obtain relevant waste disposal permits from the appropriate authorities; and • disposal of waste should be done at licensed waste disposal facilities.	Minimize waste impacts from storage	Contractor	All construction sites	Construction stage	Waste Disposal Ordinance
S7.4.1	WM5	 Excavated and C&D Materials Wherever practicable, C&D materials should be segregated from other wastes to avoid contamination and ensure acceptability at public fill reception facilities or reclamation sites. The following mitigation measures should be implemented in handling the excavated and C&D materials: maintain temporary stockpiles and reuse excavated fill material for backfilling; carry out on-site sorting; make provisions in the Contract documents to allow and promote the use of recycled aggregates where appropriate; and implement a trip-ticket system for each works contract to ensure that the disposal of C&D materials are properly documented and verified, so as to avoid the illegal dumping and landfilling of C&D materials on farmlands/ riverbanks at TCW; The recommended C&D materials handling should include: 	Minimize waste impacts from excavated and C&D materials	Contractor	All construction sites		 Land (Miscellaneous Provisions) Ordinance Waste Disposal Ordinance ETWB TCW No. 19/2005 Project Administrative Handbook for Civil Engineering Works, 2012 Edition

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
		On-site sorting of C&D materials					
		Reuse of C&D materials					
		Use of Standard Formwork and Planning of Construction Materials purchasing					
S7.4.1	WM6	Provision of Wheel Wash Facilities Wheel wash facilities have to be provided at the site entrance before the trucks leaving the works area. Dust disturbance due to the trucks transportation to the public road network could be minimized by such arrangement.	Minimize waste impacts from trucks transportation		All construction sites	Construction Stage	N/A
S7.4.1	WM7	Excavated Contaminated Soil As a precaution, it is recommended that standard good site practice should be implemented during the construction phase to minimize any potential exposure to contaminated soils or groundwater.	Remediate contaminated soil	Contractor	All construction sites where applicable	Construction stage	 Practice Guide for Investigation and Remediation of Contaminated Land
S7.4.1	WM8	 Excavated Marine Sediments Reference has been made to the sediment testing results. Possible mitigation measures to handle the contaminated/uncontaminated sediment are summarized as follows. All construction plant and equipment shall be designed and maintained to minimise the risk of silt, sediments, contaminants or other pollutants being released into the water column or deposited in the locations other than designated location. All vessels shall be sized such that adequate draft is maintained between vessels and the sea bed at all states of the tide to ensure that undue turbidity is not generated by turbulence from vessel movement or propeller wash. Adequate freeboard shall be maintained on barges to 	Handle excavated sediment	Contractor	All construction sites where applicable	Construction stage	• ETWB-TCW 34/2002

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
		ensure that decks are not washed by wave action.					
S7.4.1	WM9	 Dumping of excavated sediment Keep and produce logs and other records to demonstrate compliance and ensure journeys are consistent with designated locations Comply with the conditions in the dumping permit. All bottom dumping vessels (hopper barges) shall be fitted with tight fittings seals to their bottom openings to prevent leakage of material. The excavated sediment shall be placed into the disposal pit by bottom dumping. Contaminated marine mud shall be transported by split barge of not less than 750m³ capacity and capable of rapid opening and discharge at the disposal site. Discharge shall be undertaken rapidly and the hoppers shall be closed immediately. Sediment adhering to the sides of the hopper shall not be washed out of the hopper and the hopper shall remain closed until the barge returns to the disposal site. For Type 3 special disposal treatment, sealing of contaminant with geosynthetic containment before dropping into designated mud pit. A geosynthetic containment method is a method whereby the sediments are sealed in geosynthetic containers and, the containers would be dropped into the designated contaminated mud pit where they would be covered by further mud disposal and later by the mud pit capping at the disposal site, thereby fulfilling the requirements for fully confined mud disposal. 	Handle excavated sediment	Contractor	All construction sites where applicable		• ETWB-TCW 34/2002
S7.4.1	WM10	<u>Chemical Waste</u>	Control the chemical waste and ensure proper	Contractor	All construction	Construction stage	1

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
		If chemical wastes are produced at the construction site, the Contractors should register with EPD as chemical waste producer. Chemical wastes should be stored in appropriate containers and collected by a licensed chemical waste collector. Chemical wastes (e.g. spent lubricant oil) should be	storage, handling and disposal.		sites		(Chemical Waste) General) Regulation
		recycled at an appropriate facility as far as possible, while the chemical waste that cannot be recycled should be disposed of at either the Chemical Waste Treatment Centre, or another licensed facility, in accordance with the Waste Disposal (Chemical Waste) (General) Regulation.					Code of Practice on the Packaging, Labelling and Storage of Chemical Waste
S7.4.1	WM11	General Refuse General refuse should be stored in enclosed bins separately from construction and chemical wastes. Recycling bins should also be placed to encourage recycling.	Minimize production of the general refuse and avoid odour, pest and litter impacts		All construction sites	Construction stage	Waste Disposal Ordinance
		 Preferably enclosed and covered areas should be provided for general refuse collection and routine cleaning for these areas should also be implemented to keep areas clean. A reputable waste collector should be employed to remove general refuse on a daily basis. 					
S7.4.1	WM12	Floating Refuse accumulated along the seawall The floating refuse along seawall should be collected to avoid accumulation. In addition, proper seawall design should be employed, and regular checking and cleaning of floating refuse should be implemented.	Control floating refuse and ensure proper disposal	Contractor	Construction sites along seawall	Construction stage	Waste Disposal Ordinance
Waste Ma	anagement (Operational Waste)					
S7.4.2	WM13	Illegal dumping and landfilling	Prevent waste from	Relevant	All	Operational stage	

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
		As a Development Permission Area (DPA) plan will be issued by the Town Planning Board as a temporary measure before the formal Outline Zoning Plan (OZP) for Tung Chung New Town Extension is adopted, statutory right to guide and control the development and use of land would be authorised. Should there be illegal dumping and landfilling observed/ reported on nearby farmlands and riverbanks, the government authority should take all necessary actions including but not limited to prosecution to remediate the circumstances.	illegal dumping and landfilling	government departments	construction sites		
S7.4.2	WM14	 Municipal Solid Waste A reputable waste collector should be employed to remove general refuse on a daily basis. A 4-bin recycling system for paper, metals, plastics and glass should be adopted together with a general refuse bin. They should be placed in prominent places to promote waste separation at source. All recyclable materials should be collected by recyclers. 	Remove general refuse generated from the proposed development	FEHD/ Relevant Operators	All construction sites	Operational stage	Waste Disposal Ordinance
S7.4.2	WM15	 Chemical Waste Localized chemical waste storage areas should be located close to the source of waste generation for temporary storage. Drum-type containers with proper labelling should be used to collect chemical wastes for storage at the designated areas. A licensed collector should be employed for the chemical waste collection and the chemical wastes should be disposed at an appropriate facility, such as 	Reduce chemical waste due to waste handling	Contractors/ Relevant Operators	All construction sites	Operational stage	
		 Chemical Waste Treatment Centre (CWTC) in Tsing Yi. Collection receipts issued by the licensed collector showing the quantities and types of chemical waste taken off-site and details of the treatment facility should be kept for record. 					

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
S7.4.2	WM16	Floating Refuse accumulated along seawall The floating refuse along seawall should be collected to avoid accumulation.	Control floating refuse and ensure proper disposal		Along seawall	Operational stage	• Waste Disposal Ordinance
S7.4.2	WM17	Floating Refuse inside Marina • Floating refuse at the marina will be collected and disposed by the licensed waste collector and as required.	Reduce floating refuse washing up onto marina by currents and wind	_	Marina	Operational stage	• Waste Disposal Ordinance

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
Land Con	tamination						
S8.4.1	LC1	Undertaking environmental Site Inspection (SI) for all potentially contaminated sites as listed in the Contamination Assessment Plan (CAP).	contamination potential before the		All potentially contaminate d sites as listed in the CAP	construction stage	 Annex 19 of the TM-EIAO, Guidelines for Assessment of Impact On Sites of Cultural Heritage and Other Impacts (Section 3: Potential Contaminated Land Issues); Guidance Manual for Use of Risk-Based Remediation Goals (RBRGs) for Contaminated Land Management; Guidance Notes for Contaminated Land Assessment and Remediation; and Practice Guide for Investigation and Remediation of Contaminated Land

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
							• Recommendation s in Health Risk Assessment
S8.4.2	LC2	Re-appraisal would be required for the surveyed sites, other remaining areas of the PDAs and the works areas for the associated infrastructures because the development of these sites/ areas would only commence a number of years later, which may allow changes in the land usage of these sites and may give rise to potential land contamination issues. The Project Proponent's appointed consultant would prepare a supplementary CAP presenting the findings of the reappraisal and strategy of the recommended SI, if required, and submit to EPD for review and approval.	To assess the latest site situation and identify any potential additional hot spots and contaminated sites.	Detailed Design	All the surveyed sites as listed in the CAP, other remaining areas of the PDAs and works areas for the associated infrastructur es	Prior to the construction stage	Ditto
S8.5	LC3	After approval of the supplementary CAP and upon completion of the SI works, the PP should prepare and submit a Contamination Assessment Report (CAR) for all potentially contaminated sites listed in the CAP to EPD for agreement.	Present the findings of SI and evaluate the level and extent of potential contamination	Detailed Design	All the surveyed sites as listed in the CAP, other remaining areas of the PDAs and works areas for the associated infrastructures	Prior to the construction stage	Ditto
S.8.5	LC4	Preparation and submission of Remediation Action Plan (RAP) to EPD for agreement if land contamination is confirmed.	Recommend appropriate mitigation measures for the contaminated soil and groundwater identified in the	Detailed Design Consultant /	All the surveyed sites as listed in the CAP, other remaining	Prior to the construction stage	Ditto

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
			assessment if remediation is required		areas of the PDAs and works areas for the associated infrastructu res		
S.8.5	LC5	Preparation and submission of Remediation Report (RR) to EPD for agreement.	Demonstrate that the decontamination work is adequate and is carried out in accordance with the endorsed CAR and RAP	Detailed Design Consultant / Private developer	All the surveyed sites as listed in the CAP, other remaining areas of the PDAs and works areas for the associated infrastructures	Prior to the construction stage	Ditto

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
Ecology	(Design Ph	ase)			•		
S9.8.1	EC1	Development under the Project have avoided all the recognised sites of conservation importance, including Country Parks,		PlanD	TCW	RODP	Not available
S9.8.1	EC2	About 30m buffer zone at the two main branches and the joined outlet section of Tung Chung Stream; and about 20m buffer for the major tributary at Ngau Au of Tung Chung Stream	To protect the Tung Chung Stream	PlanD	Tung Chung Stream	RODP	Not available
S9.8.2	EC3	Detailed designs should avoid the encroachment of important habitats (e.g. Fung Shui Wood) within the Project Site		PlanD	TCW	Design Phase	Not available
S9.8.2	EC4	Detailed designs of noise barriers to prevent bird collision	To prevent bird collision	HyD	Noise barriers	Design Phase	Guidelines on Design of Noise Barriers
S9.8.2	EC5	Measures and suitable designs of sewage pumping stations to prevent emergency discharge accidents in TCE and TCW 100% standby pumping capacity within each SPS, with spare pump up to 50% pumping capacity stockpiled in each SPS for any emergency use Twin rising mains Dual-feed power supply Emergency storage facilities up to 6-hours ADWF capacity; and Emergency communication mechanism amongst relevant government departments.	bodies from impacts due to emergency discharge in TCE and TCW	DSD	Proposed and Upgraded Sewage pumping stations at TCE and TCW	Design Phase	• DSD standards

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
Ecology	(Constructio	on Phase)					
S9.8.2	EC6	Adoption of non-dredged reclamation method	To maintain the marine water quality	Contractor	Reclamation area of TCE and Road P1	Construction phase	• EIA • Contractual requirements
S9.8.3	EC7	Compensation woodland planting	To compensate loss of woodland, fung shui wood and orchard	Contractor	Uphill of Sheung Lei Pai FSW and Tung Chung Road		EIA Contractual requirements
S9.8.3	EC8	Planting of emergent plant	To provide habitats for this Jhora Scrub Hopper, and to compensate the loss of their habitats (wet abandoned agricultural land) in northern section of Fong Yuen		Inside the future River Park	Construction phase	EIA Contractual requirements
S9.8.3	EC9	Capture-and-translocation exercise	Minimize the potential impact to amphibian species of conservation importance including Romer's Tree Frog and Chinese Bullfrog due to site formation	For public works, provided by the government departments responsible for the construction of those public works or the site formation works. For TCV-1 and	the eastern branch of Tung Chung Stream, in particular 1)	Capture-and- translocation exercise before commencement of site formation	

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
				TCV-5, where the lands within mostly belong to private lots, the future project proponents of those private lots, via the established mechanism for land transaction application.	branch of Tung Chung Stream, 3) the road		
S9.8.3	EC10	Preservation and/or Transplantation of plant species of conservation importance and the following monitoring of preserved/transplanted plant individuals	Protection of plant species of conservation importance	For public works, provided by the government departments responsible for the construction of those public works or the site formation works.	Within construction sites All areas for public works Also be required in private lands	before commencement of site formation.	Contractual requirements

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
				For TCV-1, where the lands within mostly belong to private lots, the future project proponents of those private lots, via the established mechanism for land transaction application.	in TCV-1.		
S9.8.3	EC11	Defining and maintaining construction site boundaries (including erection of site hoarding, fences etc.)	Screen construction disturbance to the nearby habitats	Contractor	Along the boundary of construction sites and buffer zones of Tung Chung Streams, along the boundary of mature woodland and Fung Shui Wood, and along the boundary between TCV-6 and the middle section of Fong Yuen	commencement of site formation	• EIA • Contractual requirements
S9.8.3	EC12	Protection of Tung Chung Stream	Minimize the potential water pollution due to	Contractor	Within construction	Construction	• EIA

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
			construction of road crossings or other works near Tung Chung Stream		sites	phase	Contractual requirements
S9.8.3	EC13	Implementation of standard site practices	Minimize the potential impact due to dust, noise and runoff during construction phase	Contractor	Within construction sites	Construction phase	• EIA • Contractual requirements
S9.8.4	EC14	Adopting Eco-shoreline design	To mitigate the impact of the marine loss	CEDD	Along future seawall	Construction stage	• EIA • Contractual requirements
S9.8.4	EC15	Strict enforcement on no-dumping	Minimise the potential impact to marine habitats	Contractor	In reclamation area as well as all works area and travel route of works vessels	Before and during construction phase	EIA Contractual requirements
S9.8.4	EC16	Spill response plan	Minimise the potential impact to marine habitats	Contractor	In reclamation area as well as all works area and travel route of works vessels	Before and during construction phase	EIA Contractual requirements
S.9.8.4	EC17	Control and minimization of marine traffic by including using larger-sized barges, land transportation of materials, reuse of excavation and C&D materials and speed limits &	Reduce marine traffic	Contractor	In reclamation area as well	Construction phase	• EIA • Contractual

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
		regular routes of works vessels			as all works area and travel route of works vessels		requirements
S9.8.4	EC18	Dolphin exclusion zone and dolphin watching plan	Protection of CWD	Contractor	In reclamation area as well as all works area	Construction phase	EIA Contractual requirements
S9.8.4	EC19	Speed limits and regular routes of works vessels; Prepare and submit a "Works Vessel Travel Route Plan"	Protection of CWD	Contractor	In reclamation area as well as all works area	Construction phase	EIA Contractual requirements
S9.11.1	EC20	Monitoring of compensatory planting woodland	Monitor the survival of trees and establishment of the woodland	CEDD/ Contractor	Areas of compensator y woodland planting	Quarterly for 3 years after completion of planting works	• EIA • Contractual requirements
S9.11.1	EC21	Monitoring of translocated amphibians	Monitor the effectiveness of the translocation programme	Public works: Responsible government departments / Contractor Private lots: Private developers	Release sites for translocated amphibians	After translocation exercise. At least three surveys in each release site during the breeding season, preferably monthly between April and June,	 EIA Contractual requirements Explanatory statement of the OZP (for private lots)
S9.11.1	EC22	Monitoring of preserved / transplanted plant species	Monitor and evaluate	Public works:	Construction	After	• EIA

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
			the effectiveness of the preservation and transplantation programme.	Responsible government departments / Contractor Private lots: Private developers	sites for preserved plants; recipient sites for transplanted plants	transplantation or preservation. For transplanted individuals, for two years, monthly for the first year, and then quarterly for the second year. For the preserved individuals, monthly throughout the construction.	requirements
S9.11.1	EC23	Monitoring of Tung Chung Stream and Wong Lung Hang Stream EISs	Protect the EISs	Contractor	Tung Chung Stream and Wong Lung Hang Stream	phase and post-	• EIA • Contractual requirements
9.11.2	EC24	Monitoring of Tung Chung Bay and Tai Ho Wan	Protect Tung Chung Bay and Tai Ho Wan	Contractor	Tung Chung Bay and Tai Ho Wan	nhase and nost-	• EIA • Contractual requirements
Ecology (Operationa	l Phase)					
S9.11.1	EC25	Monitoring of emergent plant inside River Park	Monitor the survival of emergent plant	DSD/ Contractor	Three months after completion of planting in future River Park	Quarterly for 2 years after completion of planting works	EIAContractual requirements

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures		Implementation Agent		Implementation Stage	Requirements and / or standards to be achieved
9.11.2	EC26	Eco-shoreline monitoring	Monitor the colonisation and establishment of fauna and/or flora, water quality, and recruitments of fisheries species	CEDD/ Contractor	Eco- shoreline at TCE PDA reclamation	nhase twice in	EIAContractual requirements

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location	Implementation Stage	Requirements and / or standards to be achieved
Fisheries	1						
S10.8	F1	Good Site Practices	To protect the fisheries resources	Contractor	In reclamation area	Construction phase	EIAContractual requirements
S10.8	F2	No dumping	To protect the fisheries resources	Contractor	In reclamation area	Construction phase	EIAContractual requirements
S10.8	F3	Spill response plan	To protect the fisheries resources	Contractor	In reclamation area	Construction phase	EIAContractual requirements
S10.9	F4	Follow the mitigation measures proposed in the water quality assessment for the construction and operation phases of the project.	To protect the fisheries resources	Contractor	Waters in Northern Lantau	Construction phase and operation phase	• EIA • Contractual requirements
S10.9	F5	Follow the mitigation measure of eco-shoreline in ecology chapter for the construction and operation phases of the project.	To enhance the fisheries resources	Contractor	Eco- shorelines	Construction phase and operation phase	EIAContractual requirements

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementati on Agent	Location	Implementation Stage	Requirements and / or standards to be achieved
Landscap	pe and Visua	el (Construction Phase)					
S11.7 MM1	LV1	Optimisation of Construction Areas & Providing Temporary Landscape on Temporary Construction – Construction areas' control shall be enforced, where possible, to ensure that the landscape and visual impacts arising from the construction activities are minimised. It includes reduction of the extent of working areas and temporary works areas, management on storing and using the construction equipment and materials, and consideration of detailed schedules to shorten the construction period. Temporary landscape treatments are considered to be adopted such as applying hydro-seeding on temporary stockpiles and reclamation areas to alleviate the potential impacts.	Minimise the landscape and visual impacts arising from the construction activities	Relevant Government Departments / Private Sector	Through-out Tung Chung West (TCW) area and Tung Chung East (TCE) area	Construction Phase	
S11.7 MM2	LV2	Minimize Topographical Change – The footprint of construction elements and temporary works areas should be optimised to reduce topographical/ landform changes, as well as reduce land take and interference with natural terrain. Where there is a need to significantly cut into the existing landform, retaining walls and cut slopes should be considered as appropriate. To minimize landform changes and land resumption, earthworks and engineered slopes should be designed to be a visually interesting, compatible with the surrounding landscape and to mimic the natural contouring and terrain as appropriate.	Reduce topographical changes and minimize land resumption	Relevant Government Departments / Private Sector	Through-out TCW area	Prior to Construction & Construction Phase	• GEO Publication No/1/2011, Technical Guidelines on Landscape Treatment for Slopes
S11.7 MM3	LV3	Preservation of Potentially Registerable OVTs, Rare and Protective Vegetation – Exiting trees to be retained within the Project Site should be carefully protected during construction. In particular Potentially Registerable OVTs are considered to be preserved according to ETWB	Protect and Preserve Trees	Relevant Government Departments / Private Sector	Onsite, particularly for TCW area	Prior to Construction & Construction Phase	• ETWB TC(W) No.29/2004 and DEVB TC(W)

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementati on Agent	Location	Implementation Stage	Requirements and / or standards to be achieved
		Technical Circular (Works) No. 29/2004. Rare and Protective Vegetation shall be protected following Forestry Regulations (Cap.96) and Protection of Endangered Species of Animals and Plants Ordinance (Cap.586). Detailed Tree Protection Specification shall be provided in the Contract Specification according to DEVB TCW No. 10/2013 Tree Preservation. Following DEVB (GLTM) Guidelines for Tree Preservation during Development, the Contractor shall be required to submit, for approval, a detailed working method statement for the protection of trees prior to undertaking any works adjacent to all retained trees, including trees in contractor's works areas. A detailed tree survey will be carried out for the Tree Removal Application (TRA) process which will be carried out at the later detailed design stage of the Project. The detailed tree survey will propose which trees should be retained, transplanted or felled and will include details of tree protection measures for those trees to be retained.					No.10/2013. • Greening, Landscape and Tree Management Section (GLTM) of the Development Bureau, Guidelines on Tree Preservation during Development (April, 2015)
S11.7 MM4	LV4	Transplanting of Existing Trees – Trees unavoidably affected by the Project works should be transplanted where practical. Trees should be transplanted straight to their final receptor locations within the site and not held in a temporary nursery as far as possible. A detailed Tree Transplanting Specification shall be provided in the Contract Specification, where applicable. Sufficient time for necessary tree root and crown preparation periods shall be allowed in the project programme. A detailed transplanting proposal will be submitted to relevant government departments for approval in accordance with DEVB TCW 10/2013 and LAO PN 7/2007 and final locations of transplanted trees should be agreed prior to commencement of the work. For trees associated with highways e.g. roadside planting	Transplant Trees where suitable for transplantation	Relevant Government Departments / Private Sector	Onsite where possible, otherwise consider offsite locations	Prior to Construction & Construction Phase	 DEVB TC(W) No.10/2013 and LAO PN7/2007 HyD HQ/GN/13 Interim Guidelines for Tree Transplanting Works under Highways Department's Vegetation Maintenance

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementati on Agent	Location	Implementation Stage	Requirements and / or standards to be achieved
		along highways, that are unavoidably affected and should be transplanted. HyD HQ/GN/13 'Interim Guidelines for Tree Transplanting Works under Highways Department's Vegetation Maintenance Ambit' should be referred to.					Ambit GLTM of the Development Bureau, Guidelines on Tree Preservation during Development (April, 2015)
S11.7 MM5	LV5	Screen hoarding – To reduce negative visual impact, construction site hoarding should be erected around the site to screen pedestrian level views into the construction area from visual sensitive receivers. Hoarding design should consider greening measures such as colour and form should be adopted to improve its visual appearance.	To screen undesirable views of the work site.	Relevant Government Departments / Private Sector	Through-out TCW and TCE areas	Construction Phase	
S11.7 MM6	LV6	Adopting Non-dredge Method for the Reclamation — In order to minimize the potential adverse impacts caused by the reclamation, a number of alternative construction methodologies has been critically examined. After considering all the options such as fully dredged, partially dredged and non-dredged methods for seawall construction and reclamation, non-dredged method for both the seawall construction and reclamation are recommended so as to minimize the generation of dredged sediment.	Minimize the potential adverse impacts caused by the reclamation	Relevant Government Departments / Private Sector	Through-out TCE area	Construction Phase	• Foreshore and Sea-bed (Reclamations) Ordinance (Cap.127)
S11.7 MM7	LV7	Protection of Natural Rivers and Streams – For all the natural rivers and streams inside the development area, in accordance with ETWB TCW 5/2005, consideration of protection measures should be made to minimize any impacts from the construction works, especially those	Protection of Natural Rivers and Streams Minimize the impacts from the construction works	Relevant Government Departments / Private Sector	Through-out TCW area	Prior to Construction & Construction Phase	 EPD ProPECC PN1/94 Construction Site Drainage. DSD Technical

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementati on Agent	Location	Implementation Stage	Requirements and / or standards to be achieved
		development near Tung Chung Stream. According to the latest RODP, a 30m buffer zone will be zoned as "CA". Precast structures or other similar approaches will be used to prevent / minimise any construction works in river and thus to avoid any direct water quality impact. Good site management as stipulated in ProPECC PN1/94 will be fully implemented to avoid polluted liquid or solid wastes from falling into the river waters.					Circular No. 2/2004. • ETWB TC(W) No.5/2005 Protection of natural streams/rivers from adverse impacts arising from construction works
S11.7 MM8	LV8	Preservation of Natural Coastline – The natural coastline along the proposed "RO" of the RODP in TCW should be preserved. The remaining natural shorelines in Tung Chung Bay including sandy shores close to the Tung Chung old pier will be conserved as a Waterfront Park according to the latest RODP.	Preservation of Natural Coastline	Relevant Government Departments	Onsite where possible	Prior to Construction & Construction Phase	
S11.7 MM9	LV9	Providing Natural Rock Material/ Planting for Artificial Seawall – There would be inevitable permanent losses of marine waters (seabed and water column), and direct impacts on existing artificial seawalls due to the reclamation. To minimize the impacts, the design of the future seawall like 'eco-shoreline' could be improved to provide high ecological functions and mitigate the impact of the loss. An 'eco-shoreline' is any shoreline which provides beneficial functions to the local ecosystem through a range of active or passive solutions, whilst providing coastal protection. By means of using natural rock materials for artificial seawall and considering to introduce a native vegetation buffer directly behind the top of seawalls as appropriate to create habitat, shelter and a source of food	Mitigate the impacts on existing artificial seawalls	Relevant Government Departments	Onsite where possible	Prior to Construction & Construction Phase	

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementati on Agent	Location	Implementation Stage	Requirements and / or standards to be achieved
		for benefiting both terrestrial and aquatic species along the foreshore, these measures can help to enhance the ecological functions and 'natural-look' of the shoreline, and the potential impacts will be mitigated.					
Landscap	e and Visua	el (Operational Phase)					
S11.7 MM10	LV10	Compensatory Planting – Compensatory planting for felled trees shall be provided to the satisfaction of relevant Government departments. Required numbers and locations of compensatory trees shall be determined and agreed separately with Government during the Tree Removal Application process under DEVB TCW No. 10/2013 and LAO PN 7/2007. The location of compensatory planting is proposed at the potential open areas such as open spaces, amenity areas, open areas of the streetscapes including roadside planting, as well as the open areas within development lots. The species to be planted should be all native species,	Compensate for trees and shrubs lost due to the Project	Relevant Government Departments / Private Sector	Onsite where possible, particular-ly for TCW area	Prior to Construction, Construction Phase & Maintenance in Operation Phase	 DEVB TC(W) No.10/2013 and LAO PN 7/2007. GLTM of the Development Bureau, Guidelines on Tree Preservation during Development (April, 2015)
		taken "Characteristics of Major Local Tree Species Propagated by AFCD" as a reference. A search of species to be planted will be conducted in a further detailed stage.					(April, 2013)
S11.7 MM11	LV11	Woodland Restoration – A search of area to mitigate the loss of woodland has been conducted. Priority has been given to the practicability of compensation of woodland within the boundary of RODP. Given the nature of the project is to provide development opportunities to satisfy the needs for the society in general and the aspirations of local communities, compensation of woodland is only possible for the areas beyond the RODP. It is considered that the areas adjoining the woodlands near the existing services reservoirs, and hillsides to the east of Tung Chung Road, would be suitable locations. The advantage of these locations is that there are existing woodlands immediately	Reprovide areas of woodland to compensate for those areas of quality woodland lost	CEDD/AFCD	In areas identified and as agreed with AFCD	Prior to Construction, Construction Phase & Maintenance in Operation Phase	 DEVB Technical Circular Works 10/2013- Tree Preservation GLTM of the Development Bureau, Guidelines on Tree Preservation

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementati on Agent	Location	Implementation Stage	Requirements and / or standards to be achieved
		downhill to the location and the Sheung Ling Pei Fung Shui Wood is further downhill behind Sheung Ling Pei Village, planting new woodland areas adjoining existing woodlands would form an ecological linkage and increase the overall habitat size, and hence would help to enhance the ecological and landscape values in the long run.					during Development (April, 2015)
		It is noted that the compensation trees for landscape impacts will also be planted near the future service reservoirs. The tree species to be planted should be all native species for woodland compensation, and the two areas uphill to Sheung Ling Pei should also make reference to the existing tree species reported in Fung Shui Woods habitat.					
S11.7 MM12	LV12	Screen Planting – Tall screen/buffer trees and shrubs should be planted to screen proposed structures such as roads and buildings. This measure will form part of the compensatory planting and will improve compatibility with the surrounding environment and create a pleasant pedestrian environment.	To screen proposed structures Improve compatibility with the surrounding environment	Relevant Government Departments	Through-out the working sites of the TCW and TCE areas	Prior to Construction, Construction Phase & Maintenance in Operation Phase	• HyD HQ/GN/15— Guidelines for Greening Works along Highways.
S11.7 MM13	LV13	Roadside Planting – Roadside greening is proposed alongside all roads within the possible developments. It will enhance local identity, if theme planting is used, and reduce visual impact through screening. At-grade road planting should be considered along central dividers and on road islands e.g. in the middle of roundabouts.	Soften the hard, straight edges and provide greening along the roads; Improve the visual amenity	Relevant Government Departments	Along new roads, and On appropriate viaducts	Prior to Construction, Construction Phase & Maintenance in Operation Phase	 HyD HQ/GN/15- Guidelines for Greening Works along Highways. Development Bureau Technical Circular Works No.2/2012 - Allocation of Space for Quality

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementati on Agent	Location	Implementation Stage	Requirements and / or standards to be achieved
							Greening on Roads

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementati on Agent	Location	Implementation Stage	Requirements and / or standards to be achieved
S11.7 MM14	LV14	Aesthetic Design of Built Development – The planning of the revised RODP has considered reducing potential visual impacts, enhancing visual amenity and keeping visual corridors. The proposed development will ensure the building massing is compatible with its surroundings. To improve visual amenity, natural building materials could be used on building facades. For example, stone and timber should be considered for architectural features; light earthy tone colours such as shades of green, shades of grey, shades of brown and off-white should be considered for the façade treatment to reduce the visibility of the development components. The form, textures, finishes and colours of the proposed development components should aim to be compatible with the existing surroundings. It would only be implemented for public developments/projects.	Improve visual amenity of the new buildings, keep visual corridors and integrate as possible into the surrounding landscape	Relevant Government Departments	Through-out the TCW and TCE areas	Prior to Construction, Maintenance in Operation Phase	 Hong Kong Planning Standards and Guidelines (HKPSG) issued by the Planning Department (As at Aug 2011); PNAP APP-152, Sustainable Building Design Guidelines
S11.7 MM15	LV15	Maximise Greening on Structures – The Government has been actively promoting greening in buildings and structures such as bridges to improve the environment. This includes actively implementing rooftop greening or vertical greening, as where practicable to enhance the cityscape and mitigate the heat island effect in urban areas. For the new built forms in TCW and TCE, it is considered the implementation of the following greening measures could alleviate the landscape and visual impacts of new development and help the development blend in with its surrounding landscape: • Sky Garden: Refuge floors or voids in building mass formed by partial removal of floor plates on certain building storeys or provision of freed up areas on certain building storeys provide opportunities for sky	Maximise Greening coverage Enhance visual amenity, create visual corridors and integrate as possible into the surrounding landscape	Relevant Government Departments	On appropriate buildings and structures	Prior to Construction, Construction Phase & Maintenance in Operation Phase	Development Bureau Technical Circular (Works) No. 3/2012 Site Coverage of Greenery for Government Building Projects PNAP APP- 152, Sustainable Building
		gardens for the proposed built development. It can allow views through the development to the background formed by the natural hillsides and					Design Guidelines

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementati on Agent	Location	Implementation Stage	Requirements and / or standards to be achieved
		enhance the visual amenity effectively. For public developments, relevant technical document Technical Circular (Works) No. 3/2012 Site Coverage of Greenery for Government Building Projects by Development Bureau in 2011 shall be referred to. For private developments, it is only applicable to sites with inadequate greening coverage and should be implemented in accordance with Sustainable Building Design Guidelines PNAP APP-152.					
		• Green Roof: The Architectural Services Department completed the Study on Green Roof Application in Hong Kong in 2007 which reviewed the latest concepts and design technology of green roof and recommended technical guidelines suitable for application in Hong Kong. The study will be taken into account to the new buildings to be built in TCW and TCE. Landscape and visual impact can be alleviated and the landscape and visual value can be enhanced. For private development, it is only applicable to sites with inadequate greening coverage and should be implemented in accordance with Sustainable Building Design Guidelines PNAP APP-152. Relevant technical document Technical Circular (Works) No. 3/2012 Site Coverage of Greenery for Government Building Projects by Development Bureau in 2011 shall be reference. For public developments, relevant technical document Technical Circular (Works) No. 3/2012 Site Coverage of Greenery for Government Building Projects by Development Bureau in 2011 shall be referred to. For private developments, it is only applicable to sites with inadequate greening coverage and should be implemented in accordance with Sustainable Building Design Guidelines PNAP APP-152.					
		Vertical Green: Planting of climbers to grow up					

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementati on Agent	Location	Implementation Stage	Requirements and / or standards to be achieved
		vertical surfaces where appropriate (e.g. building edges), to soften hard structures and facilities. Relevant technical document Technical Circular (Works) No. 3/2012 Site Coverage of Greenery for Government Building Projects by Development Bureau in 2011 shall be observed. For public developments, relevant technical document Technical Circular (Works) No. 3/2012 Site Coverage of Greenery for Government Building Projects by Development Bureau in 2011 shall be reference. For private development, it is only applicable to sites with inadequate greening coverage and should be implemented in accordance with Sustainable Building Design Guidelines PNAP APP-152. • Greening on infrastructure: Planting could be provided on infrastructure such as bridges where appropriate to enhance greenery to soften its built edges. Screen planting could be provided near infrastructure to reduce any undesirable visual impacts.					
S11.7 MM16	LV16	Noise barrier design — The visual impact of noise mitigation measures will be mitigated by appropriate detailed design, including suitable combination of transparent and sound absorbent materials, appropriate colour selection of panels and supporting structures, or provision of at-grade planting of trees, shrubs and/or climbers camouflage to the barriers, as well as design of supporting structures to incorporate a high level of quality and aesthetics. A combination of transparent panels at top and solid panels at bottom would lighten the visual impact, and at the same time maintain the attractiveness by using colourful panels. The noise barriers would be implemented for District Distributor Roads and Local Distributor Roads at both TCE and TCW area.	Minimize the visual impact from the structures of noise barriers	HyD	Noise barriers within the TCW and TCE areas	Prior to Construction, Construction Phase & Maintenance in Operation Phase	 GLTM of the Development Bureau's Guidelines on Greening of Noise Barriers (April 2012). Guidelines on Design of Noise Barriers by HyD and EPD in 2003

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementati on Agent	Location	Implementation Stage	Requirements and / or standards to be achieved
S11.7 MM17	LV17	Landscape Treatment for Polders & Attenuation Ponds – There would be polders and attenuation ponds in TCW. While they are primarily used for receiving and treating surface runoff and alleviating the flood risk during heavy rainfall, the design of those has provided an opportunity to have a synergy to enhance both the ecological and landscape values together. Depending on detailed design, part of these attenuation	Enhance the landscape and visual value	DSD	Polders & Attenuation Ponds where possible	Prior to Construction, Construction Phase & Maintenance in Operation Phase	
		ponds (mainly the biofiltration zone) could be refined in an appropriate manner, without compromising its primary functions of treating surface runoff and flood protection, to incorporate ecological and landscape design such as planting of aquatic plants and butterfly foodplant for providing the landscape and ecological enhancement.					
Landscape	e and Visua	l (Construction & Operational Phase)					
S11.7 MM18	LV18	Landscaping on Slopes – Hydro seeding of modified slopes should be done as soon as grading works are completed to prevent erosion and subsequent loss of landscape resources and character. Woodland tree seedlings and/ or shrubs should be planted where gradient and site conditions allow. In addition, landscape planting should be provided for the retaining structures associated with modified slopes where condition allow.	Enhance landscape value, plant diversity and their visual appearance	CEDD	Onsite, particularly in TCW area	Prior to Construction, Construction Phase & Maintenance in Operation Phase	• GEO Publication No.1/2011 Technical Guidelines on Landscape Treatment for Slopes by CEDD in 2011
S11.7 MM19	LV19	Landscape Treatment on Channelized Watercourses – For the channelized watercourses in Tung Chung Stream that will be dechannelized, the Drainage Services Department Practice Note No.1/2005 – Guidelines on Environmental Considerations for River Channel Design, should be considered and appropriate measures included ensuring the new watercourses match the existing as far as possible.	Avoid direct impacts on the watercourse Improve the visual amenity	CEDD	The channelized watercourses throughout the TCW area	Prior to Construction, Construction Phase & Maintenance in Operation Phase	• Drainage Services Department Practice Note No.1/2005 — Guidelines on Environmental

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementati on Agent	Location	Implementation Stage	Requirements and / or standards to be achieved
		Measures can include enhancement planting to upgrade the channels as appropriate, including consideration of wetland planting along embankments where appropriate; as well as consideration of the best materials for the channel lining (e.g. gabion).					Considerations for River Channel Design
S11.7 MM20	LV20	Light Control – Construction day and night time lighting should be controlled to minimize glare impact to adjacent VSRs during the construction stage. Street and night time lighting shall also be controlled to minimize glare impact to adjacent VSRs during the operation phase.	Minimize negative glare impact to adjacent VSRs	Relevant Government Departments / Private Sector	Through-out the TCW and TCE areas	Construction Phase & Operation Phase	

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
Cultural 1	Heritage Im	pact (Construction and Operational Phase)					
S.12.5	СН1	Terrestrial Archaeology • Implement rescue excavations/ survey-cum-rescue excavations/ further surveys after land resumption and prior to any construction works (see Figure 14.1 for the locations of rescue excavations/survey-cum-rescue excavations/further survey)	Rescue excavations to salvage archaeological data and cultural materials Survey-cum-rescue excavations to better locate and design the follow up rescue excavations Further surveys to obtain sufficient data for formulation of appropriate mitigation measures	Future Private Developer	After land resumption and prior to any construction works	resumption and prior to any construction works	Guidelines for Cultural Heritage Impact Assessment TM-EIAO Annex 10 and Annex 19 Antiquities and Monuments Ordinance
S.12.5	CH2	Terrestrial Archaeology Implement watching brief during construction phase (see Figure 14.1 for the locations of watching brief)	To identify and record any archaeological material or features revealed during construction phase	Future Private	During construction phase	During construction phase	

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
EM&A P	roject						
S13.2	EM1	An Independent Environmental Checker needs to be employed as per the EM&A Manual.	Control EM&A Performance	Project Proponent	All constructi on sites	Construction stage	EIAO Guidance Note No.4/2010TM-EIAO
S13.2 – 13.4	EM2	 An Environmental Team needs to be employed as per the EM&A Manual. Prepare a systematic Environmental Management Plan to ensure effective implementation of the mitigation measures. An environmental impact monitoring needs to be implementing by the Environmental Team to ensure all the requirements given in the EM&A Manual are fully complied with. 	Perform environmental monitoring & auditing	Project Proponent	All constructi on sites	Construction stage	• EIAO Guidance Note No.4/2010 • TM-EIAO

ET's note: Pages B-53 and B-54 are not relevant to the Project works in Tung Chung West and therefore not presented.

EIA EM&A Log Ref Recommended Mitigation Measures		Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
--	--	-------------------------	----------------------	-------------------------	---

Post-planting Monitoring and Maintenance (Details to be provided after the submission of Detailed Compensatory Woodland Planting Plan as required under EP Condition 2.22)

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
-------------	-----------------	---------------------------------	---	-------------------------	----------------------	-------------------------	---

Use of New Low Noise Road Surfacing Material(s) (Details to be provided after the submission of Plan for Review of Use of New Low Noise Road Surfacing Material(s) as required under EP Condition 2.23)

Environmental Mitigation Implementation Schedule – Tung Chung New Town Extension

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
Follow-up actions to be taken by the Contractor and Dump Truck Drivers in case of Illegal Dumping and Landfilling of C&D Materials (Extracted from Waste Mana submitted under Condition 2.24 of the EP)						Management Plan	
S5.4	WM1	Investigation report will be prepared by the Contractor and submit to ER within 2 working days.	Control EM&A Performance	Contractor	All constructi on sites		• EP • Contractual requirements
S5.4	WM2	The Contractor will discuss with ER for the follow up actions (e.g. warning letter, cease operation, etc.) if required.	Control EM&A Performance	Contractor	All constructi on sites		• EP • Contractual requirements

D. Status of Submissions and Implementation Status of Mitigation Measures under EP

Appendix D: Status of Submissions and Implementation Status of Mitigation Measures under EP

EP Condition	Submission / Implementation Status	Status
2.1	Set up of Community and Professional Liaison Groups	Community and Professional Liaison Groups were set up
2.1	Complaint Management Plan (for Contracts 5 and 6)	Accepted by EPD
2.5	Employment of Qualified Ecologist(s)	Qualified Ecologists have been employed to carry out work relating to ecological aspects
2.6	Employment of Surveillance Team	Surveillance Team has been employed to conduct regular site inspection
2.11	Management Organisations (for Contracts 5 and 6)	Updated Submission submitted to EPD on 13 May 2022
2.12	Construction Works Schedule and Location Plans (for Contracts 5 and 6)	Accepted by EPD
2.18	Plan on Provision of Buffer Zones	Accepted by EPD
2.19	River Park Plan	Revised Submission submitted to EPD on 6 Jan 2022
2.20	Habitat Enhancement and Translocation Plan for Amphibian Species of Conservation Importance	Accepted by EPD
2.21	Detailed Preservation and/or Translocation Plan for Plant Species of Conservation Importance	Revised Submission submitted to EPD on 30 Mar 2022
2.22	Detailed Compensatory Woodland Planting Plan	Revised Submission submitted to EPD on 4 Apr 2022
2.23	Plan for Review of Use of New Low Noise Road Surfacing Material(s)	Revised Submission submitted to EPD on 2 Dec 2021
2.24	Waste Management Plan (for Contracts 5 and 6)	Accepted by EPD
2.31	Implement Plan on Provision of Buffer Zones, River Park Plan, Habitat Enhancement and Translocation Plan for Amphibian Species of Conservation Importance, Detailed Preservation and/or Translocation Plan for Plant Species of Conservation Importance and Detailed Compensatory Woodland Planting Plan	Provision of Buffer Zones and Habitat Enhancement and Translocation Plan for Amphibian Species of Conservation Importance are under implementation. Others are to be implemented.
2.32	Implement Plan for Review of Use of New Low Noise Road Surfacing Material(s)	To be implemented
2.32	Implement Waste Management Plan	Under implementation
2.33	Install noise barriers and low noise road surfacing at the extended Chung Mun Road and Road D3. All noise mitigation measures implemented shall be properly maintained during the operation of the above roads.	To be implemented
2.34	Implement a deodouriser with an odour removal efficiency of at least 95% shall be installed, operated and maintained within each sewage pumping station. The exhaust of the deodouriser shall be oriented away from sensitive receivers; and all odourous facilities of each sewage pumping station shall be enclosed and negative pressure shall be maintained within the facilities.	To be implemented
2.35	Enclose all the pumps inside a building structure	To be implemented

EP Condition	Submission / Implementation Status	Status
2.36	(i) a 100% standby pumping capacity shall be installed and maintained;	To be implemented
	(ii) a 50% spare pumping capacity shall be installed and maintained;	To be implemented
	(iii) dual-feed power supply shall be installed and maintained; and	To be implemented
	(iv) an emergency facility with a 6-hour storage capacity of average dry weather flow shall be installed and maintained.	To be implemented

E. Status of Statutory Environmental Requirements


Appendix E: Status of Statutory Environmental Requirements

Contract No.	Description	Location	Ref. No.	Status
General	Environmental Permit	TCW Works Areas	EP-519/2016	Issued on 9 Aug 2016
NL/2020/05 ("Contract 5")	Billing Account for Disposal of Construction Waste	Contract 5 works areas	Account No. 7040874	Issued on 25 Jun 2021
	Registration as Chemical Waste Producer	Contract 5 works areas	WPN 5213-950-B2634-01	Issued on 13 Jul 2021
	Discharge Licence under Water Pollution Control Ordinance	Area Part E Ma Wan Chung Nullah	WT00040844-2022	Valid from 27 May 2022 to 31 May 2027
		Cheung Tung Road, Tai Ho Wan, Tung Chung	476380	Application submitted to EPD on 24 Jan 2022
	Construction Noise Permit	Junction of Chung Yan Road and Tung Chung Road North, near Wong Nai Uk, Tung Chung	478865	Application submitted to EPD on 21 Apr 2022
NL/2020/06 ("Contract 6")	Billing Account for Disposal of Construction Waste	Contract 6 works areas	Account No. 7040815	Issued on 17 Jun 2021
	Registration as Chemical Waste Producer	Contract 6 works areas	WPN 5213-950-C4603-01	Issued on 13 Jul 2021
	Discharge Licence under Water Pollution Control Ordinance	Pumping Station at Chung Mun Road	WT00039653-2021	Valid from 17 Jan 2022 to 31 Jan 2027
		Area 42	WT00040646-2022	Valid from 29 Apr 2022 to 30 Apr 2027
	Construction Noise Permit	-	-	-

F. Air Quality

- F1. Locations of Air Quality Monitoring Stations
- F2. Air Quality Monitoring Equipment Calibration Certificates
- F3. Air Quality Monitoring Schedule
- F4. Air Quality Monitoring Results
- F5. Air Quality Monitoring Event and Action Plan

F1. Locations of Air Quality Monitoring Stations

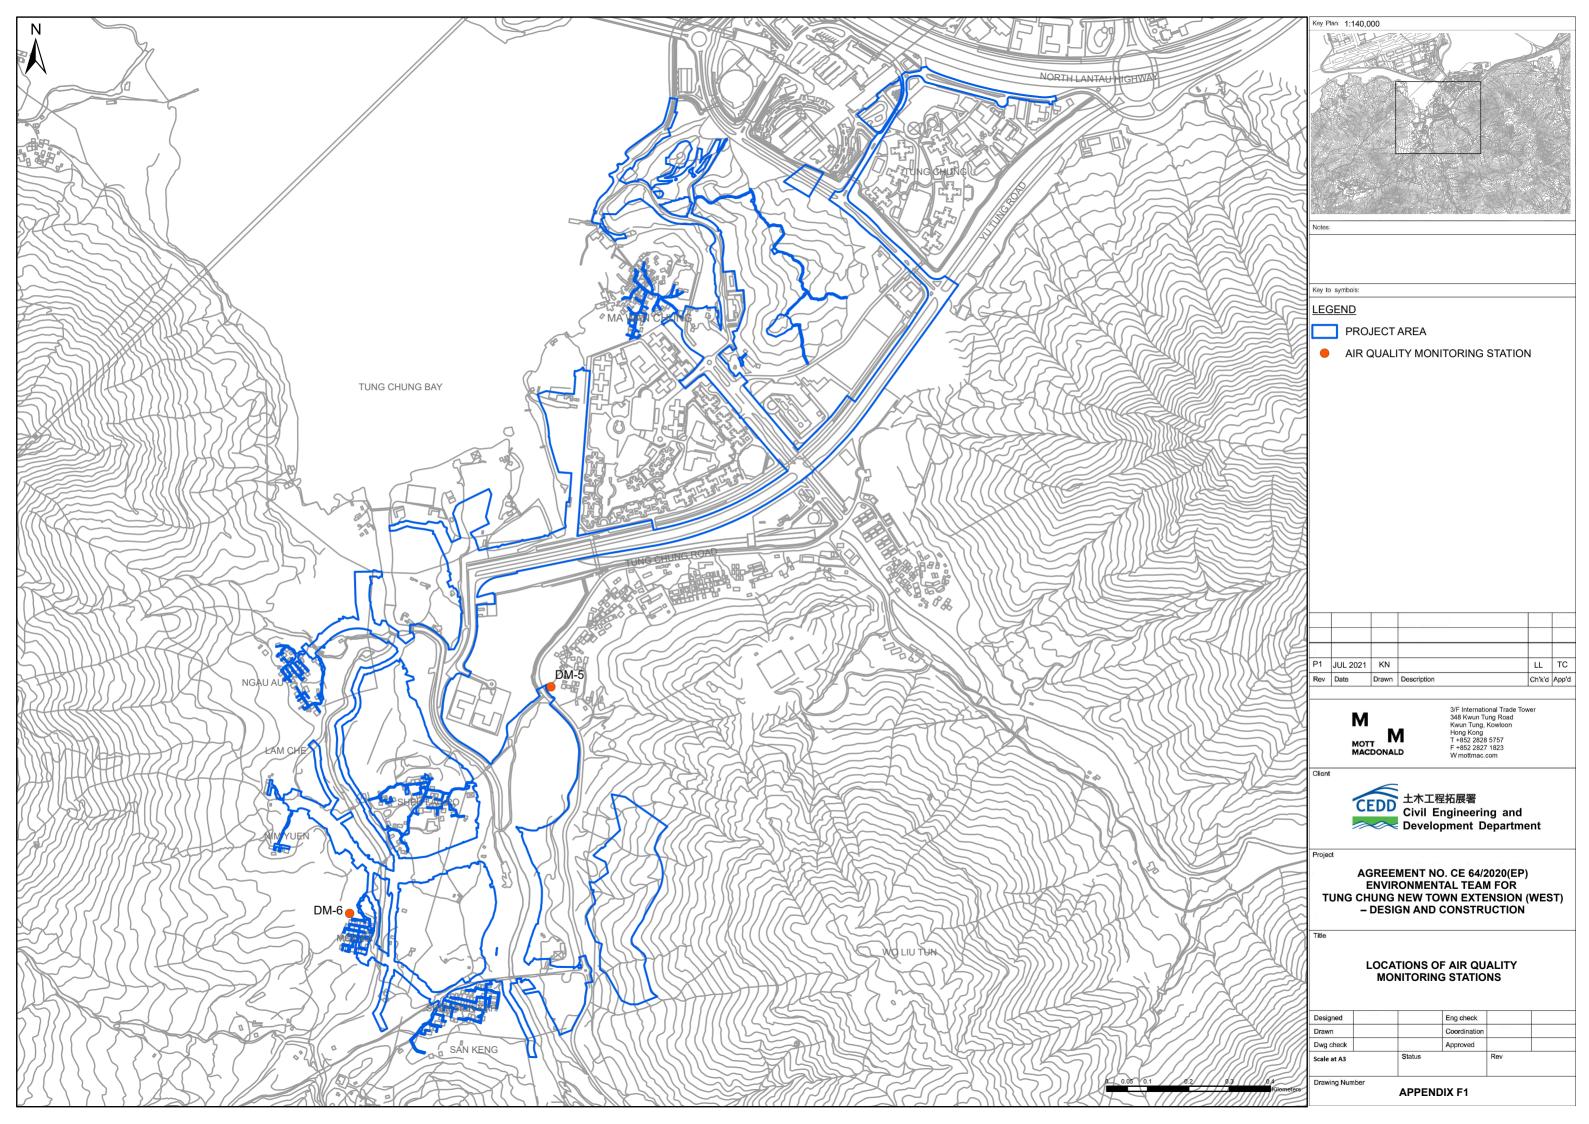

F2. Air Quality Monitoring Equipment Calibration Certificates

ALS Technichem (HK) Pty Ltd

ALS Laboratory Group

ANALYTICAL CHEMISTRY & TESTING SERVICES



SUB-CONTRACTING REPORT

CONTACT : MR K.W. FAN WORK ORDER : HK2144588

CLIENT : ENVIROTECH SERVICES CO.

ADDRESS : RM113, 1/F, MY LOFT, 9 HOI WING ROAD, SUB-BATCH : 1

TUEN MUN, N.T. HONG KONG

DATE RECEIVED : 2-NOV-2021

DATE OF ISSUE : 11-NOV-2021

PROJECT : --- NO. OF SAMPLES : 1

CLIENT ORDER :---

General Comments

 Sample(s) was/ were submitted by client. Sample(s) arrived laboratory in ambient condition. The result(s) related only to the item(s) tested.

- Sample information (Project name, Sample ID, Sampling date/time, etc.) is provided by client.
- Calibration was subcontracted to and analysed by Action-United Environmental Services & Consulting.

Signatories

This document has been signed by those names that appear on this report and are the authorised signatories

Signatories Position

Diaband Funan

Richard Fung Managing Director

This is the Final Report and supersedes any preliminary report with this batch number.

All pages of this report have been checked and approved for release.

: HK2144588 WORK ORDER

SUB-BATCH

: 1 : ENVIROTECH SERVICES CO. CLIENT

PROJECT



ALS Lab	Client's Sample ID	_	Sample Date	External Lab Report No.
ID		Туре		
HK2144588-001	S/N: 276019	Equipments	02-Nov-2021	S/N: 276019

Equipment Verification Report (TSP)

Equipment Calibrated:

Type: Laser Dust monitor

Manufacturer: Sibata LD-3B

Serial No. 276019

Equipment Ref: Nil

Job Order HK2144588

Standard Equipment:

Standard Equipment: Higher Volume Sampler (TSP)

Location & Location ID: AUES office (calibration room)

Equipment Ref: HVS 018

Last Calibration Date: 5 November 2021

Equipment Verification Results:

Verification Date: 5 November 2021


Hour	Time	Mean Temp °C	Mean Pressure (hPa)	Concentration in ug/m³ (Standard Equipment)	Total Count (Calibrated Equipment)	Count/Minute (Total Count/min)
2hr01min	09:11 ~ 11:12	25.6	1012.5	51.2	4508	37.2
2hr01min	11:15 ~ 13:16	25.6	1012.5	47.8	3690	30.4
2hr02min	13:20 ~ 15:22	25.6	1012.5	50.4	3979	32.7

Linear Regression of Y or X

Slope (K-factor): <u>1.4601 (μg/m³)/CPM</u>

Correlation Coefficient (R) 0.9930

Date of Issue 8 November 2021



Remarks:

- 1. **Strong** Correlation (R>0.8)
- 2. Factor 1.4601 (µg/m³)/CPM should be applied for TSP monitoring

*If R<0.5, repair or re-verification is required for the equipment

Operator : _____ Fai So Signature : _____ Date : <u>8 November 2021</u>

QC Reviewer : Ben Tam Signature : Date : 8 November 2021

TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location: Gold King Industrial Building, Kwai Chung Date of Calibration: 5-Nov-21
Location ID: Calibration Room Next Calibration Date: 5-Feb-22

CONDITIONS

Sea Level Pressure (hPa) Temperature (°C) 1012.5 25.6

Corrected Pressure (mm Hg)
Temperature (K)

759.375 299

CALIBRATION ORIFICE

Make-> TISCH
Model-> 5025A
Calibration Date-> 19-Jan-21

Qstd Slope -> Qstd Intercept -> Expiry Date-> 2.10574 -0.00985 18-Jan-22

CALIBRATION

Plate	H20 (L)	H2O (R)	H20	Qstd	I	IC	LINEAR
No.	(in)	(in)	(in)	(m3/min)	(chart)	corrected	REGRESSION
18	6.2	6.2	12.4	1.675	52	51.93	Slope = 24.2092
13	5	5	10.0	1.504	48	47.93	Intercept = 10.8881
10	3.9	3.9	7.8	1.329	42	41.94	Corr. coeff. = 0.9959
8	2.5	2.5	5.0	1.065	36	35.95	
5	1.0	1.0	2.0	0.675	28	27.96	

Calculations:

Qstd = 1/m[Sqrt(H20(Pa/Pstd)(Tstd/Ta))-b]

IC = I[Sqrt(Pa/Pstd)(Tstd/Ta)]

Ostd = standard flow rate

IC = corrected chart respones

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration (deg K)

Pstd = actual pressure during calibration (mm Hg)

For subsequent calculation of sampler flow:

1/m((I)[Sqrt(298/Tav)(Pav/760)]-b)


m = sampler slope

b = sampler intercept

I = chart response

Tay = daily average temperature

Pav = daily average pressure

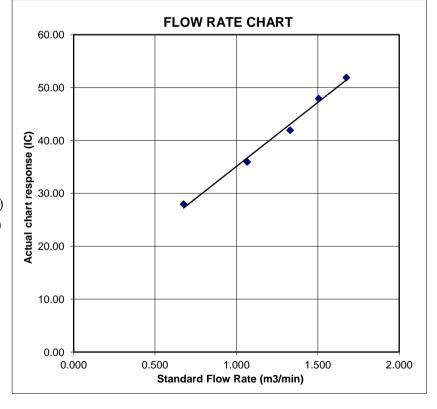



RECALIBRATION DUE DATE:

January 19, 2022

Certificate of Calibration

Calibration Certification Information

Cal. Date: January 19, 2021

Rootsmeter S/N: 438320

Ta: 294
Pa: 755.1

°K

Operator: Jim Tisch

Calibration Model #:

TE-5025A

Calibrator S/N: 1941

mm Hg

Run	Vol. Init (m3)	Vol. Final (m3)	ΔVol. (m3)	ΔTime (min)	ΔP (mm Hg)	ΔH (in H2O)
1	1	2	1	1.4830	3.2	2.00
2	3	4	1	1.0420	6.4	4.00
3	5	6	1	0.9290	8.0	5.00
4	7	8	1	0.8840	8.8	5.50
5	9	10	1	0.7340	12.9	8.00

	Data Tabulation							
Vstd	Qstd	$\sqrt{\Delta H \left(\frac{Pa}{Pstd}\right) \left(\frac{Tstd}{Ta}\right)}$		Qa	$\sqrt{\Delta H (Ta/Pa)}$			
(m3)	(x-axis)	(y-axis)	Va	(x-axis)	(y-axis)			
1.0029	0.6762	1.4192	0.9958	0.6715	0.8824			
0.9986	0.9583	2.0071	0.9915	0.9516	1.2479			
0.9965	1.0726	2.2440	0.9894	1.0650	1.3952			
0.9954	1.1260	2.3535	0.9883	1.1180	1.4633			
0.9899	1.3487	2.8385	0.9829	1.3391	1.7648			
	m=	2.10574		m=	1.31858			
QSTD	b=	-0.00985	QA	b=	-0.00612			
-	r=	0.99992	,	r=	0.99992			

Calculations						
Vstd= ΔVol((Pa-ΔP)/Pstd)(Tstd/Ta)	Va= ΔVol((Pa-ΔP)/Pa)					
Qstd= Vstd/∆Time	Qa= Va/ΔTime					
For subsequent flow rate calculations:						
Qstd= $1/m \left(\sqrt{\Delta H \left(\frac{Pa}{Pstd} \right) \left(\frac{Tstd}{Ta} \right)} \right) - b \right)$	$\mathbf{Qa} = 1/m \left(\left(\sqrt{\Delta H \left(Ta/Pa \right)} \right) - b \right)$					

Standard Conditions					
Tstd:	298.15 °K				
Pstd: 760 mm Hg					
Key					
ΔH: calibrator manometer reading (in H2O)					
ΔP: rootsmeter manometer reading (mm Hg)					
Ta: actual absolute temperature (°K)					
Pa: actual barometric pressure (mm Hg)					
b: intercept					
m: slope					

RECALIBRATION

US EPA recommends annual recalibration per 1998
40 Code of Federal Regulations Part 50 to 51,
Appendix B to Part 50, Reference Method for the
Determination of Suspended Particulate Matter in
the Atmosphere, 9.2.17, page 30

FAX: (513)467-9009

ALS Technichem (HK) Pty Ltd

ALS Laboratory Group

ANALYTICAL CHEMISTRY & TESTING SERVICES



SUB-CONTRACTING REPORT

CONTACT : MR K.W. FAN WORK ORDER : HK2146425

CLIENT : ENVIROTECH SERVICES CO.

ADDRESS : RM113, 1/F, MY LOFT, 9 HOI WING ROAD, SUB-BATCH : 1

TUEN MUN, N.T. HONG KONG

DATE RECEIVED : 11-NOV-2021

DATE OF ISSUE : 22-NOV-2021

PROJECT : ---- NO. OF SAMPLES : 1

CLIENT ORDER :---

General Comments

 Sample(s) was/ were submitted by client. Sample(s) arrived laboratory in ambient condition. The result(s) related only to the item(s) tested.

- Sample information (Project name, Sample ID, Sampling date/time, etc.) is provided by client.
- Calibration was subcontracted to and analysed by Action-United Environmental Services & Consulting.

Signatories

This document has been signed by those names that appear on this report and are the authorised signatories

Signatories Position

Diahand Funan

Richard Fung Managing Director

This is the Final Report and supersedes any preliminary report with this batch number.

All pages of this report have been checked and approved for release.

: HK2146425 WORK ORDER

SUB-BATCH

: 1 : ENVIROTECH SERVICES CO. CLIENT

PROJECT



ALS Lab	Client's Sample ID	Sample Type	Sample Date	External Lab Report No.
HK2146425-001	S/N: 6Z7784		11-Nov-2021	S/N: 6Z7784

Equipment Verification Report (TSP)

Equipment Calibrated:

Type: Laser Dust monitor

Manufacturer: Sibata LD-3B

Serial No. 6Z7784

Equipment Ref: Nil

Job Order HK2146425

Standard Equipment:

Standard Equipment: Higher Volume Sampler (TSP)

Location & Location ID: AUES office (calibration room)

Equipment Ref: HVS 018

Last Calibration Date: 5 November 2021

Equipment Verification Results:

Verification Date: 16 November 2021

Hour	Time	Mean Temp °C	Mean Pressure (hPa)	Concentration in ug/m³ (Standard Equipment)	Total Count (Calibrated Equipment)	Count/Minute (Total Count/min)
2hr01min	09:17 ~ 11:18	23.2	1017	36.0	2196	18.2
2hr01min	11:22 ~ 13:23	23.2	1017	36.7	2850	23.6
2hr01min	13:27 ~ 15:28	23.2	1017	52.5	3151	26.1

Linear Regression of Y or X

Slope (K-factor): <u>1.8375 (μg/m³)/CPM</u>

Correlation Coefficient (R) 0.9755

Date of Issue 19 November 2021

60 50 40 30 20 y=1.8375x+0.0938 R² = 0.9516

Remarks:

1. **Strong** Correlation (R>0.8)

2. Factor 1.8375 (µg/m³)/CPM should be applied for TSP monitoring

*If R<0.5, repair or re-verification is required for the equipment

Operator : Fai So Signature : Date : 19 November 2021

QC Reviewer : Ben Tam Signature : Date : 19 November 2021

TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location: Gold King Industrial Building, Kwai Chung Date of Calibration: 5-Nov-21
Location ID: Calibration Room Next Calibration Date: 5-Feb-22

CONDITIONS

Sea Level Pressure (hPa) Temperature (°C) 1012.5 25.6

Corrected Pressure (mm Hg)
Temperature (K)

759.375 299

CALIBRATION ORIFICE

Make-> TISCH
Model-> 5025A
Calibration Date-> 19-Jan-21

Qstd Slope -> Qstd Intercept -> Expiry Date-> 2.10574 -0.00985 18-Jan-22

CALIBRATION

Plate	H20 (L)	H2O (R)	H20	Qstd	I	IC	LINEAR
No.	(in)	(in)	(in)	(m3/min)	(chart)	corrected	REGRESSION
18	6.2	6.2	12.4	1.675	52	51.93	Slope = 24.2092
13	5	5	10.0	1.504	48	47.93	Intercept = 10.8881
10	3.9	3.9	7.8	1.329	42	41.94	Corr. coeff. = 0.9959
8	2.5	2.5	5.0	1.065	36	35.95	
5	1.0	1.0	2.0	0.675	28	27.96	

Calculations:

Qstd = 1/m[Sqrt(H20(Pa/Pstd)(Tstd/Ta))-b]

IC = I[Sqrt(Pa/Pstd)(Tstd/Ta)]

Ostd = standard flow rate

IC = corrected chart respones

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration (deg K)

Pstd = actual pressure during calibration (mm Hg)

For subsequent calculation of sampler flow:

1/m((I)[Sqrt(298/Tav)(Pav/760)]-b)


m = sampler slope

b = sampler intercept

I = chart response

Tay = daily average temperature

Pav = daily average pressure

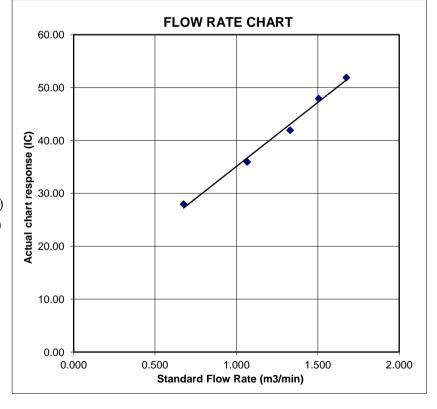



RECALIBRATION DUE DATE:

January 19, 2022

Certificate of Calibration

Calibration Certification Information

Cal. Date: January 19, 2021

Rootsmeter S/N: 438320

Ta: 294
Pa: 755.1

°K

Operator: Jim Tisch

Calibration Model #:

TE-5025A

Calibrator S/N: 1941

mm Hg

Run	Vol. Init (m3)	Vol. Final (m3)	ΔVol. (m3)	ΔTime (min)	ΔP (mm Hg)	ΔH (in H2O)
1	1	2	1	1.4830	3.2	2.00
2	3	4	1	1.0420	6.4	4.00
3	5	6	1	0.9290	8.0	5.00
4	7	8	1	0.8840	8.8	5.50
5	9	10	1	0.7340	12.9	8.00

	Data Tabulation						
Vstd	Qstd	$\sqrt{\Delta H \left(\frac{Pa}{Pstd}\right) \left(\frac{Tstd}{Ta}\right)}$		Qa	$\sqrt{\Delta H (Ta/Pa)}$		
(m3)	(x-axis)	(y-axis)	Va	(x-axis)	(y-axis)		
1.0029	0.6762	1.4192	0.9958	0.6715	0.8824		
0.9986	0.9583	2.0071	0.9915	0.9516	1.2479		
0.9965	1.0726	2.2440	0.9894	1.0650	1.3952		
0.9954	1.1260	2.3535	0.9883	1.1180	1.4633		
0.9899	1.3487	2.8385	0.9829	1.3391	1.7648		
	m=	2.10574		m=	1.31858		
QSTD	b=	-0.00985	QA	b=	-0.00612		
-	r=	0.99992	,	r=	0.99992		

Calculations						
Vstd= ΔVol((Pa-ΔP)/Pstd)(Tstd/Ta)	Va= ΔVol((Pa-ΔP)/Pa)					
Qstd= Vstd/∆Time	Qa= Va/ΔTime					
For subsequent flow r	ate calculations:					
Qstd= $1/m \left(\sqrt{\Delta H \left(\frac{Pa}{Pstd} \right) \left(\frac{Tstd}{Ta} \right)} \right) - b \right)$	$\mathbf{Qa} = 1/m \left(\left(\sqrt{\Delta H \left(Ta/Pa \right)} \right) - b \right)$					

	Standard Conditions					
Tstd:	298.15 °K					
Pstd:	760 mm Hg					
	Key					
ΔH: calibrate	or manometer reading (in H2O)					
	ter manometer reading (mm Hg)					
Ta: actual absolute temperature (°K)						
Pa: actual barometric pressure (mm Hg)						
b: intercept						
m: slope						

RECALIBRATION

US EPA recommends annual recalibration per 1998
40 Code of Federal Regulations Part 50 to 51,
Appendix B to Part 50, Reference Method for the
Determination of Suspended Particulate Matter in
the Atmosphere, 9.2.17, page 30

FAX: (513)467-9009

F3. Air Quality Monitoring Schedule

May 2022 - Impact Monitoring Schedule for Tung Chung West

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
1	2	3	4	5	6 Air Quality Monitoring	7
					All Quality Monitoring	
8	9	10	11	12	13	14
			Air Quality Monitoring			
15	16	17	18	19	20	21
		Air Quality Monitoring				
22	23	24	25	26	27	28
	Air Quality Monitoring				Air Quality Monitoring	
29	30	31				
				Notes: Air Quality Monitoring Statio	n: DM-5 - Lung Tseung Tau DM-6 - Mok Ka	
					z o monna	

F4. Air Quality Monitoring Results

1-hour TSP Results


Station: DM5 - Lung Tseung Tau

Date	Strat Time	Finish Time	Weather	1-hr TSP (μg/m³)	Action Level (μg/m³)	Limit Level (μg/m³)
06-May-22	8:36	9:36	Sunny	22.0	266	500
06-May-22	9:36	10:36	Sunny	22.0	266	500
06-May-22	10:36	11:36	Sunny	26.0	266	500
11-May-22	13:43	14:43	Cloudy	19.0	266	500
11-May-22	14:43	15:43	Cloudy	27.0	266	500
11-May-22	15:43	16:43	Cloudy	24.0	266	500
17-May-22	9:23	10:23	Sunny	13.0	266	500
17-May-22	10:23	11:23	Sunny	16.0	266	500
17-May-22	11:23	12:23	Sunny	17.0	266	500
23-May-22	8:45	9:45	Cloudy	14.0	266	500
23-May-22	9:45	10:45	Cloudy	26.0	266	500
23-May-22	10:45	11:45	Cloudy	33.0	266	500
27-May-22	9:18	10:18	Cloudy	30.0	266	500
27-May-22	10:18	11:18	Cloudy	34.0	266	500
27-May-22	12:27	13:27	Cloudy	43.0	266	500

1-hour TSP Results

Station: DM6 - Mok Ka

Date	Start Time	Finish Time	Weather		Action Level	3
Date	Start Time	rinish time	weather	1-hr TSP (μg/m ³)	$(\mu g/m^3)$	Limit Level (µg/m³)
06-May-22	8:51	9:51	Sunny	21.0	260	500
06-May-22	9:51	10:51	Sunny	21.0	260	500
06-May-22	10:51	11:51	Sunny	22.0	260	500
11-May-22	14:01	15:01	Cloudy	31.0	260	500
11-May-22	15:01	16:01	Cloudy	30.0	260	500
11-May-22	16:01	17:01	Cloudy	28.0	260	500
17-May-22	9:35	10:35	Sunny	19.0	260	500
17-May-22	10:35	11:35	Sunny	17.0	260	500
17-May-22	11:35	12:35	Sunny	18.0	260	500
23-May-22	9:01	10:01	Cloudy	14.0	260	500
23-May-22	10:01	11:01	Cloudy	21.0	260	500
23-May-22	11:01	12:01	Cloudy	23.0	260	500
27-May-22	9:30	10:30	Cloudy	23.0	260	500
27-May-22	10:30	11:30	Cloudy	23.0	260	500
27-May-22	12:41	13:41	Cloudy	27.0	260	500

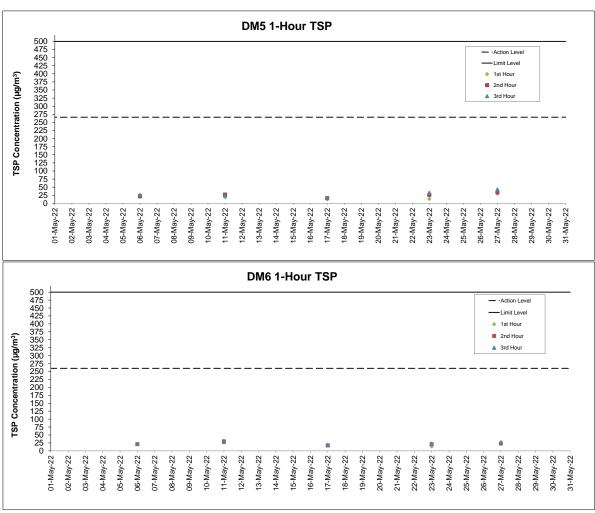

- Notes

 1. Major site activities carried out during the reporting period are summarized in Section 1.4 of the monthly EM&A report.

 2. Weather conditions during monitoring are presented in the data tables above.

 3. QA/QC requirements as stipulated in the EM&A Manual were carried out during measurement.

F5. Air Quality Monitoring Event and Action Plan

Table F5.1: Event and Action Plan for Construction Air Quality (Action Level)

Event	Action					
	ET	IEC	ER	Contractor		
Action Level						
Exceedance for one sample	 Identify source, investigate the causes of exceedance and propose remedial measures; Inform IEC and ER; Repeat measurement to confirm finding; Increase monitoring frequency to daily. 	Check monitoring data submitted by ET; Check Contractor's working method.	Notify Contractor.	Rectify any unacceptable practice; Amend working methods if appropriate.		
Exceedance for two or more consecutive samples	1. Identify source; 2. Inform IEC and ER; 3. Advise the ER on the effectiveness of the proposed remedial measures; 4. Repeat measurements to confirm findings; 5. Increase monitoring frequency to daily; 6. Discuss with IEC and Contractor on remedial actions required; 7. If exceedance continues, arrange meeting with IEC and ER; 8. If exceedance stops, cease additional monitoring.	1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the ET on the effectiveness of the proposed remedial measures; 5. Supervise Implementation of remedial measures.	Confirm receipt of notification of failure in writing; Notify Contractor; Ensure remedial measures properly implemented.	1. Submit proposals for remedial to ER within 3 working days of notification; 2. Implement the agreed proposals; 3. Amend proposal if appropriate.		


Table F5.2: Event and Action Plan for Construction Air Quality (Limit Level)

Event	Action						
	ET	IEC	ER	Contractor			
Limit Level							
Exceedance for one sample	Identify source, investigate the causes of exceedance and propose remedial measures; Inform ER, Contractor and EPD; Repeat measurement to confirm finding; Increase monitoring frequency to daily; Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results.	 Check monitoring data submitted by ET; Check Contractor's working method; Discuss with ET and Contractor on possible remedial measures; Advise the ER on the effectiveness of the proposed remedial measures; Supervise implementation of remedial measures. 	1.Confirm receipt of notification of failure in writing; 2.Notify Contractor; 3.Ensure remedial measures properly implemented	 Take immediate action to avoid further exceedance; Submit proposals for remedial actions to IEC within 3 working days of notification; Implement the agreed proposals; Amend proposal if appropriate. 			
Exceedance for two or more consecutive samples	 Notify IEC, ER, Contractor and EPD; Identify source; Repeat measurement to confirm findings; Increase monitoring frequency to daily; Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; Arrange meeting with IEC and ER to discuss the remedial actions to be taken; Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; If exceedance stops, cease additional monitoring. 	Discuss amongst ER, ET, and Contractor on the potential remedial actions; Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; Supervise the implementation of remedial measures.	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. In consultation with the IEC, agree with the Contractor on the remedial measures to be implemented; 4. Ensure remedial measures properly implemented; 5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated.	1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within 3 working days of notification; 3. Implement the agreed proposals; 4. Resubmit proposals if problem still not under control; 5. Stop the relevant portion of works as determined by the ER until the exceedance is abated.			

G. Noise

- **G1.** Locations of Construction Noise Monitoring Stations
- **G2.** Construction Noise Monitoring Equipment Calibration Certificates
- **G3.** Construction Noise Monitoring Schedule
- **G4.** Construction Noise Monitoring Results
- **G5.** Construction Noise Monitoring Event and Action Plan

G1. Locations of Construction Noise Monitoring Stations

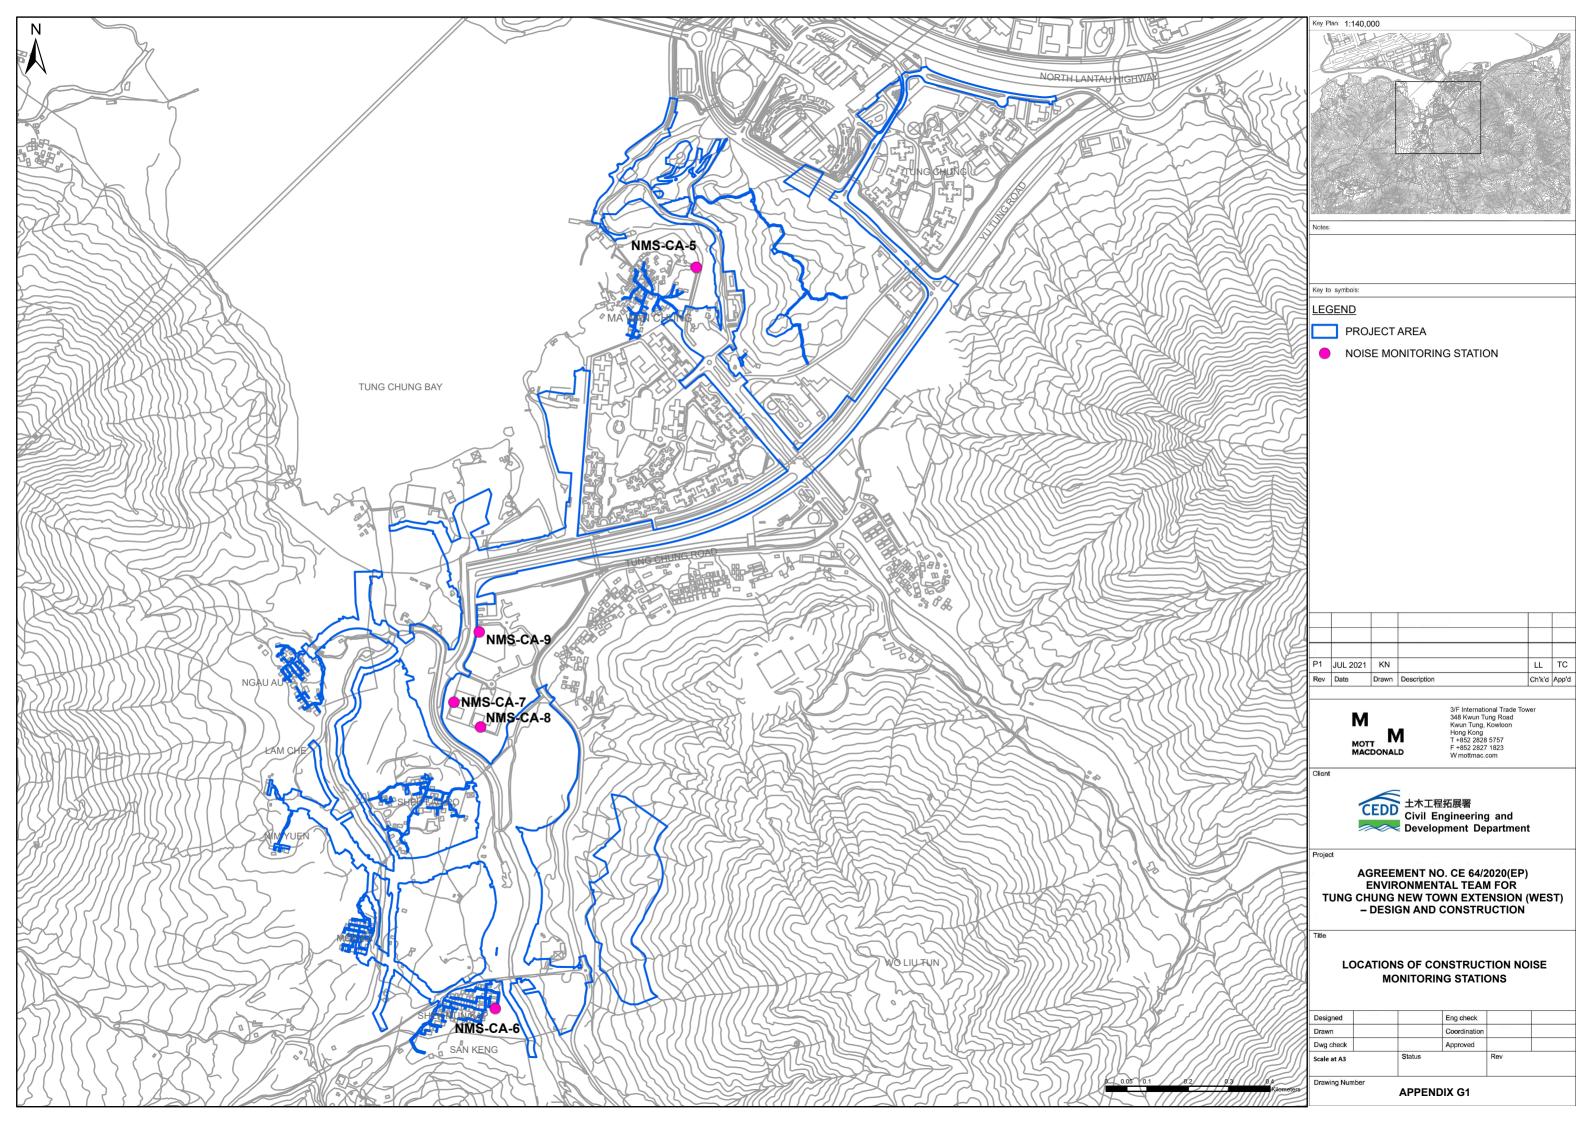

G2. Construction Noise Monitoring Equipment Calibration Certificates



Sun Creation Engineering Limited

Calibration & Testing Laboratory

Certificate of Calibration

校下證書

Certificate No.:

C213253

證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號: IC21-1006)

Date of Receipt / 收件日期: 21 May 2021

Description / 儀器名稱

Precision Acoustic Calibrator

Manufacturer / 製造商

LARSON DAVIS

Model No. / 型號

CAL200

Serial No./編號

11333

Supplied By / 委託者

Envirotech Services Co.

Room 113, 1/F, My Loft, 9 Hoi Wing Road, Tuen Mun,

New Territories, Hong Kong

TEST CONDITIONS/測試條件

Temperature / 溫度 :

Relative Humidity / 相對濕度 :

 $(50 \pm 25)\%$

Line Voltage / 電壓 :

TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST/測試日期

4 June 2021

TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.

The results do not exceed manufacturer's specification.

The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via:

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies / Keysight Technologies

- Fluke Everett Service Center, USA

Tested By

測試

K P Cheuk Project Engineer

Certified By

核證

C Lee

Engineer

Date of Issue

7 June 2021

簽發日期

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited - Calibration & Testing Laboratory c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong 輝創工程有限公司 - 校正及檢測實驗所 c/o 香港新界屯門與安里一號四樓 Tel/電話: (852) 2927 2606 Fax/傳真: (852) 2744 8986



Sun Creation Engineering Limited

Calibration & Testing Laboratory

Certificate of Calibration

Certificate No.:

C213253

證書編號

1. The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours before the commencement of the test.

2. The results presented are the mean of 3 measurements at each calibration point.

3. Test equipment:

Equipment ID

CL130 CL281

TST150A

Description

Universal Counter

Multifunction Acoustic Calibrator

Measuring Amplifier

Certificate No.

C203952 AV210017

C201309

4. Test procedure: MA100N.

5. Results:

5.1 Sound Level Accuracy

UUT	Measured Value	Mfr's Spec.	Uncertainty of Measured Value
Nominal Value	(dB) _	(dB)	(dB)
94 dB, 1 kHz	93.8	± 0.2	± 0.2
114 dB, 1 kHz	113.8		

5.2 Frequency Accuracy

UUT Nominal Value	Measured Value	Mfr's	Uncertainty of Measured Value
(kHz)	(kHz)	Spec.	(Hz)
1	1 000	1 kHz ± 1 %	± 1

Remark: The uncertainties are for a confidence probability of not less than 95 %.

Note:

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。



Sun Creation Engineering Limited

Calibration & Testing Laboratory

Certificate of Calibration 校正證書

Certificate No.: C216702

證書編號

·ITEM TESTED / 送檢項目 (Job No. / 序引編號: IC21-2322)

Date of Receipt / 收件日期: 9 November 2021

Description / 儀器名稱

Sound Level Meter

Manufacturer / 製造商

Rion

Model No./型號 Serial No./編號

NL-52 00710259

Supplied By / 委託者

Envirotech Services Co.

Room 113, 1/F, My Loft, 9 Hoi Wing Road, Tuen Mun,

New Territories, Hong Kong

TEST CONDITIONS / 測試條件

Temperature / 温度

Relative Humidity / 相對濕度 :

 $(50 \pm 25)\%$

Line Voltage / 電壓 :

TEST SPECIFICATIONS / 測試規範

Calibration

DATE OF TEST/測試日期

20 November 2021

TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.

The results do not exceed manufacturer's specification. (after adjustment)

The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via:

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies / Keysight Technologies
- Fluke Everett Service Center, USA

Tested By 測試

HT Wong Assistant Engineer

Certified By 核證

K/C Lee Engineer Date of Issue 簽發日期

Website/網址: www.suncreation.com

22 November 2021

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited - Calibration & Testing Laboratory c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong 輝創工程有限公司 – 校正及檢測實驗所

c/o 香港新界屯門興安里一號四樓 Tel/電話: (852) 2927 2606

Fax/傳真: (852) 2744 8986 E-mail/電郵: callab@suncreation.com Page 1 of 4



Sun Creation Engineering Limited

Calibration & Testing Laboratory

Certificate of Calibration 校正證書

Certificate No.:

C216702

證書編號

1. The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours, and switched on to warm up for over 10 minutes before the commencement of the test.

2. Self-calibration using the internal standard (After Adjustment) was performed before the test 6.1.1.2 to 6.3.2.

3. The results presented are the mean of 3 measurements at each calibration point.

4. Test equipment:

Equipment ID

Description

Certificate No.

CL280 CL281 40 MHz Arbitrary Waveform Generator

C210084

Multifunction Acoustic Calibrator

AV210017

- 5. Test procedure: MA101N.
- 6. Results:
- 6.1 Sound Pressure Level
 - 6.1.1 Reference Sound Pressure Level

6.1.1.1 Before Adjustment

UUT Setting			Applie	d Value	UUT	IEC 61672	
Range	Function	Frequency	Time	Level	Freq.	Reading	Class 1 Spec.
(dB)		Weighting	Weighting	(dB)	(kHz)	(dB)	(dB)
30 - 130	L_A	A	Fast	94.00	1	* 96.0	± 1.1

^{*} Out of IEC 61672 Class 1 Spec.

· 6.1.1.2 After Adjustment

UUT Setting				Applie	d Value	UUT	IEC 61672
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	Reading (dB)	Class 1 Spec. (dB)
30 - 130	L_{A}	A	Fast	94.00	1	94.0	± 1.1

6.1.2 Linearity

	UU'	T Setting	Applie	d Value	UUT	
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	Reading (dB)
30 - 130	L_A	A	Fast	94.00 104.00	1	94.0 (Ref.) 104.1
				114.00		114.1

IEC 61672 Class 1 Spec. : \pm 0.6 dB per 10 dB step and \pm 1.1 dB for overall different.

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。



Sun Creation Engineering Limited

Calibration & Testing Laboratory

Certificate of Calibration 校正證書

Certificate No.:

C216702

證書編號

'6.2 Time Weighting

UUT Setting			Applied Value		UUT	IEC 61672	
Range (dB)	Function	Frequency Weighting			Freq. (kHz)	Reading (dB)	Class 1 Spec. (dB)
30 - 130	L_A	A	Fast Slow	94.00	1	94.0 94.0	Ref. ± 0.3

6.3 Frequency Weighting

6.3.1 A-Weighting

UUT Setting				Applied Value		UUT	IEC 61672
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq.	Reading (dB)	Class 1 Spec. (dB)
30 - 130	L _A	A	Fast	94.00	63 Hz	67.7	-26.2 ± 1.5
					125 Hz	77.7	-16.1 ± 1.5
					250 Hz	85.3	-8.6 ± 1.4
					500 Hz	90.7	-3.2 ± 1.4
					1 kHz	94.0	Ref.
		y * .		4	2 kHz	95.2	$+1.2 \pm 1.6$
		,	3		4 kHz	95.0	$+1.0 \pm 1.6$
					8 kHz	92.9	-1.1 (+2.1; -3.1)
					16 kHz	86.0	-6.6 (+3.5 ; -17.0

6.3.2 C-Weighting

	UUT Setting			Applied Value		UUT	IEC 61672
Range	Function	Frequency	Time	Level	Freq.	Reading	Class 1 Spec.
(dB)		Weighting	Weighting	(dB)		(dB)	(dB) ₃
30 - 130	L_{C}	С	Fast	94.00	63 Hz	93.1	-0.8 ± 1.5
					125 Hz	93.8	-0.2 ± 1.5
					250 Hz	94.0	0.0 ± 1.4
. 4	W -				500 Hz	94.0	0.0 ± 1.4
					1 kHz	94.0	Ref.
		194			2 kHz	93.8	-0.2 ± 1.6
	1-1-1				4 kHz	93.2	-0.8 ± 1.6
					8 kHz	91.0	-3.0 (+2.1; -3.1)
				200000000	16 kHz	84.1	-8.5 (+3.5; -17.0)

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。



輝創工程有限公司

Sun Creation Engineering Limited

Calibration & Testing Laboratory

Certificate of Calibration 校正證書

Certificate No.: C216702

證書編號

Remarks: - UUT Microphone Model No.: UC-59 & S/N: 13748

- Mfr's Spec. : IEC 61672 Class 1

- Uncertainties of Applied Value : 94 dB : 63 Hz - 125 Hz : \pm 0.35 dB

104 dB: 1 kHz : ± 0.10 dB (Ref. 94 dB) 114 dB: 1 kHz : ± 0.10 dB (Ref. 94 dB)

- The uncertainties are for a confidence probability of not less than 95 %.

Note:

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

G3.	Construction	Noise	Monito	ring	Schedu	ıle
-----	--------------	--------------	---------------	------	--------	-----

May 2022 - Impact Monitoring Schedule for Tung Chung West

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
1	2	3	Noise Monitoring	5	6	7
8	9	10	11	12	13 Noise Monitoring	14
15	16	17	18	19 Noise Monitoring	20	21
22	23	24	25	26 Noise Monitoring	27	28
29	30	31 Noise Monitoring				
				Notes: Noise Monitoring Stations:	NMS-CA-5 - Village house NMS-CA-6 - Village house NMS-CA-7 - YMCA of Hon NMS-CA-8 - Caritas Charle	in Shek Mun Kap g Kong Christian College

G4.	Construction	Noise	Monitoring	Results
------------	--------------	-------	------------	---------

Noise Measurement Results

Station: NMS-CA-5 Village House in Ma Wan Chung

D-4- 14/41		T!	Measured	Measured	Measured	
Date	Weather	Time	L _{eg(Smins)} dB(A)	L ₁₀ dB(A)	L _{so} dB(A)	L _{eq(30mins)} dB(A) [∧]
04-May-22	Sunny	13:00	56.3	60.2	50.0	
04-May-22	Sunny	13:05	57.9	62.7	51.7	
04-May-22	Sunny	13:10	61.2	64.3	54.9	60
04-May-22	Sunny	13:15	60.7	64.0	55.6	00
04-May-22	Sunny	13:20	61.0	65.3	56.0	
04-May-22	Sunny	13:25	60.5	62.8	56.3	
13-May-22	Cloudy	13:01	51.8	54.3	48.5	
13-May-22	Cloudy	13:06	53.6	56.2	49.3	
13-May-22	Cloudy	13:11	52.0	54.3	49.3	54
13-May-22	Cloudy	13:16	53.9	56.6	50.5	54
13-May-22	Cloudy	13:21	53.4	57.0	50.2	
13-May-22	Cloudy	13:26	55.8	59.2	50.4	
19-May-22	Cloudy	13:02	56.0	58.1	48.4	
19-May-22	Cloudy	13:07	59.0	63.0	52.0	
19-May-22	Cloudy	13:12	52.8	53.9	51.4	57
19-May-22	Cloudy	13:17	56.5	59.9	51.6	37
19-May-22	Cloudy	13:22	58.2	60.3	53.3	
19-May-22	Cloudy	13:27	59.1	61.6	53.6	
26-May-22	Cloudy	13:00	50.4	52.1	48.2	
26-May-22	Cloudy	13:05	52.8	57.6	48.1	
26-May-22	Cloudy	13:10	54.3	57.0	47.6	54
26-May-22	Cloudy	13:15	55.7	58.4	52.2	34
26-May-22	Cloudy	13:20	54.5	56.3	51.2	
26-May-22	Cloudy	13:25	54.6	58.1	50.3	
31-May-22	Cloudy	13:02	54.9	56.2	53.0	
31-May-22	Cloudy	13:07	58.5	62.4	51.5	
31-May-22	Cloudy	13:12	62.5	65.7	53.3	61
31-May-22	Cloudy	13:17	61.8	65.1	53.6	01
31-May-22	Cloudy	13:22	62.6	65.6	54.9	
31-May-22	Cloudy	13:27	61.7	65.1	53.3	

Remarks:
(^) +3dB (A) Façade correction included for free-field measurement.

Noise Measurement Results

Station: NMS-CA-6 Village House in Shek Mun Kap

Date Weather		Time	Measured	Measured	Measured	ΙΔ
Date	weather	Time	L _{eq(5mins)} dB(A)	L ₁₀ dB(A)	L _{so} dB(A)	L _{eq(30mins)} dB(A) [↑]
04-May-22	Sunny	11:15	50.2	52.8	44.2	
04-May-22	Sunny	11:20	50.7	53.3	44.6	
04-May-22	Sunny	11:25	53.1	55.1	44.9	50
04-May-22	Sunny	11:30	47.8	50.0	42.1	30
04-May-22	Sunny	11:35	45.9	47.8	42.7	
04-May-22	Sunny	11:40	48.1	51.3	42.7	
13-May-22	Cloudy	11:30	52.7	53.7	51.0	
13-May-22	Cloudy	11:35	53.3	55.4	51.6	
13-May-22	Cloudy	11:40	55.9	58.1	52.1	54
13-May-22	Cloudy	11:45	53.4	57.0	50.8	34
13-May-22	Cloudy	11:50	55.6	58.3	50.6	
13-May-22	Cloudy	11:55	52.4	53.9	50.6	
19-May-22	Cloudy	11:17	53.8	56.1	47.5	
19-May-22	Cloudy	11:22	50.2	53.2	47.1	
19-May-22	Cloudy	11:27	53.4	54.8	46.1	54
19-May-22	Cloudy	11:32	55.5	58.3	46.2	34
19-May-22	Cloudy	11:37	49.5	52.5	46.4	
19-May-22	Cloudy	11:42	57.8	62.6	45.3	
26-May-22	Cloudy	11:20	51.5	53.6	49.1	
26-May-22	Cloudy	11:25	48.7	50.0	46.9	
26-May-22	Cloudy	11:30	52.5	53.2	46.8	51
26-May-22	Cloudy	11:35	50.9	51.8	47.2	31
26-May-22	Cloudy	11:40	52.4	52.5	46.5	
26-May-22	Cloudy	11:45	48.4	50.5	45.5	
31-May-22	Cloudy	11:12	55.1	57.2	50.7	
31-May-22	Cloudy	11:17	52.9	55.3	49.0	
31-May-22	Cloudy	11:22	51.0	53.5	47.5	53
31-May-22	Cloudy	11:27	50.5	52.9	45.7	33
31-May-22	Cloudy	11:32	50.3	52.8	46.6	
31-May-22	Cloudy	11:37	55.4	58.3	47.5	

Remarks:
(^) +3dB (A) Façade correction included for free-field measurement.

Noise Measurement Results

Station: NMS-CA-7 YMCA of Hong Kong Christian College

Data	Date Weather		Measured	Measured	Measured	
Date	weather	Time	L _{eq(5mins)} dB(A)	L ₁₀ dB(A)	L _{so} dB(A)	L _{eq(30mins)} dB(A)
04-May-22	Sunny	09:19	61.8	63.7	56.6	
04-May-22	Sunny	09:24	63.6	66.6	57.2	
04-May-22	Sunny	09:29	62.2	63.8	57.3	62
04-May-22	Sunny	09:34	62.8	65.1	55.5	02
04-May-22	Sunny	09:39	60.8	62.5	55.2	
04-May-22	Sunny	09:44	61.6	63.4	55.9	
13-May-22	Cloudy	09:35	56.1	58.2	54.2	
13-May-22	Cloudy	09:40	56.6	59.2	54.0	
13-May-22	Cloudy	09:45	54.7	56.1	53.5	- 56
13-May-22	Cloudy	09:50	55.5	56.9	54.0	30
13-May-22	Cloudy	09:55	56.1	57.7	54.2	
13-May-22	Cloudy	10:00	55.7	57.2	53.9	
19-May-22	Cloudy	09:19	62.7	64.6	57.6	
19-May-22	Cloudy	09:24	60.8	63.4	57.0	
19-May-22	Cloudy	09:29	63.2	65.6	57.2	63
19-May-22	Cloudy	09:34	63.3	65.1	58.4	- 03
19-May-22	Cloudy	09:39	63.8	66.6	60.0	
19-May-22	Cloudy	09:44	63.2	65.9	59.3	
26-May-22	Cloudy	09:22	63.1	64.6	60.9	
26-May-22	Cloudy	09:27	62.8	63.9	61.0	
26-May-22	Cloudy	09:32	62.7	64.3	61.1	62
26-May-22	Cloudy	09:37	62.0	63.1	60.8	02
26-May-22	Cloudy	09:42	60.6	62.6	57.6	
26-May-22	Cloudy	09:47	58.5	59.4	56.9	
31-May-22	Cloudy	09:27	58.9	60.7	56.1	
31-May-22	Cloudy	09:32	58.3	59.2	56.0	
31-May-22	Cloudy	09:37	60.4	63.1	56.4	60
31-May-22	Cloudy	09:42	58.3	59.8	56.5	DU
31-May-22	Cloudy	09:47	58.0	59.2	55.9	
31-May-22	Cloudy	09:52	63.4	66.4	58.6	

Noise Measurement Results


Station: NMS-CA-8 Caritas Charles Vath College

Date	Weather	Time	Measured	Measured	Measured	
Date	weather	Time	L _{eq(5mins)} dB(A)	L ₁₀ dB(A)	L _{so} dB(A)	L _{eq(30mins)} dB(A)
04-May-22	Sunny	10:17	62.2	64.0	59.2	
04-May-22	Sunny	10:22	63.5	67.1	58.6	
04-May-22	Sunny	10:27	61.4	63.5	58.6	62
04-May-22	Sunny	10:32	62.8	66.0	58.8	02
04-May-22	Sunny	10:37	60.5	62.2	58.2	
04-May-22	Sunny	10:42	60.8	63.6	57.5	
13-May-22	Cloudy	10:29	58.3	60.4	55.7	
13-May-22	Cloudy	10:34	57.4	59.4	55.1	
13-May-22	Cloudy	10:39	58.2	59.7	56.3	57
13-May-22	Cloudy	10:44	57.2	58.5	55.7	37
13-May-22	Cloudy	10:49	56.8	59.2	54.2	
13-May-22	Cloudy	10:54	56.4	57.5	54.5	
19-May-22	Cloudy	10:16	62.7	65.3	58.7	
19-May-22	Cloudy	10:21	64.2	66.9	60.1	
19-May-22	Cloudy	10:26	61.2	64.3	56.9	63
19-May-22	Cloudy	10:31	63.3	66.2	56.7	03
19-May-22	Cloudy	10:36	62.5	64.8	56.2	
19-May-22	Cloudy	10:41	62.2	64.7	57.9	
26-May-22	Cloudy	10:19	59.5	60.7	57.9	
26-May-22	Cloudy	10:24	60.7	62.4	58.6	
26-May-22	Cloudy	10:29	60.6	62.6	57.8	62
26-May-22	Cloudy	10:34	64.6	67.3	61.0	62
26-May-22	Cloudy	10:39	63.6	65.3	60.6	
26-May-22	Cloudy	10:44	63.0	65.1	60.2	
31-May-22	Cloudy	10:10	61.4	64.4	56.5	
31-May-22	Cloudy	10:15	60.1	62.3	56.1	1
31-May-22	Cloudy	10:20	60.6	63.1	55.9	60
31-May-22	Cloudy	10:25	59.8	62.5	55.3	00
31-May-22	Cloudy	10:30	60.3	62.4	56.1	1
31-May-22	Cloudy	10:35	59.7	62.4	55.2	

Noise Measurement Results

Station: NMS-CA-9 Hong Chi Shiu Pong Morninghope School

Date Weather		Time	Measured	Measured	Measured	1 1974)
Date	weather	Time	$\mathbf{L}_{eq(Smins)} dB(A)$	L ₁₀ dB(A)	L ₉₀ dB(A)	$\mathbf{L}_{\text{eq(30mins)}} \text{dB(A)}$
04-May-22	Sunny	08:29	58.9	62.5	53.9	
04-May-22	Sunny	08:34	59.6	62.2	54.2	
04-May-22	Sunny	08:39	60.5	62.8	54.7	62
04-May-22	Sunny	08:44	60.9	64.7	52.3	62
04-May-22	Sunny	08:49	64.1	65.2	51.7	
04-May-22	Sunny	08:54	63.5	64.2	54.5	
13-May-22	Cloudy	08:38	58.5	59.7	54.2	
13-May-22	Cloudy	08:43	58.8	62.1	53.6	
13-May-22	Cloudy	08:48	60.6	65.1	53.6	59
13-May-22	Cloudy	08:53	57.3	59.4	54.5	39
13-May-22	Cloudy	08:58	57.3	59.2	53.6	
13-May-22	Cloudy	09:03	58.2	62.3	53.5	
19-May-22	Cloudy	08:29	60.9	64.1	54.9	
19-May-22	Cloudy	08:34	58.1	61.0	53.6	
19-May-22	Cloudy	08:39	58.9	61.3	53.6	60
19-May-22	Cloudy	08:44	58.0	60.5	53.6	60
19-May-22	Cloudy	08:49	61.5	65.2	55.4	
19-May-22	Cloudy	08:54	62.9	65.8	58.4	
26-May-22	Cloudy	08:31	62.0	65.3	57.7	
26-May-22	Cloudy	08:36	60.6	61.7	57.6	
26-May-22	Cloudy	08:41	61.8	63.6	57.6	61
26-May-22	Cloudy	08:46	59.3	61.1	56.7	61
26-May-22	Cloudy	08:51	61.1	62.5	59.0	
26-May-22	Cloudy	08:56	62.1	64.3	59.2	
31-May-22	Cloudy	08:42	59.9	62.6	55.5	
31-May-22	Cloudy	08:47	60.1	62.1	54.9	
31-May-22	Cloudy	08:52	62.9	64.7	59.7	61
31-May-22	Cloudy	08:57	62.9	65.1	60.5	01
31-May-22	Cloudy	09:02	61.1	63.4	56.4	
31-May-22	Cloudy	09:07	60.7	62.1	58.9	

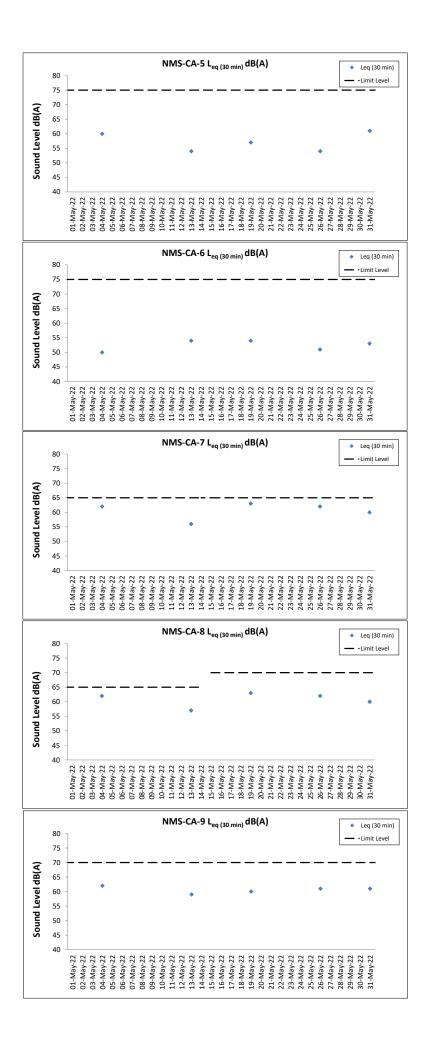

G5. Construction Noise Monitoring Event and Action Plan


Table G5.1: Event and Action Plan for Construction Noise

Event	Action								
	ET		IEC	;	ER		Co	ontractor	
Action Level Exceedance	1. 2. 3. 4.	Notify IEC, ER and Contractor; Carry out investigation; Report the results of investigation to the IEC, ER and Contractor; Discuss with the Contractor and formulate remedial measures; Increase monitoring frequency to check mitigation effectiveness.	 2. 3. 	Review the analysed results submitted by the ET; Review the proposed remedial measures by the Contractor and advise the ER accordingly; Supervise the implementation of remedial measures.	 2. 3. 4. 	Confirm receipt of notification of failure in writing; Notify Contractor; Require Contractor to propose remedial measures for the analysed noise problem; Ensure remedial measures are properly implemented	1.	Submit noise mitigation proposals to IEC and ER; Implement noise mitigation proposals.	
Limit Level Exceedance	1. 2. 3. 4. 5.	Identify source; Inform IEC, ER, EPD and Contractor; Repeat measurements to confirm findings; Increase monitoring frequency; Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; Inform IEC, ER and EPD the causes and actions taken for the exceedances; Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; If exceedance stops, cease additional monitoring.	 2. 3. 	Discuss amongst ER, ET, and Contractor on the potential remedial actions; Review Contractors remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; Supervise the implementation of remedial measures.	1. 2. 3. 4. 5.	Confirm receipt of notification of failure in writing; Notify Contractor; Require Contractor to propose remedial measures for the analysed noise problem; Ensure remedial measures properly implemented; If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated.	1. 2. 3. 4. 5.	Take immediate action to avoid further exceedance; Submit proposals for remedial actions to IEC within 3 working days of notification; Implement the agreed proposals; Resubmit proposals if problem still not under control; Stop the relevant portion of works as determined by the ER until the exceedance is abated.	

H. Water Quality

- **H1. Locations of Water Quality Monitoring Stations**
- **H2. Water Quality Monitoring Equipment Calibration Certificates**
- **H3. Water Quality Monitoring Schedule**
- **H4. Water Quality Monitoring Results**
- H5. Water Quality Monitoring Event and Action Plan

H1. Locations of Water Quality Monitoring Stations

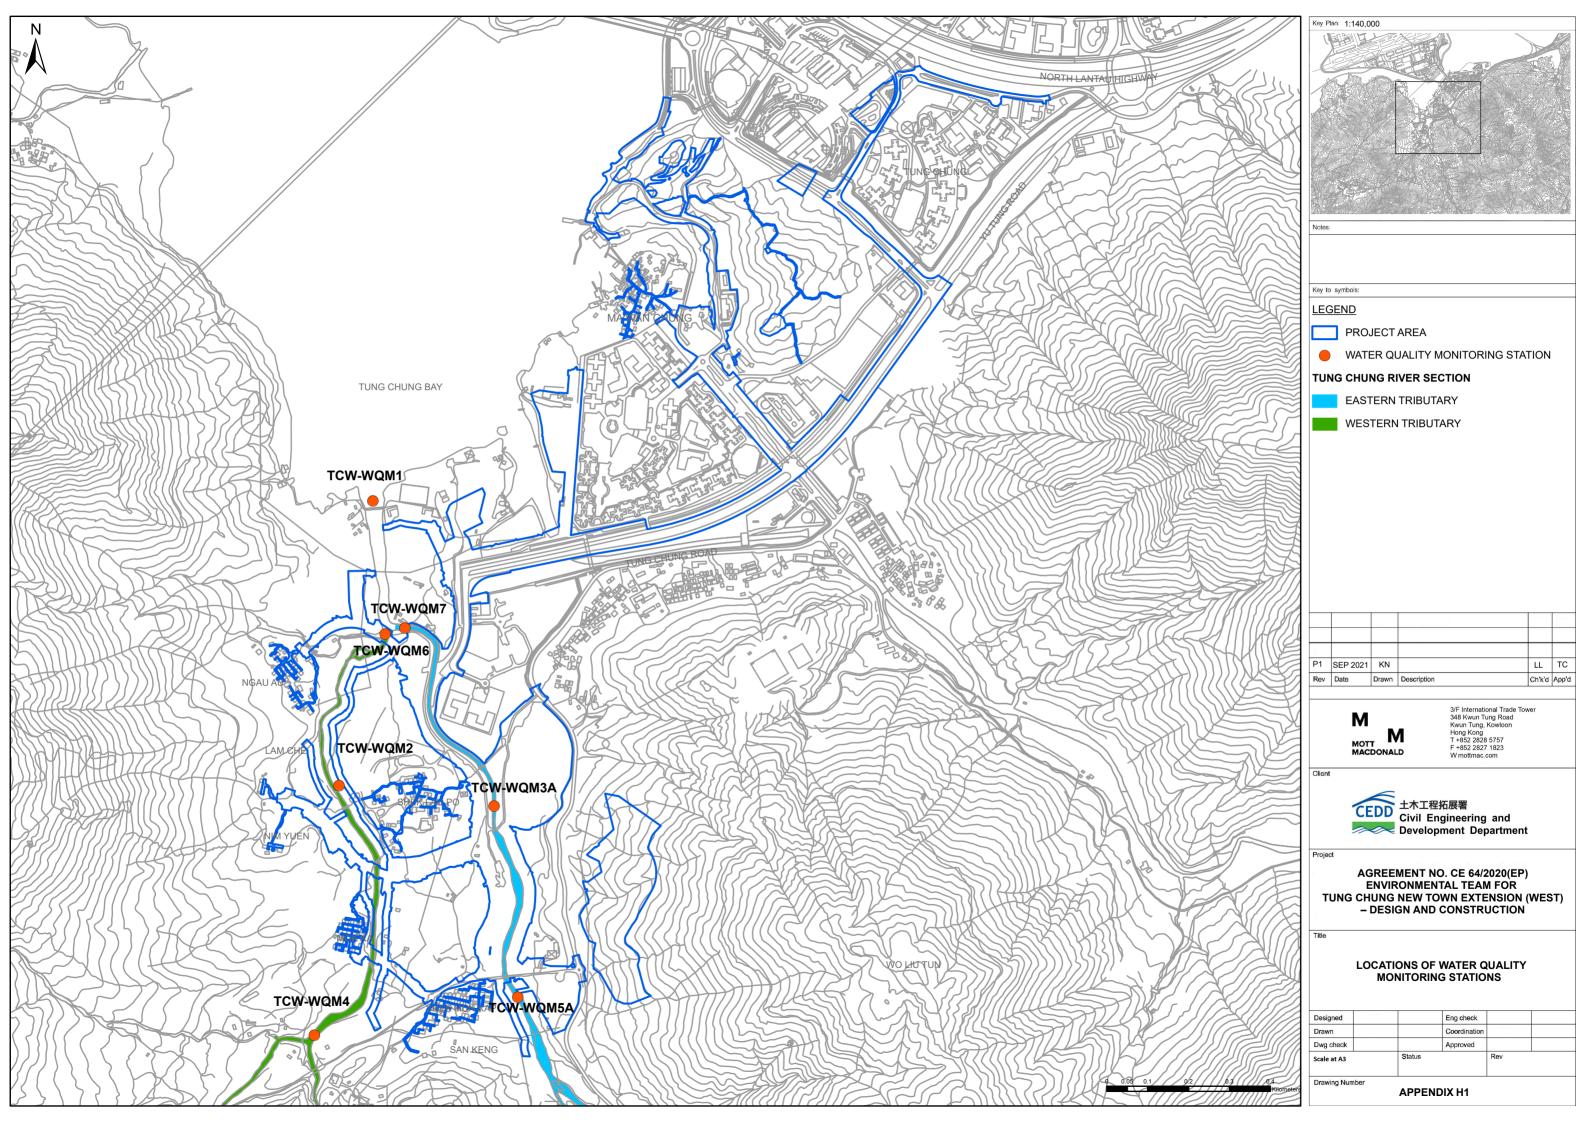

H2. Water Quality Monitoring Equipment Calibration Certificates



FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre 5 Lok Yi Street, Tai Lam Tuen Mun, NT Hong Kong

Report No.: 221149WA220558



Page 1 of 3

Report on Calibration of HORIBA Multifunction Meter

Information Supplied by Client

Client

: ENVIROTECH SERVICE COMPANY

Client's address

RM113, 1/F, MY LOFT, 9 HOI WING ROAD, TUEN MUN, N.T.,

HONG KONG

Calibration Item

Description

Multifunctional Meter

Manufacturer

HORIBA

Model

U-5000

Serial No.

.

Equipment No.

LUAVCDWU

Laboratory Information

Lab. sample ID

WA220558/1

Date sample received

18/03/2022

Date of calibration

21/03/2022

Next calibration date

20/06/2022

Test method used

In-house comparison method

Note: This report refers only to the sample(s) tested and the result(s) applied to the sample(s) as received.



FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre 5 Lok Yi Street, Tai Lam Tuen Mun, NT Hong Kong

Report No.: 221149WA220558

Page 2 of 3

Results:

A. pH calibration

	pH value at 25°C									
Theoretical	Measured	Deviation (pH value)	Maximum acceptable Deviation (pH value)							
4.0	3.90	-0.10								
7.0	7.01	+0.01	±0.20							
10.0	10.00	0.00								

B. Salinity calibration

	Salinity, ppt										
Theoretical	Measured	Deviation (%)	Maximum acceptable Deviation (%)								
0	0.03	-									
10	10.70	+7.0									
20	20.89	+4.5	±10.0								
30	30.80	+2.7									
40	40.65	+1.6									

C. Dissolved Oxygen calibration

Transcort ou oxygon o	. Diocontou Oxygon oundration									
	Dissolved oxygen content, mg/L									
Theoretical	Theoretical Measured Deviation (mg/L) Maximum acceptable Deviation (mg/L)									
4.85	4.89	+0.04								
6.95	6.80	-0.15	±0.20							
8.26	8.41	+0.15								

Certified by :

Approved Signatory : CHAN Hoi Yan, Winnie

Assistant Manager

Date : 24

Note: This report refers only to the sample(s) tested and the result(s) applied to the sample(s) as received.



FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre 5 Lok Yi Street, Tai Lam Tuen Mun, NT Hong Kong

Report No.: 221149WA220558

Page 3 of 3

Results:

D. Temperature calibration

	Tempe	rature, °C	
Thermometer reading	Measured	Deviation (°C)	Maximum acceptable Deviation (°C)
10.5	10.21	-0.29	
20.3	20.53	+0.23	±2.0
40.2	39.99	-0.21	

E. Turbidity calibration

	Turbidit	ty, N.T.U.	
Theoretical	Measured	Deviation (%)	Maximum acceptable Deviation (%)
0	0.18	-	
4	3.98	-0.5	
40	39.5	-1.3	±10.0
80	80.6	+0.8	±10.0
400	398	-0.5	
800	803	+0.4	

F. Conductivity calibration

num acceptable eviation (%)
±10.0

Certified by :

Approved Signatory: CHAN Hoi Yan, Winnie

Assistant Manager

Date

** End of Report **

Note: This report refers only to the sample(s) tested and the result(s) applied to the sample(s) as received.

H3. Water Quality Monitoring Schedule

May 2022 - Impact Monitoring Schedule for Tung Chung West

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
1	2	3	4	5	6	7
		Water (14:30)		Water (15:30)		Water (16:30)
8	9	10	11	12	13	14
	,	10		12		17
		Water (17:00)		Water (10:30)		Water (11:00)
15	16	17	18	19	20	21
	Water (13:00)		Water (14:30)		Water (15:30)	
	vvater (15.00)		vvator (14.00)		Water (10.00)	
22	23	24	25	26	27	28
	Water (09:00)		Water (10:00)		Water (11:30)	
	, ,		,			
29	30	31				
	Water (14:00)					
ntes:						

Notes:

Impact Water Quality Monitoring Stations:

TCW-WQM1 - Downstream of Tung Chung Stream

Tung Chung Stream (West)

TCW-WQM2 - Middle of Tung Chung Stream (West)
TCW-WQM4 - Upstream of Tung Chung Stream (West)
TCW-WQM6 - Downstream of Tung Chung Stream (West)

Tung Chung Stream (East)

TCW-WQM3A - Middle of Tung Chung Stream (East) [aka Upstream of River Park]


TCW-WQM5A - Upstream of Tung Chung Stream (East)


TCW-WQM7 - Downstream of Tung Chung Stream (East) [aka Downstream of River Park]


Remark:

Water quality monitoring is arranged at the ebb tide of each monitoring day. Tidal information refers to Chek Lap Kok East provided by the Hong Kong Observatory.

H4. Water Quality Monitoring Results









Note: The Action and Limit Level of dissolved oxygen can be referred to Table 4.3 of the monthly EM&A report.


Major site activities carried out during the reporting period are summarized in Section 1.4 of the monthly EM&A report.

Weather conditions during monitoring are presented in the data tables above.

QA/ QC requirements as stipulated in the EM&A Manual were carried out during measurement.









Note: The Action and Limit Level of turbidity can be referred to Table 4.3 of the monthly EM&A report.


Major site activities carried out during the reporting period are summarized in Section 1.4 of the monthly EM&A report.

Weather conditions during monitoring are presented in the data tables above.

QA/ QC requirements as stipulated in the EM&A Manual were carried out during measurement.







Note: The Action and Limit Level of suspended solids can be referred to Table 4.3 of the monthly EM&A report.

Major site activities carried out during the reporting period are summarized in Section 1.4 of the monthly EM&A report.

Weather conditions during monitoring are presented in the data tables above.

QA/ QC requirements as stipulated in the EM&A Manual were carried out during measurement.

Water Quality Monitoring Results on 03 May 2022 during Ebb Tide

Monitoring Station	Weather	Tidal Condition	Sampling	Replicate	Water Te			Н	Salinit	y (ppt)	Condo (µS	uctivity /cm)	DO Satu	ration (%)	Dissolved (mg	d Oxygen g/L)	Turbidi	ty(NTU)		led Solids g/L)
	Condition	Tradi Corrainon	Time	rtopiloato	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average
TCW-WQM1	Common	Dough	14:19	1st	25.8	25.8	8.6	8.6	24.67	24.67	38800	38800	108.3	108.3	7.7	7.7	9.5	9.4	1.8	1.8
TCVV-VVQIVIT	Sunny	Rough	14.19	2nd	25.8	25.0	8.6	0.0	24.67	24.07	38800	30000	108.2	100.3	7.7	7.7	9.3	9.4	1.7	1.0
TOW WOMO	Cummu	NA	10.10	1st	22.7	22.7	6.7	6.7	0.04	0.04	78	79	53.0	56.1	4.6	4.0	1.3	1.3	1.1	1.1
TCW-WQM2	Sunny	INA	12:13	2nd	22.7	22.1	6.7	0.7	0.04	0.04	79	79	59.1	30.1	5.1	4.9	1.2	1.3	1.1	1.1
TOW WOMON	Commen	NA	44.24	1st	23.1	23.1	6.9	6.0	0.04	0.04	90	90	70.6	71.9	6.1	6.0	2.8	2.9	1.4	4.5
TCW-WQM3A	Sunny	NA NA	11:34	2nd	23.1	23.1	6.9	6.9	0.04	0.04	89	90	73.1	71.9	6.3	6.2	2.9	2.9	1.6	1.5
TOW WOMA	Cummu	NA	10:26	1st	21.8	21.8	6.4	6.4	0.02	0.02	43	44	57.9	58.0	5.1	5.1	1.7	1.6	0.6	0.6
TCW-WQM4	Sunny	NA NA	10:26	2nd	21.8	21.8	6.4	0.4	0.02	0.02	44	44	58.0	58.0	5.1	5.1	1.4	1.0	0.6	0.6
TCW-WQM5A	Cummu	NA	10:55	1st	22.6	22.6	7.2	7.2	0.02	0.02	40	40	91.1	92.0	7.9	8.0	1.1	1.1	0.7	0.7
TCVV-VVQIVISA	Sunny	NA NA	10:55	2nd	22.6	22.0	7.2	1.2	0.02	0.02	40	40	92.9	92.0	8.0	8.0	1.1	1.1	0.6	0.7
TCW-WQM6	Cummu	NA	40.47	1st	22.6	22.6	6.6	6.6	0.05	0.05	104	104	76.7	76.5	6.6	6.6	1.3	1.3	0.8	0.9
TCVV-VVQIVIO	Sunny	NA NA	12:47	2nd	22.6	22.0	6.6	0.0	0.05	0.05	104	104	76.2	70.5	6.6	0.0	1.2	1.3	0.9	0.9
TCW-WQM7	Commen	NIA.	40.07	1st	29.0	28.9	9.4	0.4	0.04	0.04	98	00	114.5	444.0	8.8	0.0	2.4	2.2	3.7	3.6
TCVV-VVQIVI7	Sunny	NA	13:27	2nd	28.9	26.9	9.4	9.4	0.04	0.04	98	98	114.7	114.6	8.8	8.8	2.1	2.3	3.4	3.0

Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

NA: This monitoring location is not subject to tidal effect.

Water Quality Monitoring Results on 05 May 2022 during Ebb Tide

Monitoring Station	Weather	Tidal Condition	Sampling	Replicate	Water Te	mperature °C)	р	Н	Salinit	y (ppt)	Cond (µS	uctivity /cm)	DO Satur	ation (%)	Dissolved (mg	d Oxygen g/L)	Turbidit	y(NTU)		ded Solids ig/L)
	Condition		Time		Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average
TOWN MONA	Common	Davish	45.00	1st	27.0	27.0	8.7	0.7	24.56	24.54	38600	- 38600	143.1	140.4	9.9	9.8	7.7	7.8	1.2	4.0
TCW-WQM1	Sunny	Rough	15:00	2nd	27.1	27.0	8.7	8.7	24.52	24.54	38600	38600	137.7	140.4	9.6	9.8	7.8	7.8	1.1	1.2
TOWNSON	0	NIA	40:40	1st	24.4	04.0	6.7	0.7	0.02	0.00	39	40	65.7	05.7	5.5		1.3	4.0	0.8	
TCW-WQM2	Sunny	NA	12:18	2nd	24.3	24.3	6.7	6.7	0.02	0.02	41	40	65.6	65.7	5.5	5.5	1.2	1.3	0.9	0.9
TOW MONTO A			44.40	1st	25.0	05.0	7.1	7.4	0.04	0.04	78	70	79.1	70.0	6.5	0.0	1.2	4.0	1.4	1.0
TCW-WQM3A	Sunny	NA	11:46	2nd	25.0	25.0	7.1	7.1	0.04	0.04	79	79	80.5	79.8	6.7	6.6	1.4	1.3	1.2	1.3
TOW WORLD	0	NIA	10.00	1st	22.8	00.0	6.5	0.5	0.03	0.00	59	50	43.3	40.0	3.7	0.7	1.6	4.0	<0.5	0.5
TCW-WQM4	Sunny	NA	10:23	2nd	22.8	22.8	6.5	6.5	0.03	0.03	58	- 59	42.7	43.0	3.7	3.7	1.5	1.6	<0.5	<0.5
TOWN MONATA	Common	NIA	10.40	1st	24.5	24.5	7.4	7.4	0.02	0.00	43	40	87.1	07.5	7.3	7.0	1.7	1.7	0.7	0.7
TCW-WQM5A	Sunny	NA	10:48	2nd	24.5	24.5	7.4	7.4	0.02	0.02	43	43	87.9	87.5	7.3	7.3	1.7	1.7	0.6	0.7
TOWNSON	0	NIA	40.50	1st	24.3	04.0	6.7	0.7	0.21	0.04	436	400	67.5	07.5	5.6	5.0	0.7	0.7	0.8	
TCW-WQM6	Sunny	NA	13:56	2nd	24.3	24.3	6.7	6.7	0.21	0.21	441	439	67.5	67.5	5.6	5.6	0.7	0.7	0.8	0.8
TOW MON47	Commi	NIA	12.10	1st	32.8	22.0	10.3	40.2	0.06	0.00	129	400	118.5	445.0	8.5	0.0	1.5	4.0	2.2	2.0
TCW-WQM7	Sunny	NA	13:40	2nd	32.8	32.8	10.3	10.3	0.06	0.06	127	128	112.7	115.6	8.1	8.3	1.6	1.6	2.1	2.2

Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

NA: This monitoring location is not subject to tidal effect.

Water Quality Monitoring Results on 07 May 2022 during Ebb Tide

Monitoring Station	Weather	Tidal Condition	Sampling	Replicate	Water Te	mperature °C)	р	Н	Salinit	y (ppt)	Cond (µS	uctivity /cm)	DO Satur	ation (%)	Dissolved (mg	d Oxygen g/L)	Turbidit	y(NTU)		ded Solids g/L)
	Condition		Time		Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average
TCW-WQM1	Clavely	Davish	16:00	1st	28.2	28.2	8.8	8.8	22.95	22.97	36300	36350	150.0	155.0	10.3	10.7	9.4	9.3	1.4	1.3
TCVV-VVQIVIT	Cloudy	Rough	16.00	2nd	28.2	20.2	8.8	0.0	22.98	22.91	36400	30330	160.0	155.0	11.0	10.7	9.1	9.3	1.2	1.3
TOWNSON	Delini	NIA	40.50	1st	25.2	05.0	6.7	0.7	0.02	0.00	40	40	44.7	44.4	3.7	0.7	1.6	4.0	1.1	4.4
TCW-WQM2	Rainy	NA	13:58	2nd	25.3	25.3	6.7	6.7	0.02	0.02	40	40	44.0	44.4	3.6	3.7	1.5	1.6	1.1	1.1
TOW MONTO A	01 1		10.00	1st	25.9	05.0	7.2	7.0	0.04	0.04	78	70	79.3	00.0	6.4	0.5	1.3	4.0	1.2	1.0
TCW-WQM3A	Cloudy	NA	13:03	2nd	25.9	25.9	7.2	7.2	0.04	0.04	77	78	81.3	80.3	6.6	6.5	1.2	1.3	1.4	1.3
TOW WORLD	Olevert	NIA	44.47	1st	23.7	00.7	6.5	0.5	0.03	0.00	63	00	42.7	40.5	3.6	0.0	1.2	4.0	<0.5	0.5
TCW-WQM4	Cloudy	NA	11:47	2nd	23.7	23.7	6.5	6.5	0.03	0.03	62	- 63	42.3	42.5	3.6	3.6	1.3	1.3	<0.5	<0.5
TOWN MONATA	Clavely	NIA	10.11	1st	25.9	25.0	7.5	7.5	0.02	0.02	44	44	88.4	07.0	7.2	7.4	1.4	4.5	0.5	0.5
TCW-WQM5A	Cloudy	NA	12:11	2nd	25.9	25.9	7.5	7.5	0.02	0.02	44	44	86.2	87.3	7.0	7.1	1.5	1.5	0.5	0.5
TOWN MONE	Dainu	NIA	4.4.24	1st	24.4	24.4	6.5	0.5	0.02	0.02	54	F.4	63.6	63.2	5.3	F 2	1.5	1.6	0.7	0.7
TCW-WQM6	Rainy	NA	14:31	2nd	24.4	24.4	6.5	6.5	0.02	0.02	54	- 54	62.8	63.2	5.3	5.3	1.6	1.0	0.7	0.7
TOW MOM	Dainu	NIA	45.04	1st	27.5	27.5	9.9	0.0	0.04	0.04	98	00	123.4	100.7	9.7	0.7	1.5	4.0	0.9	0.0
TCW-WQM7	Rainy	NA	15:01	2nd	27.6	27.5	9.9	9.9	0.04	0.04	98	- 98	122.0	122.7	9.6	9.7	1.6	1.6	0.8	0.9

Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

NA: This monitoring location is not subject to tidal effect.

Water Quality Monitoring Results on 10 May 2022 during Ebb Tide

Monitoring Station	Weather	Tidal Condition	Sampling	Replicate	Water Te	mperature 'C)	р	Н	Salinit	y (ppt)	Cond (µS	uctivity /cm)	DO Satur	ation (%)	Dissolved (mg	d Oxygen g/L)	Turbidi	ty(NTU)		led Solids g/L)
	Condition		Time		Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average
TCW-WQM1	Rainy	Rough	16:37	1st	27.5	27.5	8.6	8.6	24.55	24.55	38600	38600	125.4	127.9	8.6	8.8	4.5	4.5	1.4	1.3
1CVV-VVQIVIT	Railly	Kougii	10.37	2nd	27.5	21.5	8.6	0.0	24.55	24.55	38600	30000	130.3	127.9	9.0	0.0	4.5	4.5	1.2	1.3
TCW-WQM2	Cloudy	NA	14:30	1st	24.8	24.8	6.6	6.6	0.02	0.02	39	39	52.6	52.1	4.4	4.4	1.8	1.8	0.6	0.7
TCVV-VVQIVIZ	Cloudy	INA	14.30	2nd	24.8	24.0	6.6	0.0	0.02	0.02	39	- 39	51.5	52.1	4.3	4.4	1.7	1.0	0.8	0.7
TOW MONAGA	Clavely	NA	14:01	1st	25.5	25.5	7.2	7.2	0.04	0.04	78	78	79.3	79.6	6.5	6.5	1.3	1.3	0.7	0.8
TCW-WQM3A	Cloudy	INA	14.01	2nd	25.5	25.5	7.2	1.2	0.04	0.04	78	70	79.9	79.6	6.5	0.5	1.3	1.3	0.8	0.8
TOWN MONA	Clavely	NIA	10.55	1st	23.8	22.0	6.4	C 4	0.03	0.00	59	50	50.7	40.0	4.3	4.0	1.4	4.4	0.5	0.5
TCW-WQM4	Cloudy	NA	12:55	2nd	23.9	23.8	6.4	6.4	0.03	0.03	58	- 59	46.8	48.8	4.0	4.2	1.4	1.4	0.5	0.5
TCW-WQM5A	Clavely	NA	13:22	1st	25.5	25.5	7.4	7.4	0.02	0.02	44	44	84.3	84.4	6.9	6.9	1.5	1.5	0.6	0.6
TCW-WQM5A	Cloudy	INA .	13:22	2nd	25.5	25.5	7.4	7.4	0.02	0.02	44	44	84.5	84.4	6.9	0.9	1.5	1.5	0.5	0.6
TCW-WQM6	Clavely	NA	14:57	1st	24.5	24.5	6.6	6.6	0.02	0.02	54	54	56.9	56.5	4.8	4.8	1.3	1.3	0.8	0.9
TCVV-VVQIVI6	Cloudy	INA .	14:57	2nd	24.5	24.5	6.6	0.0	0.02	0.02	53	54	56.0	50.5	4.7	4.8	1.3	1.3	0.9	0.9
TOWNAMA	Dainu	NIA	45.45	1st	26.6	20.0	9.1	0.1	0.04	0.04	93	00	97.0	00.0	7.8	7.0	1.5	4.5	1.1	4.4
TCW-WQM7	Rainy	NA	15:15	2nd	26.6	26.6	9.1	9.1	0.04	0.04	93	- 93	96.6	96.8	7.8	7.8	1.5	1.5	1.1	1.1

Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

NA: This monitoring location is not subject to tidal effect.

Water Quality Monitoring Results on 12 May 2022 during Ebb Tide

Monitoring Station	Weather	Tidal Condition	Sampling	Replicate	Water Te	mperature °C)	р	Н	Salinit	y (ppt)		uctivity /cm)	DO Satur	ation (%)	Dissolved (mg	d Oxygen g/L)	Turbidit	y(NTU)		led Solids g/L)
	Condition		Time		Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average
TOWN MONA	Dainu	Dough	10:27	1st	23.6	23.6	7.3	7.3	0.07	0.07	140	142	84.5	84.5	7.2	7.2	12.1	12.1	9.5	0.7
TCW-WQM1	Rainy	Rough	10:27	2nd	23.6	23.0	7.3	7.3	0.07	0.07	143	142	84.5	84.5	7.2	1.2	12.1	12.1	9.9	<u>9.7</u>
TOWNAMO	Deline	NIA	44.40	1st	23.2	00.0	6.9	0.0	0.01	0.04	35	05	90.7	00.0	7.7	7.0	3.5	0.7	3.5	0.5
TCW-WQM2	Rainy	NA	11:13	2nd	23.2	23.2	6.9	6.9	0.01	- 0.01	35	35	91.1	90.9	7.8	7.8	3.9	3.7	3.4	3.5
TOW MONTO A			10.05	1st	24.1	04.4	7.2	7.0	0.04	0.04	83	00	92.3	00.0	7.8	7.0	19.8	40.7	26.7	00.4
TCW-WQM3A	Rainy	NA	12:05	2nd	24.1	24.1	7.2	7.2	0.04	0.04	83	- 83	92.9	92.6	7.8	7.8	19.5	<u>19.7</u>	26.1	<u>26.4</u>
TOWNSONA	Deline	NIA	10:00	1st	23.4	00.4	7.1	7.4	0.01	0.04	30	00	77.8	70.0	6.6	0.0	3.8	0.0	2.8	0.0
TCW-WQM4	Rainy	NA	12:30	2nd	23.4	23.4	7.0	7.1	0.01	0.01	29	30	81.4	79.6	6.9	6.8	3.8	3.8	3.1	3.0
TOW MONTA	Dainu	NIA	10.50	1st	24.2	24.2	5.8	o	0.01	0.04	23	22	60.3	50.0	5.1	5.0	15.1	45.4	20.9	20.7
TCW-WQM5A	Rainy	NA	12:56	2nd	24.2	24.2	5.8	5.8	0.01	0.01	23	- 23	58.8	59.6	4.9	5.0	15.1	15.1	20.5	20.7
TCW-WQM6	Dainu	NA	09:29	1st	23.3	23.3	7.1	7.1	0.02	0.02	44	44	97.8	97.6	8.3	8.3	4.7	5.0	3.6	3.9
TCVV-VVQIVI6	Rainy	INA	09:29	2nd	23.3	23.3	7.1	7.1	0.02	0.02	44	44	97.4	97.6	8.3	8.3	5.2	5.0	4.1	3.9
TOW MOM	Dainu	NIA	00.54	1st	24.0	24.0	7.1	7.4	0.04	0.04	91	00	80.1	70.7	6.7	0.7	5.6	F.0	6.8	7.0
TCW-WQM7	Rainy	NA	09:54	2nd	24.0	24.0	7.1	7.1	0.04	0.04	93	92	79.2	79.7	6.7	6.7	5.6	5.6	7.2	7.0

Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

NA: This monitoring location is not subject to tidal effect.

Water Quality Monitoring Results on 14 May 2022 during Ebb Tide

Monitoring Station	Weather	Tidal Condition	Sampling	Replicate	Water Te	mperature °C)	р	Н	Salinit	y (ppt)	Cond (µS	uctivity /cm)	DO Satur	ation (%)	Dissolved (mg	d Oxygen g/L)	Turbidit	y(NTU)		led Solids g/L)
	Condition		Time		Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average
TOWN MONA	Clavely	Davish	40.47	1st	24.1	24.1	7.2	7.0	5.04	F 02	9030	9005	83.1	83.2	6.8	6.0	2.5	2.6	0.8	0.0
TCW-WQM1	Cloudy	Rough	10:47	2nd	24.1	24.1	7.2	7.2	5.01	5.03	8980	9005	83.3	83.2	6.8	6.8	2.6	2.0	0.9	0.9
TOWNSONS	Olevert	NIA	44.00	1st	23.3	00.0	7.0	7.0	0.02	0.00	41	40	90.4	00.0	7.7	7.7	1.1	4.0	0.9	0.0
TCW-WQM2	Cloudy	NA	11:23	2nd	23.3	23.3	7.0	7.0	0.02	0.02	39	40	88.7	89.6	7.6	7.7	1.3	1.2	0.8	0.9
TOW MONTO A	01 1		44.50	1st	23.8	00.0	7.0	7.0	0.03	0.00	65	0.5	91.3	24.0	7.7		2.5	0.4	1.5	4.5
TCW-WQM3A	Cloudy	NA	11:56	2nd	23.8	23.8	7.0	7.0	0.03	0.03	65	65	91.2	91.3	7.7	7.7	2.3	2.4	1.4	1.5
TOWNSONA	Olevert	NIA	40.00	1st	23.7	00.7	6.2	0.0	0.01	0.04	33	00	66.9	00.0	5.7	5.7	1.3	4.0	0.6	0.0
TCW-WQM4	Cloudy	NA	12:28	2nd	23.7	23.7	6.2	6.2	0.01	0.01	33	- 33	65.5	66.2	5.6	5.7	1.3	1.3	0.5	0.6
TOWN MONATA	Clavely	NIA	40.54	1st	23.8	22.7	6.7	0.7	0.01	0.04	32	22	96.6	00.5	8.2	0.0	2.5	2.6	1.2	4.0
TCW-WQM5A	Cloudy	NA	12:54	2nd	23.7	23.7	6.7	6.7	0.01	0.01	32	32	96.3	96.5	8.2	8.2	2.6	2.6	1.4	1.3
TOWN MONE	Clavely	NIA	00.50	1st	23.3	23.3	6.9	0.0	0.02	0.02	44	44	99.6	99.1	8.5	8.5	1.2	1.2	1.5	1.4
TCW-WQM6	Cloudy	NA	09:59	2nd	23.3	23.3	6.9	6.9	0.02	0.02	44	44	98.5	99.1	8.4	8.5	1.2	1.2	1.3	1.4
TOW MOM	Clavely	NIA	10:00	1st	24.0	24.0	7.3	7.0	0.04	0.04	87	07	93.8	04.4	7.9	0.0	2.2	2.2	1.5	4.6
TCW-WQM7	Cloudy	NA	10:09	2nd	24.0	24.0	7.3	7.3	0.04	0.04	87	- 87	94.4	94.1	8.0	- 8.0	2.2	2.2	1.7	1.6

Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

NA: This monitoring location is not subject to tidal effect.

Water Quality Monitoring Results on 16 May 2022 during Ebb Tide

Monitoring Station	Weather	Tidal Condition	Sampling	Replicate	Water Te	mperature °C)	р	Н	Salinit	y (ppt)	Cond (µS	uctivity /cm)	DO Satur	ation (%)	Dissolved (mg	d Oxygen g/L)	Turbidi	ty(NTU)		ded Solids g/L)
	Condition		Time		Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average
TCW-WQM1	Rainy	Rough	12:45	1st	25.1	25.1	7.9	7.9	21.61	21.63	34400	34450	56.6	56.4	4.1	4.1	3.6	3.4	1.5	1.5
TCVV-VVQIVIT	Kalliy	Kougii	12.45	2nd	25.1	23.1	7.9	7.9	21.65	21.03	34500	34430	56.1	30.4	4.1	4.1	3.2	3.4	1.5	1.5
TCW-WQM2	Rainy	NA	10:21	1st	21.8	21.8	6.9	6.9	0.02	0.02	36	- 36	91.9	91.4	8.1	8.1	1.4	1.4	0.7	0.8
TCVV-VVQIVIZ	Kalliy	INA	10.21	2nd	21.8	21.0	6.9	6.9	0.02	0.02	36	- 30	90.9	91.4	8.0	0.1	1.4	1.4	0.8	0.8
TOW MONAGA	Daine	NA	09:38	1st	22.0	22.0	7.0	7.0	0.03	0.03	62	- 62	94.4	94.4	8.3	8.3	1.6	1.6	1.3	- 1.4
TCW-WQM3A	Rainy	INA INA	09:38	2nd	22.0	22.0	7.0	7.0	0.03	0.03	62	62	94.3	94.4	8.2	8.3	1.6	1.0	1.4	1.4
TCW-WQM4	Rainy	NA	08:37	1st	22.5	22.5	6.2	6.1	0.02	0.02	39	39	81.5	81.4	7.1	7.1	1.3	1.4	0.5	0.6
TCVV-VVQIVI4	Kalliy	INA	06.37	2nd	22.5	22.5	6.1	0.1	0.02	0.02	38	39	81.3	01.4	7.0	1 7.1	1.4	1.4	0.6	0.6
TCW-WQM5A	Rainy	NA	09:06	1st	21.9	21.9	6.5	6.5	0.01	0.01	32	32	92.4	92.2	8.1	8.1	1.4	1.4	1.5	1.5
TCW-WQWBA	Kalliy	INA	09.06	2nd	21.9	21.9	6.5	6.5	0.01	0.01	32	32	91.9	92.2	8.0	0.1	1.3	1.4	1.4	1.5
TCW-WQM6	Rainy	NA	11:04	1st	21.9	21.9	6.6	6.6	0.02	0.02	47	47	88.4	89.6	7.7	7.8	1.7	1.7	1.3	1.4
TCVV-VVQIVIO	Kalliy	INA	11.04	2nd	21.9	21.9	6.6	0.0	0.02	0.02	46	47	90.7	09.0	7.9	7.0	1.7	1.7	1.4	1.4
TCW-WQM7	Doiny	NA	11:36	1st	22.7	22.7	7.2	7.2	0.05	0.05	110	110	84.5	84.1	7.3	7.3	2.9	2.9	1.7	- 1.8
1 CVV-VV QIVI7	Rainy	IVA	11.30	2nd	22.7	22.1	7.3	1.2	0.05	0.05	109	110	83.6	04.1	7.2	1.3	2.9	2.9	1.8	1.0

Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

NA: This monitoring location is not subject to tidal effect.

Water Quality Monitoring Results on 18 May 2022 during Ebb Tide

Monitoring Station	Weather	Tidal Condition	Sampling	Replicate	Water Te	mperature 'C)	р	Н	Salinit	y (ppt)	Condi (µS	uctivity /cm)	DO Satur	ation (%)	Dissolved (mg	d Oxygen g/L)	Turbidi	ty(NTU)		ded Solids g/L)
	Condition		Time		Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average
TCW-WQM1	Cloudy	Rough	14:20	1st	26.1	26.0	8.0	8.0	22.08	22.09	35100	35100	58.6	57.4	4.2	4.1	3.5	3.4	2.1	2.2
1CVV-VVQIVIT	Cloudy	Kougii	14.20	2nd	26.0	20.0	8.0	6.0	22.10	22.09	35100	33100	56.1	37.4	4.0	4.1	3.3	3.4	2.3	2.2
TCW-WQM2	Cloudy	NA	12:19	1st	22.8	22.8	6.8	6.8	0.05	0.05	107	107	62.2	60.2	5.4	5.2	1.4	1.4	0.6	0.6
TCVV-VVQIVIZ	Cloudy	INA	12.19	2nd	22.9	22.0	6.8	0.0	0.05	0.05	107	107	58.2	60.2	5.0	5.2	1.4	1.4	0.6	0.6
TOW MONAGA	Clavely	NA	12:00	1st	22.9	22.9	7.1	7.1	0.03	0.03	61	C4	96.9	96.9	8.3	8.3	1.2	4.0	0.8	- 0.8
TCW-WQM3A	Cloudy	INA .	12:00	2nd	22.9	22.9	7.2	7.1	0.03	0.03	61	61	96.8	96.9	8.3	8.3	1.2	1.2	0.8	0.8
TCW-WQM4	Clavely	NA	44.44	1st	22.3	22.3	6.5	6.5	0.02	0.02	50	50	56.6	58.7	4.9	5.1	1.3	1.5	0.6	0.6
TCVV-VVQIVI4	Cloudy	INA .	11:14	2nd	22.3	22.3	6.5	0.5	0.02	0.02	49	50	60.8	58.7	5.3	5.1	1.6	1.5	<0.5	0.6
TCW-WQM5A	Clavely	NA	11:36	1st	22.5	22.5	6.7	6.7	0.01	0.01	33	33	86.9	86.9	7.5	7.5	1.6	1.6	0.8	0.8
TCVV-VVQIVISA	Cloudy	INA .	11:36	2nd	22.5	22.5	6.7	6.7	0.01	0.01	33	33	86.8	86.9	7.5	7.5	1.6	1.0	0.7	0.8
TCW-WQM6	Clavely	NA	12:56	1st	22.9	22.9	6.8	6.8	0.22	0.22	453	454	86.6	86.2	7.4	7.4	1.4	1.3	1.2	1.3
TCVV-VVQIVIO	Cloudy	INA .	12:56	2nd	22.9	22.9	6.8	0.8	0.22	0.22	455	454	85.8	86.2	7.4	7.4	1.1	1.3	1.4	1.3
TOW MOM7	Clavely	NIA	12.07	1st	26.7	20.7	7.0	7.0	0.19	0.40	390	200	76.6	70.0	6.1	6.4	2.5	2.4	1.4	4.0
TCW-WQM7	Cloudy	NA	13:07	2nd	26.7	26.7	7.0	7.0	0.18	0.19	389	390	75.8	76.2	6.1	6.1	2.3	2.4	1.2	1.3

Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

NA: This monitoring location is not subject to tidal effect.

Water Quality Monitoring Results on 20 May 2022 during Ebb Tide

Monitoring Station	Weather	Tidal Condition	Sampling	Replicate	Water Te	mperature C)	р	Н	Salinit	y (ppt)	Cond (µS	uctivity /cm)	DO Satu	ration (%)	Dissolved (mg	d Oxygen g/L)	Turbidi	ty(NTU)		led Solids g/L)
	Condition		Time	. rop.iodio	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average
TCW-WQM1	Sunny	Rough	15:04	1st	28.1	28.1	8.3	8.3	20.27	20.33	32500	32600	108.8	108.4	7.6	7.6	4.3	4.3	1.1	1.2
TCVV-VVQIVIT	Suring	Rough	15.04	2nd	28.2	20.1	8.3	0.5	20.39	20.33	32700	32000	108.0	100.4	7.5	7.0	4.2	4.3	1.3	1.2
TCW-WQM2	Sunny	NIA	13:02	1st	25.5 25.5	25.5	6.9	6.9	0.02	0.02	51	51	52.9	53.4	4.3	4.4	1.3	4.4	0.6	0.6
		NA	13.02	2nd		25.5	7.0	0.9	0.02	0.02	50	51	53.8	55.4	4.4	4.4	1.4	1.4	0.5	0.6
TOWN MONAGA	Common	NA	10:10	1st	26.0	26.1	7.2	7.2	0.02	0.02	55	50	94.2	94.0	7.6	7.6	1.8	1.8	0.7	0.8
TCW-WQM3A	Sunny	INA	12:19	2nd	26.1	20.1	7.2	7.2	0.02	0.02	56	56	93.7	94.0	7.6	7.0	1.7	1.8	0.8	0.8
TOW MONA	Sunny	NA	44.47	1st	23.7 23.6	00.0	6.4	0.4	0.02	0.00	52	50	57.6	57.5	4.9	4.0	1.2	4.0	<0.5	<0.5
TCW-WQM4			11:17	2nd		23.6	6.4	6.4	0.02	0.02	53	53	57.3	57.5	4.9	4.9	1.4	1.3	<0.5	70.5
TOWN MONATA	0	NIA	44.40	1st	25.7	05.7	7.0	7.0	0.01	0.04	35	05	87.1	07.0	7.1	7.4	1.2	4.0	0.8	0.0
TCW-WQM5A	Sunny	NA	11:43	2nd	25.7	25.7	7.0	7.0	0.01	0.01	35	35	86.9	87.0	7.1	7.1	1.3	1.3	0.9	0.9
TOWNOMO	0	NIA	10.05	1st	25.5	05.0	6.8	0.0	0.40	0.40	822	040	66.4	05.0	5.4	5.4	1.4	4.5	0.8	0.0
TCW-WQM6	Sunny	NA	13:25	2nd	25.6	25.6	6.8	6.8	0.40	0.40	816	819	64.8	65.6	5.3	5.4	1.5	1.5	0.9	0.9
TO 101 101 00 47	Commis	NA	40.57	1st 2nd	29.5	29.6	6.9	6.0	0.64	0.04	1300	1290	68.7	60.0	5.2	5.0	1.3	4.4	1.0	4.4
TCW-WQM7	Sunny		13:57		29.7		6.9	6.9	0.64	0.64	1280		68.8	68.8	5.2	5.2	1.5	1.4	1.2	1.1

Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

NA: This monitoring location is not subject to tidal effect.

Water Quality Monitoring Results on 23 May 2022 during Ebb Tide

Monitoring Station	Weather	Tidal Condition	Sampling	Replicate	Water Te	mperature °C)	р	Н	Salinit	y (ppt)	Cond (µS	uctivity /cm)	DO Satur	ation (%)	Dissolved (mg	d Oxygen g/L)	Turbidit	y(NTU)		ded Solids g/L)
	Condition		Time		Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average
TCW-WQM1	Cloudy	Rough	08:53	1st	26.5	26.5	8.3	8.3	20.23	20.24	32400	32450	72.0	73.6	5.2	5.3	2.7	2.7	1.6	1.7
TCVV-VVQIVIT	Cloudy	Rough	06.53	2nd	26.5	8.3	0.3	20.25	20.24	32500	32450	75.2	73.0	5.4	5.5	2.6	2.1	1.8	1.7	
TCW-WQM2 Clo	Clavely	NIA	10:20	1st	24.3	24.2	7.1		0.01	0.04	32	- 32 -	84.1	04.2	7.1	7.4	1.2	1.3	0.8	0.0
	Cloudy	NA	10:39	2nd	24.2	24.2	7.1	7.1	0.01	0.01	32		84.5	84.3	7.1	7.1	1.3	1.3	0.8	0.8
	Cloudy	NA	44.00	1st	24.9	- 24.9	7.3	7.3	0.03	0.00	61	00	94.9	95.4	7.9	7.0	1.3	4.0	1.0	4.0
TCW-WQM3A			11:03	2nd	24.9		7.3		0.03	0.03	62	62	95.8	55.4	7.9	7.9	1.3	1.3	1.0	1.0
TOWN MONA	Cloudy	NA	44.40	1st	24.5	24.5	6.3	6.3	0.02	0.02	42	40	48.4	47.0	4.0	2.0	1.6	1.7	<0.5	<0.5
TCW-WQM4			11:40	2nd	24.5	24.5	6.3	6.3	0.02	0.02	42	42	45.6	47.0	3.8	3.9	1.8	1.7	<0.5	VO.3
TCW-WQM5A	Clavely	NA	12:03	1st	25.7	25.7	7.2	7.2	0.02	0.02	36	36	91.4	91.6	7.5	7.5	1.6	1.6	0.6	0.7
TCVV-VVQIVISA	Cloudy	I NA	12:03	2nd	25.7	25.7	7.2	7.2	0.02	0.02	36	30	91.7	91.6	7.5	7.5	1.6	1.0	0.8	0.7
TOWN MONE	Clavely	NIA	09:32	1st	23.9	23.9	7.0	7.0	0.02	0.02	47	47	80.2	81.3	6.8	0.0	1.5	4.4	0.9	0.0
TCW-WQM6	Cloudy	NA	09:32	2nd	23.9	23.9	7.0	7.0	0.02	0.02	47	47	82.4	81.3	6.9	6.9	1.3	1.4	0.9	0.9
TOW WOMZ	Clavely	NA	09:56	1st	26.1	26.1	9.7	0.7	0.03	0.03	72	- 72	112.9		9.1	0.4	1.6	4.7	1.0	1.0
TCW-WQM7	Cloudy			2nd	26.1		9.7	9.7	0.03		72		112.3	112.6	9.1	9.1	1.8	1.7	1.0	1.0

Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

NA: This monitoring location is not subject to tidal effect.

Water Quality Monitoring Results on 25 May 2022 during Ebb Tide

Monitoring Station	Weather	Tidal Condition	Sampling	Replicate	Water Te	mperature °C)	р	Н	Salinit	y (ppt)	Cond (µS	uctivity /cm)	DO Satur	ation (%)	Dissolved (mg	d Oxygen g/L)	Turbidi	ty(NTU)		led Solids g/L)				
	Condition		Time		Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average				
TCW-WQM1	Cloudy	Rough	10:19	1st	26.7	26.7	8.2	8.2	22.50	22.50	35700	35700	63.3	62.3	4.5	4.4	4.1	4.3	1.2	1.3				
TCVV-VVQIVIT	Cloudy	rtough	10.19	2nd	26.8	20.7	8.2	0.2	22.50	22.50	35700	33700	61.2	02.3	4.3	4.4	4.4	4.3	1.3	1.5				
TCW-WQM2 C	Cloudy	NIA	11:02	1st	24.7	24.7	6.9	- 6.8 -	0.03	0.03	72	73	52.1	51.5	4.3	4.3	2.5	2.4	0.7	0.8				
		NA	11.02	2nd	24.7		6.8		0.03		74	13	50.8	51.5	4.2	4.3	2.2	2.4	0.8	0.6				
TOW WOMON	Cloudy	NA	NIA	NIA	NA	NA 11.	11:35	1st	25.0	25.0	7.2	7.2	0.03	0.03	63	- 63	94.1	94.1	7.8	7.8	1.2	4.0	1.0	4.0
TCW-WQM3A			11:35	2nd	25.0	25.0	7.3	7.2	0.03	0.03	62	63	94.0	94.1	7.8	7.8	1.2	1.2	1.0	1.0				
TOWN MONA	Cloudy	NA	10.11	1st	24.8	24.0	6.3		0.02	0.00	44	44	58.0	50.0	4.8	4.0	1.4	4.4	<0.5	<0.5				
TCW-WQM4			12:11	2nd	24.7	24.8	6.3	6.3	0.02	0.02	43	44	58.3	58.2	4.8	4.8	1.3	1.4	<0.5	20.5				
TCW-WQM5A	Clavidy	NA	12:39	1st	25.3	25.3	7.3	7.3	0.02	0.02	36	36	95.6	95.6	7.9	7.9	1.3	1.3	0.6	0.7				
TCW-WQM5A	Cloudy	INA	12:39	2nd	25.3	25.3	7.3	1.3	0.02	0.02	36	- 30	95.6	95.6	7.9	7.9	1.3	1.3	0.7	0.7				
TOWN MONE	Clavidy	NIA	09:12	1st	24.1	24.1	6.8	6.8	0.02	0.02	45	45	83.7	02.0	7.0	7.1	1.4	4.5	0.8	0.9				
TCW-WQM6	Cloudy	NA	09:12	2nd	24.1	24.1	6.8	0.8	0.02	0.02	45	45	84.1	83.9	7.1	7.1	1.5	1.5	0.9	0.9				
TC\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\	Cloudy	NIA	00:42	1st 2nd	26.8	- 26.8	10.1	10.1	0.03	- 0.03	76	70	131.5	121 4	10.5	10.5	3.3	3.3	1.2	1.2				
TCW-WQM7	Cloudy	NA	09:42		26.8		10.1	10.1	0.03		76	- 76	131.3	131.4	10.5	10.5	3.2	3.3	1.1	1.2				

Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

NA: This monitoring location is not subject to tidal effect.

Water Quality Monitoring Results on 27 May 2022 during Ebb Tide

Monitoring Station	Weather	Tidal Condition	Sampling	Replicate	Water Te			Н	Salinit	y (ppt)	Condo (µS	uctivity /cm)	DO Satu	ration (%)	Dissolved (mg	d Oxygen g/L)	Turbidi	ty(NTU)		led Solids g/L)
	Condition	Tradi Condition	Time	Tropiloato	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average
TCW-WQM1	Claudia	Dough	44.00	1st	26.8	26.9	7.9	7.9	22.05	22.07	35100	35100	45.2	44.6	3.2	3.2	3.5	3.5	3.5	2.7
1 0 77 - 77 Q 1711	Cloudy	Rough	11:02	2nd	26.9	7.9	7.9	7.3	22.09	22.07	35100	35100	43.9	44.0	3.1	3.2	3.4	3.5	3.8	3.7
TCW-WQM2	Olevek	NA.	44.50	1st	25.0	04.0	7.1		0.01	0.01	35	35	82.0	00.0	6.8	0.0	1.3	1.4	1.2	4.0
TCVV-VVQIM2	Cloudy	NA	11:50	2nd	24.9	24.9	7.1	7.1	0.01		35	35	83.7	82.9	6.9	6.9	1.4		1.1	1.2
TOWNS	Rainy		40.40	1st	25.4		7.2	7.0	0.03	0.00	66	-00	90.3	20.0	7.4	7.4	1.6	4.7	2.0	1.0
TCW-WQM3A		NA	12:19	2nd	25.4	25.4	7.2	7.2	0.03	0.03	66	66	90.3	90.3	7.4	7.4	1.7	1.7	1.8	1.9
TOW WOM	Cloudy	NA	10.50	1st	25.5		6.3	0.0	0.02	0.00	46	40	46.0	47.4	3.8	0.0	1.7	4.0	0.6	0.7
TCW-WQM4			12:56	2nd	25.3	25.4	6.3	6.3	0.02	0.02	45	46	48.8	47.4	4.0	3.9	1.9	1.8	0.8	0.7
TOW WOMEN	Olevek	NA.	40.00	1st	25.4	05.4	7.0	7.0	0.02	0.00	36	00	93.6	00.5	7.7	7.7	2.2	0.4	1.4	4.4
TCW-WQM5A	Cloudy	NA	13:23	2nd	25.4	25.4	7.0	7.0	0.02	0.02	36	36	93.3	93.5	7.7	7.7	2.5	2.4	1.3	1.4
TOW WOME	Claudi	NIA	40.40	1st	24.9	24.9	6.8		0.02	0.00	49	40	80.9	79.7	6.7		1.5	4.5	1.7	4.0
TCW-WQM6	Cloudy	NA	10:12	2nd	24.9	24.9	6.9	6.9	0.02	0.02	49	49	78.4	79.7	6.5	6.6	1.4	1.5	1.8	1.8
TOW WOMA	Claudi	NIA.	40.25	1st	26.1	20.4	8.4	0.4	0.04	0.04	78	70	101.0	101.5	8.2	0.0	2.3	2.4	2.1	2.2
TCW-WQM7	Cloudy	NA	10:35	2nd	26.1	26.1	8.4	8.4	0.04		78	78	101.5	101.3	8.2	8.2	2.5	2.4	2.2	2.2

Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

NA: This monitoring location is not subject to tidal effect.

Water Quality Monitoring Results on 30 May 2022 during Ebb Tide

Monitoring Station	Weather	Tidal Condition	Sampling	Replicate	Water Te	mperature °C)	р	Н	Salinit	y (ppt)	Cond (µS	uctivity /cm)	DO Satur	ation (%)	Dissolved (mg	d Oxygen g/L)	Turbidit	y(NTU)		led Solids g/L)	
3	Condition		Time	.,	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	
TCW-WQM1	Cloudy	Dough	14:04	1st	30.2	30.2	8.5	8.5	17.24	17.25	28100	28100	132.0	135.4	9.0	9.3	9.2	9.2	2.5	2.6	
TCVV-VVQIVIT	Cloudy	Rough	14.04	2nd	30.2	8.5	0.0	17.26	17.25	28100	20100	138.7	135.4	9.5	9.5	9.2	9.2	2.6	2.0		
TCW-WQM2 Clo	0	NIA	40.05	1st	27.8	07.0	6.8	0.0	0.02		36	20	71.8	70.7	5.6	5.0	1.4		0.9	0.0	
	Cloudy	NA	12:25	2nd	27.8	27.8	6.8	6.8	0.02	0.02	36	- 36	69.6	70.7	5.5	5.6	1.3	1.4	0.7	0.8	
	Cloudy	NA		44.50	1st	28.2	00.0	7.4	7.4	0.03	0.00	61	00	96.9	00.0	7.6	7.0	1.3	4.0	0.9	
TCW-WQM3A			11:52	2nd	28.2	28.2	7.4	7.4	0.03	0.03	62	62	96.2	96.6	7.5	7.6	1.3	1.3	0.9	0.9	
TOWNSONA	Cloudy	NA	40.50	1st	25.9	25.9	6.3	0.0	0.02	0.00	44	44	60.7	00.5	4.9	4.0	1.8	4.7	<0.5	<0.5	
TCW-WQM4			10:53	2nd	25.9	25.9	6.3	6.3	0.02	0.02	44	44	60.3	60.5	4.9	4.9	1.6	1.7	<0.5	20.5	
TOWNSALA	Olevert	NIA	44.00	1st	27.9	07.0	7.4	7.4	0.02	0.00	38	00	87.8	07.5	6.9	0.0	1.5	4.0	0.9	0.0	
TCW-WQM5A	Cloudy	NA	11:23	2nd	28.0	27.9	7.4	7.4	0.02	0.02	38	- 38	87.2	87.5	6.8	6.9	1.6	1.6	0.6	0.8	
TOWNSON	Olevert	NIA	40.50	1st	27.2	07.0	6.7	0.7	0.02	0.00	47	47	80.6	70.0	6.4	0.0	1.5	4.0	0.8	0.0	
TCW-WQM6	Cloudy	NA	12:53	2nd	27.2	27.2	6.7	6.7	0.02	0.02	47	47	77.2	78.9	6.1	6.3	1.6	1.6	0.9	0.9	
TOW MON47	Claudi	NA	12.25	1st	33.6	9.9	0.0	0.04		84	0.4	112.3		8.0	0.0	1.9	4.0	1.8	4.7		
TCW-WQM7	Cloudy		13:25	2nd	33.6	33.6	9.9	9.9	0.04	0.04	84	- 84	111.9	112.1	8.0	8.0	1.7	1.8	1.6	1.7	

Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

NA: This monitoring location is not subject to tidal effect.

H5. Water Quality Monitoring Event and Action Plan

Table H5.1: Event and Action Plan for Construction Water Quality

Event				
	ET	IEC	ER	Contractor
Action Level Exceedance for one sampling day	1. Inform IEC, Contractor and ER; 2. Check monitoring data, all plant, equipment and Contractor's working methods; and 3. Discuss remedial measures with IEC and Contractor and ER.	Discuss with ET, ER and Contractor on the implemented mitigation measures; Review proposals on remedial measures submitted by Contractor and advise the ER accordingly; and Review and advise the ET and ER on the effectiveness of the implemented mitigation measures.	Discuss with IEC, ET and Contractor on the implemented mitigation measures; Make agreement on the remedial measures to be implemented; Supervise the implementation of agreed remedial measures.	1. Identify source(s) of impact; 2. Inform the ER and confirm notification of the non-compliance in writing; 3. Rectify unacceptable practice; 4. Check all plant and equipment; 5. Consider changes of working methods; 6. Discuss with ER, ET and IEC and purpose remedial measures to IEC and ER; and 7. Implement the agreed mitigation measures.
Action Level Exceedance for more than one consecutive sampling days	Repeat in-situ measurement on next day of exceedance to confirm findings; Inform IEC, contractor and ER; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss remedial measures with IEC, contractor and ER Ensure remedial measures are implemented.	1. Discuss with ET, Contractor and ER on the implemented mitigation measures; 2. Review the proposed remedial measures submitted by Contractor and advise the ER accordingly; and 3. Review and advise the ET and ER on the effectiveness of the implemented mitigation measures.	Discuss with ET, IEC and Contractor on the proposed mitigation measures; Make agreement on the remedial measures to be implemented; and Discuss with ET, IEC and Contractor on the effectiveness of the implemented remedial measures.	 Identify source(s) of impact; Inform the ER and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment and consider changes of working methods; Discuss with ET, IEC and ER and submit proposal of remedial measures to ER and IEC within 3 working days of notification; and Implement the agreed mitigation measures.


Event Action

	ET	IEC	ER	Contractor
Limit Level Exceedance for one sampling day	1. Repeat in-situ measurement on next day of exceedance to confirm findings; 2. Inform IEC, contractor and ER; 3. Rectify unacceptable practice; 4. Check monitoring data, all plant, equipment and Contractor's working methods; 5. Consider changes of working methods; 6. Discuss mitigation measures with IEC, ER and Contractor; and 7. Ensure the agreed remedial measures are implemented.	Discuss with ET, Contractor and ER on the implemented mitigation measures; Review the proposed remedial measures submitted by Contractor and advise the ER accordingly; and Review and advise the ET and ER on the effectiveness of the implemented mitigation measures.	Discuss with ET, IEC and Contractor on the implemented remedial measures; Request Contractor to critically review the working methods; Make agreement on the remedial measures to be implemented; and Discuss with ET, IEC and Contractor on the effectiveness of the implemented remedial measures.	 Identify source(s) of impact; Inform the ER and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment and consider changes of working methods; Discuss with ET, IEC and ER and submit proposal of additional mitigation measures to ER and IEC within 3 working days of notification; and Implement the agreed remedial measures.
Limit Level Exceedance for more than one consecutive sampling days	1. Inform IEC, Contractor and ER; 2. Check monitoring data, all plant, equipment and Contractor's working methods; 3. Discuss mitigation measures with IEC, ER and Contractor; and 4. Ensure mitigation measures are implemented; and 5. Increase the monitoring frequency to daily until no exceedance of Limit Level for two consecutive days.	1. Discuss with ET, Contractor and ER on the implemented mitigation measures; 2. Review the proposed remedial measures submitted by Contractor and advise the ER accordingly; and 3. Review and advise the ET and ER on the effectiveness of the implemented mitigation measures.	 Discuss with ET, IEC and Contractor on the implemented remedial measures; Request Contractor to critically review the working methods; Make agreement on the remedial measures to be implemented; Discuss with ET and IEC on the effectiveness of the implemented mitigation measures; and Consider and instruct, if necessary, the Contractor to slow down or to stop all or part of the relevant site construction activities until no exceedance of Limit level. 	 Identify source(s) of impact; Inform the ER and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment and consider changes of working methods; Discuss with ET, IEC and ER and submit proposal of additional mitigation measures to ER and IEC within 3 working days of notification; and Implement the agreed remedial measures. As directed by the ER, to slow down or stop all or part of the relevant site construction activities until no exceedance of Limit level.

I. Ecology

- **I1. Locations of Ecological Impact Monitoring Stations**
- 12. Ecologically-related Water Quality Monitoring Equipment Calibration Certificates
- 13. Representative Photos of Species Surveyed
- I4. Monthly Monitoring Data of Stream Fauna (Aquatic invertebrate) in the Reporting Period
- 15. Monthly Monitoring Data of Stream Fauna (Fish) in the Reporting Period
- I6. Event and Action Plan for Exceedance in Action and Limit Levels of Stream Fauna
- 17. Summary of Water Quality Data in the Reporting Period

I1. Location of Ecological Impact Monitoring Stations

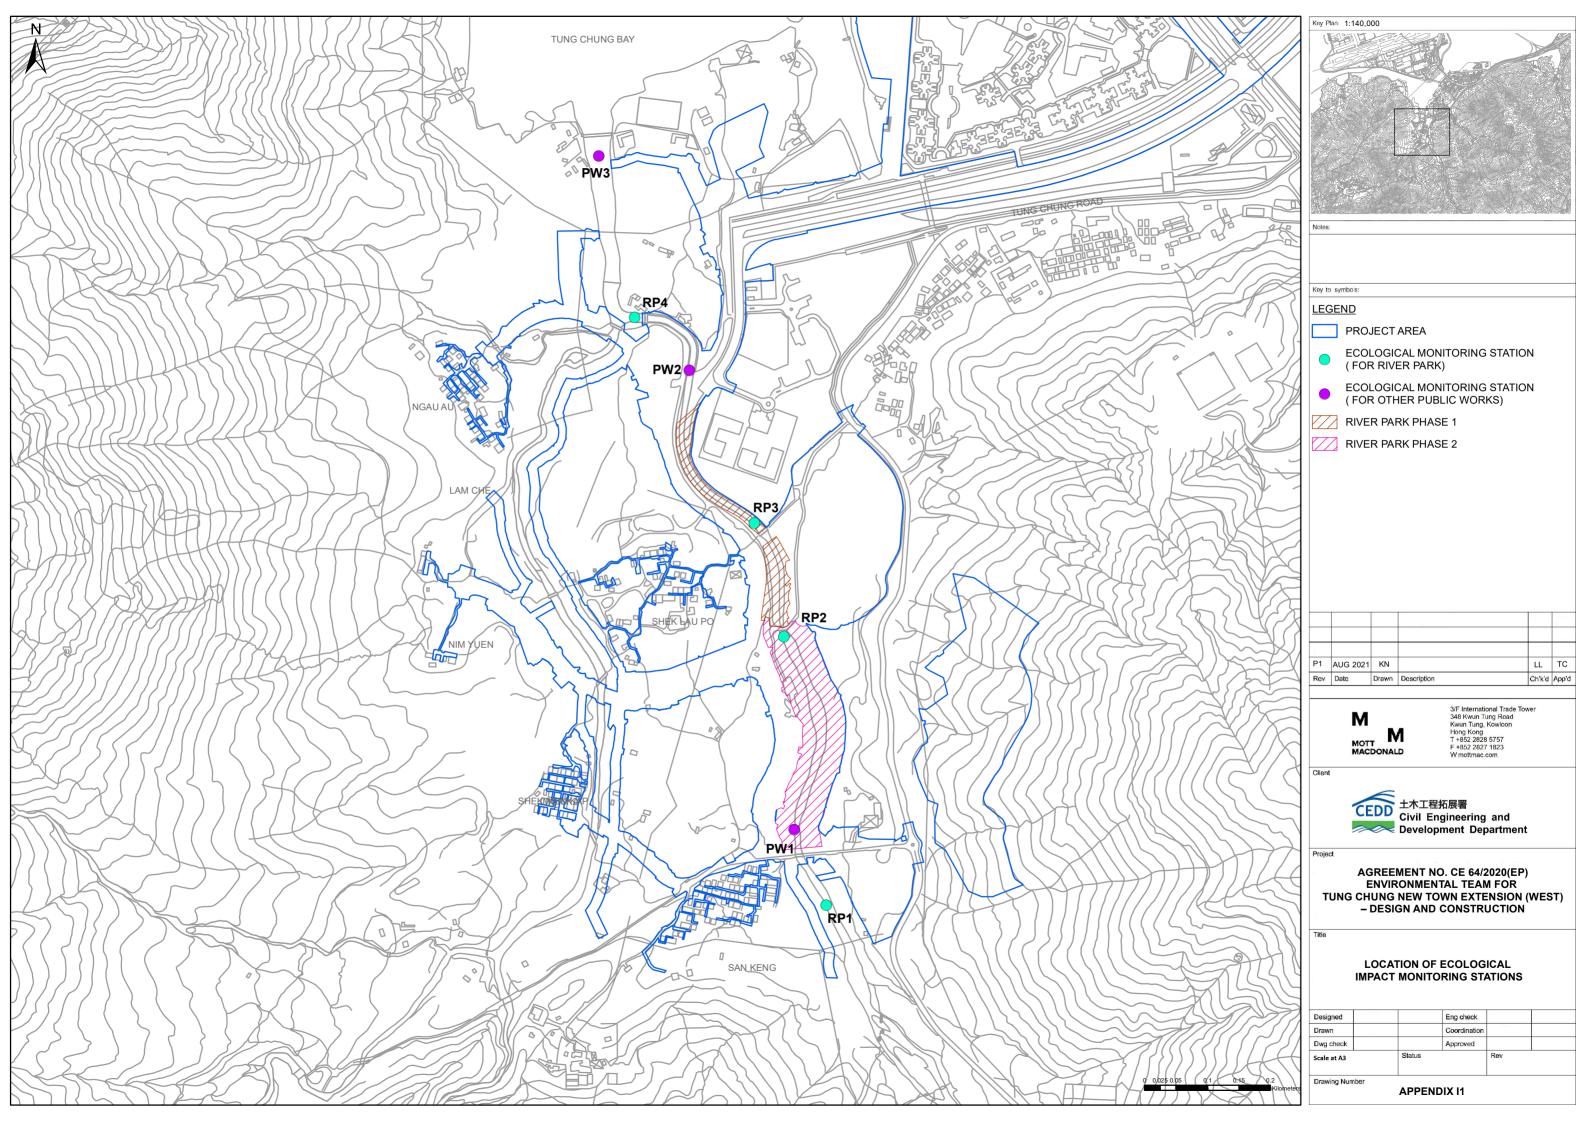

I2. Ecologically-related Water Quality Monitoring Equipment Calibration Certificates



ALS Technichem (HK) Pty Ltd

11/F, Chung Shun Knitting Centre 1-3 Wing Yip Street, Kwai Chung N.T., Hong Kong

T: +852 2610 1044 | F: +852 2610 2021

REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION

CONTACT: **THOMAS CHAN** HK2211534 WORK ORDER:

CLIENT: MOTT MACDONALD HONG KONG LIMITED

3/F, MANULIFE PLACE, **ADDRESS:** SUB-BATCH:

> 348 KWUN TONG ROAD, LABORATORY: HONG KONG KWUN TONG, KLN DATE RECEIVED: 31-Mar-2022

DATE OF ISSUE: 11-Apr-2022

SPECIFIC COMMENTS

Equipment information (Brand name, Model No., Serial No. and Equipment No.) is provided by client.

The performance of the equipment stated in this report is checked with independent reference material and results compared against a calibrated secondary source.

The "Tolerance Limit" quoted is the acceptance criteria applicable for similar equipment used by the laboratory or quoted from relevant international standards.

The "Next Calibration Date" is recommended according to best practice principle as practised by the laboratory or quoted from relevant international standards.

The validity of equipment/ meter performance only applies to the result(s) stated in the report.

Multifunctional Meter Equipment Type: Service Nature: Performance Check

Scope: Conductivity, Dissolved Oxygen, pH Value, Turbidity, Salinity and Temperature

Brand Name/ Model No.: [HORIBA]/ [U-53]

Serial No./ Equipment No.: [X42XKBNO/4BHN08KG]/ [N/A]

Date of Calibration: 11-April-2022

GENERAL COMMENTS

This report superseded any previous report(s) with same work order number.

Mr Chan Siu Ming, Vico Manager - Inorganics

Ra Sti

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd.

REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION

HK2211534 WORK ORDER:

SUB-BATCH:

DATE OF ISSUE: 11-Apr-2022

CLIENT: MOTT MACDONALD HONG KONG LIMITED

Equipment Type: Multifunctional Meter

Brand Name/ Model No.:

[HORIBA]/[U-53]

Serial No./

Date of Calibration:

[X42XKBNO/4BHN08KG]/[N/A]

Equipment No.:

11-April-2022

PARAMETERS:

Conductivity Method Ref: APHA (21st edition), 2510B

Expected Reading (µS/cm)	Displayed Reading (μS/cm)	Tolerance (%)
146.9	142	-3.3
6667	6370	-4.5
12890	12200	-5.4
58670	54200	-7.6
	Tolerance Limit (%)	±10.0

Date of Next Calibration:

Dissolved Oxygen Method Ref: APHA (21st edition), 45000: G

Expected Reading (mg/L)	Displayed Reading (mg/L)	Tolerance (mg/L)
3.84	3.68	-0.16
6.28	6.17	-0.11
8.49	8.50	+0.01
	Tolerance Limit (mg/L)	±0.20

pH Value Method Ref: APHA (21st edition), 4500H: B

Expected Reading (pH unit)	Displayed Reading (pH unit)	Tolerance (pH unit)
4.0	4.00	+0.00
7.0	7.00	+0.00
10.0	9.98	-0.02
	Tolerance Limit (pH unit)	±0.20

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.

> Mr Chan Siu Ming, Vico Manager - Inorganics

Ma Si

11-July-2022

REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION

WORK ORDER: HK2211534

SUB-BATCH: 0

DATE OF ISSUE: 11-Apr-2022

CLIENT: MOTT MACDONALD HONG KONG LIMITED

Equipment Type: Multifunctional Meter

Brand Name/ Model No.:

[HORIBA]/[U-53]

Serial No./ Equipment No.:

[X42XKBNO/4BHN08KG]/ [N/A]

Date of Calibration:

11-April-2022

Date of Next Calibration:

11-July-2022

PARAMETERS:

Turbidity Method Ref: APHA (21st edition), 2130B

Expected Reading (NTU)	Displayed Reading (NTU)	Tolerance (%)
0	0.00	
4	4.18	+4.5
40	42.0	+5.0
80	78.2	-2.3
400	440	+10.0
800	856	+7.0
	Tolerance Limit (%)	±10.0

Salinity Method Ref: APHA (21st edition), 2520B

Expected Reading (ppt)	Displayed Reading (ppt) Tolerance (%)	
0	0.00	
10	9.45	-5.5
20	18.57	-7.2
30	28.65	-4.5
	Tolerance Limit (%)	±10.0

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.

Mr Chan Siu Ming, Vico Manager - Inorganics

Ma Ship

REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION

WORK ORDER: HK2211534

SUB-BATCH: 0

DATE OF ISSUE: 11-Apr-2022

CLIENT: MOTT MACDONALD HONG KONG LIMITED

Equipment Type: Multifunctional Meter

Brand Name/ Model No.:

[HORIBA]/ [U-53]

Serial No./ Equipment No.:

[X42XKBNO/4BHN08KG]/ [N/A]

Date of Calibration: 11-April-2022 Date of Next Calibration: 11-July-2022

PARAMETERS:

Temperature Method Ref: Section 6 of International Accreditation New Zealand Technical

Guide No. 3 Second edition March 2008: Working Thermometer Calibration Procedure.

Expected Reading (°C)	Displayed Reading (°C)	Tolerance (°C)
8.5	9.05	+0.6
20.5	21.00	+0.5
36.5	37.34	+0.8
	Tolerance Limit (°C)	±2.0

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless

of equipment precision or significant figures.

Mr Chan Siu Ming, Vico Manager - Inorganics

Ma Ship

I 3.	Representative Photos of Species Surveyed



Acrossocheilus beijiangensis*



Barbodes semifasciolatus



Parazacco spilurus*



Favonigobius gymnauchen



Rhyacophilidae



Hydropsychidae



Ophiogomphus sinicus



Euphaea decorata

I4. Monthly Monitoring Data of Stream Fauna (Aquatic invertebrate) in the Reporting Period

Relative abundance: +: Uncommon, ++: Common, +++: Abundant

Date	Sampling Point	Method	Scientific Name	Common Name	Chinese Name	Abundance	Relative Abundance
May/22	PW3	Kick	Amphipoda	Scud	端足類	50+	
May/22	PW3	Observe	Ptilomera tigrina	Water Strider	虎紋毛足澗黽蝽		+
May/22	PW3	Observe	Rhagovelia sp.	Smaller Water Strider	水黽		++
May/22	RP4	Observe	Macrobrachium sp.	Freshwater Prawn	沼蝦屬		+
May/22	RP4	Observe	Tarebia granifera	Freshwater Snail	斜粒粒蜷		++
May/22	RP4	Kick	Tarebia granifera	Freshwater Snail	斜粒粒蜷	5	
May/22	RP4	Observe	Ptilomera tigrina	Water Strider	虎紋毛足澗黽蝽		+
May/22	RP4	Kick	Eriocheir hepuensis	Hepu Mitten Crab	合浦絨螯蟹	1	
May/22	PW2	Kick	Caridina cantonensis	Freshwater Shrimp	廣東米蝦	3	
May/22	PW2	Kick	Rhagovelia sp.	Smaller Water Strider	水黽	1	
May/22	PW2	Kick	Baetidae	Small Minnow Mayfly	四節蜉科	18	
May/22	PW1	Kick	Hydropsychidae	Caddisfly (Larva)	石蛾 (稚蟲)	1	
May/22	PW1	Kick	Lepidostomatidae	Caddisfly (Larva)	石蛾 (稚蟲)	1	
May/22	PW1	Kick	Physella acuta	European Physa	尖膀胱螺	1	
May/22	PW1	Kick	Ophiogomphus sinicus	Chinese Hooktail (Larva)	中華長鈎春蜓 (稚蟲)	1	
May/22	PW1	Kick	Euphaea decorata	Black-banded Gossamerwing (Larva)	方帶溪蟌 (稚蟲)	2	
May/22	PW1	Kick	Baetidae	Small Minnow Mayfly	四節蜉科	8	
May/22	RP2	Kick	Baetidae	Small Minnow Mayfly	四節蜉科	6	
May/22	RP2	Kick	Hydropsychidae	Caddisfly (Larva)	石蛾 (稚蟲)	1	
May/22	RP2	Kick	Rhyacophilidae	Caddisfly (Larva)	流石蛾	1	
May/22	RP1	Observe	Ptilomera tigrina	Water Strider	虎紋毛足澗黽蝽		+
May/22	RP1	Observe	Rhagovelia sp.	Smaller Water Strider	水黽		+
May/22	RP1	Kick	Rhagovelia sp.	Smaller Water Strider	水黽	1	
May/22	RP1	Kick	Baetidae	Small Minnow Mayfly	四節蜉科	7	
May/22	RP1	Kick	Euphaea decorata	Black-banded Gossamerwing (Larva)	方帶溪蟌 (稚蟲)	1	
May/22	RP1	Kick	Hydropsychidae	Caddisfly (Larva)	石蛾 (稚蟲)	1	
May/22	RP3	Kick	Caridina cantonensis	Freshwater Shrimp	廣東米蝦	6	
May/22	RP3	Kick	Baetidae	Small Minnow Mayfly	四節蜉科	50+	

I5. Monthly Monitoring Data of Stream Fauna (Fish) in the Reporting Period

Relative abundance: +: Uncommon, ++: Common, +++: Abundant

Date	Sampling Point	Method	Scientific Name	Common Name	Chinese Name	Abundance	Relative Abundance
May/22	PW3	Kick	Favonigobius gymnauchen	Sharp-nosed Sand Goby	裸項蜂巢鰕虎魚	1	
May/22	PW3	Kick	Terapon jarbua	Jarbua Terapon	細鱗鯻	1	
May/22	PW3	Observe	Gerres oyena	Common Silverbiddy	奧奈銀鱸		+
May/22	PW3	Observe	Glossogobius giuris	Fork Tongue Goby	舌鰕虎魚		++
May/22	PW3	Observe	Mugilidae	Mullet	鯔科		+++
May/22	PW3	Observe	Tilaipia sp.	Tilapia	鯽魚		+
May/22	RP4	Observe	Barbodes semifasciolatus	Chinese Barb	五線無鬚舥		+
May/22	RP4	Observe	Mugilidae	Mullet	鯔科		+++
May/22	RP4	Observe	Oryzias curvinotus*	Rice Fish	弓背青鱂		++
May/22	RP4	Observe	Parazacco spilurus*	Predaceous Chub	異鱲		+
May/22	RP4	Observe	Xiphophorus hellerii	Swordtail	劍尾魚		+
May/22	PW2	Kick	Xiphophorus hellerii	Swordtail	劍尾魚	1	
May/22	PW1	Observe	Acrossocheilus beijiangensis*	Beijiang Thick-lipped Barb	北江光唇魚		+
May/22	PW1	Cage	Acrossocheilus beijiangensis*	Beijiang Thick-lipped Barb	北江光唇魚	1	
May/22	PW1	Observe	Liniparhomaloptera disparis	Broken-band Hillstream Loach	擬平鰍		++
May/22	PW1	Kick	Liniparhomaloptera disparis	Broken-band Hillstream Loach	擬平鰍	3	
May/22	PW1	Observe	Parazacco spilurus*	Predaceous Chub	異鱲		+++
May/22	PW1	Cage	Parazacco spilurus*	Predaceous Chub	異鱲	2	
May/22	PW1	Observe	Xiphophorus hellerii	Swordtail	劍尾魚		+++
May/22	PW1	Cage	Xiphophorus hellerii	Swordtail	劍尾魚	10	
May/22	PW1	Observe	Xiphophorus variatus	Variable Platyfish	雜色劍尾魚		++
May/22	PW1	Observe	Poecilia maculatis	Southern Platyfish	花斑劍尾魚		+++
May/22	PW1	Cage	Poecilia maculatis	Southern Platyfish	花斑劍尾魚	1	
May/22	RP2	Observe	Acrossocheilus beijiangensis*	Beijiang Thick-lipped Barb	北江光唇魚		+++
May/22	RP2	Cage	Acrossocheilus beijiangensis*	Beijiang Thick-lipped Barb	北江光唇魚	3	
May/22	RP2	Observe	Barbodes semifasciolatus	Chinese Barb	五線無鬚舥		++
May/22	RP2	Cage	Barbodes semifasciolatus	Chinese Barb	五線無鬚舥	3	
May/22	RP2	Observe	Liniparhomaloptera disparis	Broken-band Hillstream Loach	擬平鰍		++
May/22	RP2	Observe	Parazacco spilurus*	Predaceous Chub	異鱲		++
May/22	RP2	Cage	Parazacco spilurus*	Predaceous Chub	異鱲	2	
May/22	RP2	Kick	Rhinogobius duospilus	-	溪吻鰕虎魚	1	
May/22	RP2	Observe	Xiphophorus hellerii	Swordtail	劍尾魚		+++
May/22	RP2	Cage	Xiphophorus hellerii	Swordtail	劍尾魚	3	
May/22	RP1	Kick	Liniparhomaloptera disparis	Broken-band Hillstream Loach	擬平鰍	2	
May/22	RP1	Observe	Parazacco spilurus*	Predaceous Chub	異鱲		++
May/22	RP1	Cage	Parazacco spilurus*	Predaceous Chub	異鱲	2	
May/22	RP1	Kick	Pseudogastromyzon myersi	Sucker-belly Loach	麥氏擬腹吸鰍	1	
May/22	RP1	Observe	Rhinogobius duospilus	-	溪吻鰕虎魚		++
May/22	RP3	Kick	Xiphophorus hellerii	Swordtail	劍尾魚	1	

^{*}Acrossocheilus beijiangensis and Oryzias curvinotus are considered as species of conservation importance (Fellowes, 2002); Parazacco spilurus is considered as species of conservation importance (Zheng & Wang, 1998)

I6. Event and Action Plan for Exceedance in Action and Limit Levels of Stream Fauna

Event	Action				
	ET	IEC	ER	Contractor	
Action Level Exceedance	 Check monitoring data and confirm findings; Investigate the cause of the reduction if it is related to construction works; Immediately inform IEC, Contractor and ER; Discuss mitigation measures with IEC, Contractor and ER; Ensure mitigation measures are implemented. 	 Check monitoring data, analysis and investigation by ET; Review the proposed mitigation measures submitted by Contractor and advise the ER accordingly; Review and advise the ET and ER on the effectiveness of the mitigation measures after implementation. 	 Check the monitoring results and findings from ET and IEC; Discuss with ET, IEC and Contractor on the proposed mitigation measures; Supervise the implementation of the mitigation measures; Discuss with ET, IEC and Contractor on the effectiveness of the implemented mitigation measures. 	 Identify source(s) of impact; Inform the ER and confirm notification of the non-compliance in writing; Discuss with ET, IEC and ER and submit proposal of mitigation measures to ER and IEC; Implement the agreed mitigation measures. Instigate remedial action to remove or reduce source of disturbance if the cause is identified as project related. 	
Limit Level Exceedance	 Check monitoring data and confirm findings; Investigate the cause of the reduction if it is related to construction works; Immediately inform IEC, Contractor and ER; Discuss additional mitigation measures with IEC, Contractor and ER; Ensure additional mitigation measures are implemented. 	 Check monitoring data, analysis and investigation by ET; Discuss with ET, Contractor and ER on the additional mitigation measures implemented; Review the proposed additional mitigation measures submitted by Contractor and advise the ER accordingly; Review and advise the ET and ER on the effectiveness of the additional mitigation measures implemented 	 Check the monitoring results and findings from ET and IEC; Discuss with ET, IEC and Contractor on the additional mitigation measures proposed; Supervise the implementation of the additional mitigation measures; Discuss with ET, IEC and Contractor on the effectiveness of the additional mitigation measures implemented. 	 Identify source(s) of impact; Inform the ER and confirm notification of the non-compliance in writing; Discuss with ET, IEC and ER and submit proposal of additional mitigation measures to ER and IEC; Implement the agreed additional mitigation measures. Instigate additional remedial action to remove or reduce source of disturbance if the cause is identified as project related. 	

I7. Summary of Water Quality Data in the Reporting Period

Tung Chung New Town Extension (West) Ecologically-related Water Quality Monitoring Results

Reporting Month:	May-2022														
Monitoring Station		RP1		RP2		RP3		RP4		PW1		PW2		PW3	
Replicate	Unit	1	2	1	2	1	2	1	2	1	2	1	2	1	2
Sampling Time	-	09:00	09:00	10:45	10:45	11:20	11:20	14:35	14:35	09:45	09:45	12:05	12:05	15:45	15:45
Weather	-	Sunny													
Sampling Depth	m	0.2	0.2	0.2	0.2	0.1	0.1	0.3	0.3	0.2	0.2	0.1	0.1	0.3	0.3
Parameter															
рН		7.2	7.2	6.9	6.9	7.1	7.1	7.7	7.6	7	6.9	8.2	8.2	7.1	7.1
Salinity	ppt	0.02	0.02	0.03	0.03	0.03	0.03	0.03	0.03	0.02	0.02	0.04	0.04	13.56	13.84
Temperature	°C	20.8	20.8	21.9	21.9	22.3	22.3	24.2	24.3	21.3	21.3	24.6	24.6	24.8	24.7
Turbidity	NTU	1.7	1.7	1.6	1.5	1.4	1.3	7.6	7.8	2.0	2.0	1.0	0.9	5.3	5.4
DO	mg/L	9.8	9.4	7.8	7.6	8.4	8.3	8.4	8.3	8.8	8.9	8.2	7.6	5.8	5.6
DO Saturation	%	109.5	105.3	89.3	86.7	96.5	95.1	100.4	99.3	98.8	99.7	98.2	91.1	75.3	73.2
Suspended Solids	mg/L	1.3	1.4	0.8	0.9	1.0	1.0	3.7	3.5	1.6	1.9	1.1	1.1	1.9	1.7
Ammonia as N	mg/L	0.03	0.03	0.03	0.03	0.04	0.02	0.04	0.03	0.08	0.08	0.04	0.05	0.03	0.03
Total Kjeldahl Nitrogen as N	mg/L	0.06	<0.05	0.10	0.09	0.09	0.08	0.12	0.10	0.15	0.14	0.12	0.14	0.11	0.10
Total Phosphorus as P	mg/L	<0.01	<0.01	0.02	0.02	0.02	0.02	0.02	0.02	0.03	0.03	0.03	0.03	0.02	0.02
Escherichia coli	CFU/100mL	58	81	160	130	99	97	120	130	150	180	140	110	72	61
Biochemical Oxygen Demand	mg/L	1.6	1.2	1.5	1.5	1.4	1.6	1.3	1.2	1.6	1.5	1.3	1.3	1.4	1.4
Chemical Oxygen Demand	mg/L	<2	2	2	<2	2	<2	<2	<2	4	6	3	4	5	6
Oil & Grease	mg/L	<2	<2	<2	<2	<2	<2	<2	<2	<2	<2	<2	<2	<2	<2

J. Cumulative Statistics on Exceedances, Environmental Complaints, Notifications of Summons and Status of Prosecutions

Table J.1: Cumulative Statistics on Exceedances

Parameter	Exceedance Level	Total No. Recorded in this Reporting Period ¹	Total No. Recorded since Project Commencement
Air Quality (1-hour TSP)	Action	0	0
	Limit	0	0
Noise	Action	0	1
	Limit	0	0
Water Quality	Action	0	0
	Limit	0	0
Ecology	Action	0	0
	Limit	0	0

Remark: (1) Exceedances, which are not project related, are not shown in this table.

Table J.2: Cumulative Statistics on Complaints, Notifications of Summons and Successful Prosecutions

Contract No.	Reporting Period	Cumulative Statistics					
		Complaints	Notifications of Summons	Prosecutions			
Contract 5 This Reporting Period (1 – 31 May 2022)		0	0	0			
	Total No. Received since Project Commencement	2	0	0			
Contract 6	This Reporting Period (1 – 31 May 2022)	0	0	0			
	Total No. Received since Project Commencement	2	0	0			

K. Monitoring Schedule for the Next Reporting Period

June 2022 - Impact Monitoring Schedule for Tung Chung West

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
,			1	2	3	4
			WQM (14:00)	DM-5, DM-6		WQM (16:00)
5	6	7	8	9	10	11
	WQM (17:00)	CA5, CA6, CA7, CA8, CA9	WQM (08:00) DM-5, DM-6		WQM (10:00)	
12	13	14	15	16	17	18
	WQM (12:00) Ecological Monitoring	DM-5, DM-6 CA5, CA6, CA7, CA8, CA9	WQM (13:30)		WQM (15:30)	
19	20	21	22	23	24	25
	WQM (17:00) DM-5, DM-6		WQM (08:30)	CA5, CA6, CA7, CA8, CA9	WQM (10:30) DM-5, DM-6	
26	27	28	29	30		
	WQM (12:00)		WQM (13:30)	DM-5, DM-6 CA5, CA6, CA7, CA8, CA9		
		Notes:				
		Air Quality Monitoring Station:	DM-6: Mok Ka CA5: Village House in	n Ma Wan Chung (G/F)		
		Noise Monitoring Station:	CA7: YMCA of Hong CA8: Caritas Charles	n Shek Mun Kap (G/F) Kong Christian College (Roof Flovath College (Roof Floor)		
		[2] Tidal information refers	ng g is arranged at ebb tide of th	ovided by Hong Kong Observatory		

